

SUBMITTAL COVERSHEET **Nanuet UFSD –Phase 3 Projects**

Architect:
KSQ Architects
215 W 40th Street, 15th Floor
New York, NY 10018

Owner:
Nanuet Union Free School District
101 Church Street
Nanuet, NY 10954

Construction Manager:
Jacobs
One Penn Plaza, 54th floor
New York, NY 10019

Contractor: Joe Lombardo Plumbing & Heating of Rockland Inc

Contract: Ron Lombardo

Address: 321 Spook Rock Road Suite 109A

Telephone: 845-357-6537

Suffern, New York 10901

Fax: 845-357-8529

School Name: Nanuet Union Free School District Phase 3 Bond Projects @ Barr Middle School & Nanuet High School

Type of Submittal:

Re-submittal: ☐ No ☐ Yes

☐ Shop Drawings
☐ Test Report

☐ Product Data
☐ Certificate

☐ Schedule
☐ Color Sample

☐ Sample
☐ Warranty

☐ _____
☐ _____

Submittal Description:

Product Name: LOMBARDO'S PROJECT MILESTONE SCHEDULE

Manufacturer: LOMBARDO updated #2 RESPONDED TO CHANGES

Subcontractor/Supplier: PEARLS CONSTRUCTION REQUESTED BY CM

References:

Spec. Section No.: 011100

Drawing No(s): _____

Paragraph: _____

Rm. or Detail No(s): _____

Architect's/ Engineer's Review Stamp	Contractor Review Statement: These documents have been checked for accuracy and coordinated with job conditions and Contract requirements by this office and have been found to comply with the provisions of the Contract Documents. Ronald J. Lombardo 1.15.24 Name: Date: Company Name: Joe Lombardo Plumbing & Heating of Rockland Inc.

Remarks:

Responses to comments received from the owner:

In response to comments received from the Owner regarding Update #2, the following responses and/or changes have been made:

- **1- The last day of school is June 26th. This has to start after that. Is this for the first and second floor? there is no abatement scope for Lombardo in the lower level.**

the abatement has been pushed to start on Mid July, 2024, the lower level abatement activity has been deleted.

C4970	Install Mechanical Ducts & Pipes Hangers - Lower Level - Barr MS	
C5000	Install Above ceiling Terminal Equipment - Lower Level - Barr MS	when will controls wiring take place?
C4980	Install HVAC Ducts & Pipes - Lower Level - Barr MS	
C4990	Insulate HVAC Ducts & Pipes - Lower Level - Barr MS	these are all scheduled to be completed at the same time? lower level and second floor
C5010	Mechanical Rough-Ins Inspection - Lower Level - Barr MS	
C5020	Mechanical Rough-Ins Punchlist - Lower Level - Barr MS	
C5030	Install Grilles & Diffusers - Lower Level - Barr MS	
C7170	Install Mechanical Equipment - Lower Level - Barr MS	

- **2- when will controls wiring take place?.**

Siemens is planning to start the mechanical controls work on July 4th, 2024 to September 2024. An additional activity for the controls work has been added to the schedule.

- **3- These are all scheduled to be completed at the same time? lower level and second floor**

There is no Mechanical work in the Lower Roof. All the activities for the mechanical work in the lower roof have been deleted.

First Floor		
Architectural		
C4140	Patch Walls - First Floor - Barr MS	what walls are to be patched during March? what work is this for
C4070	Patch Ceilings - First Floor - Barr MS	
C3720	Patch Flooring - First Floor - Barr MS	where is the casework install?

- **4- where is the casework install?**

Activities for casework installation for 1st and 2nd floor have been added to the schedule.


Mechanical		45	15-Jan-2024	19-Mar-2024
C3730	Install Mechanical Ducts & Pipes Hangers - First Floor - Barr MS	1	15-Jan-2024	16-Jan-2024
C3750	Install HWC Ducts & Pipes - First Floor - Barr MS	12	17-Jan-2024	01-Feb-2024
C3760	Install Above ceiling Terminal Equipment - First Floor - Barr MS	4	17-Jan-2024	22-Jan-2024
C3800	Insulate HWC Ducts & Pipes - First Floor - Barr MS	1	02-Feb-2024	02-Feb-2024
C3870	Mechanical Rough-ins Inspection - First Floor - Barr MS	2	05-Feb-2024	06-Feb-2024
C3880	Mechanical Rough-ins Punchlist - First Floor - Barr MS	2	07-Feb-2024	08-Feb-2024
C4090	Install Grilles & Diffusers - First Floor - Barr MS	4	09-Feb-2024	14-Feb-2024
C7160	Install Mechanical Equipment - First Floor - Barr MS	10	06-Mar-2024	19-Mar-2024
Second Floor		44	05-Jan-2024 A	16-Sep-2024

- 5- not completed, provide date for when it will be finished

The mechanical work at 1st floor – Barr MS will take place in July,2024

- 6- is this unit ventilator installed? UVs are not marked.








The activity for the mechanical equipment has been deleted, and the above ceiling terminal equipment activity name is containing the installation of the unit ventilator with its number.

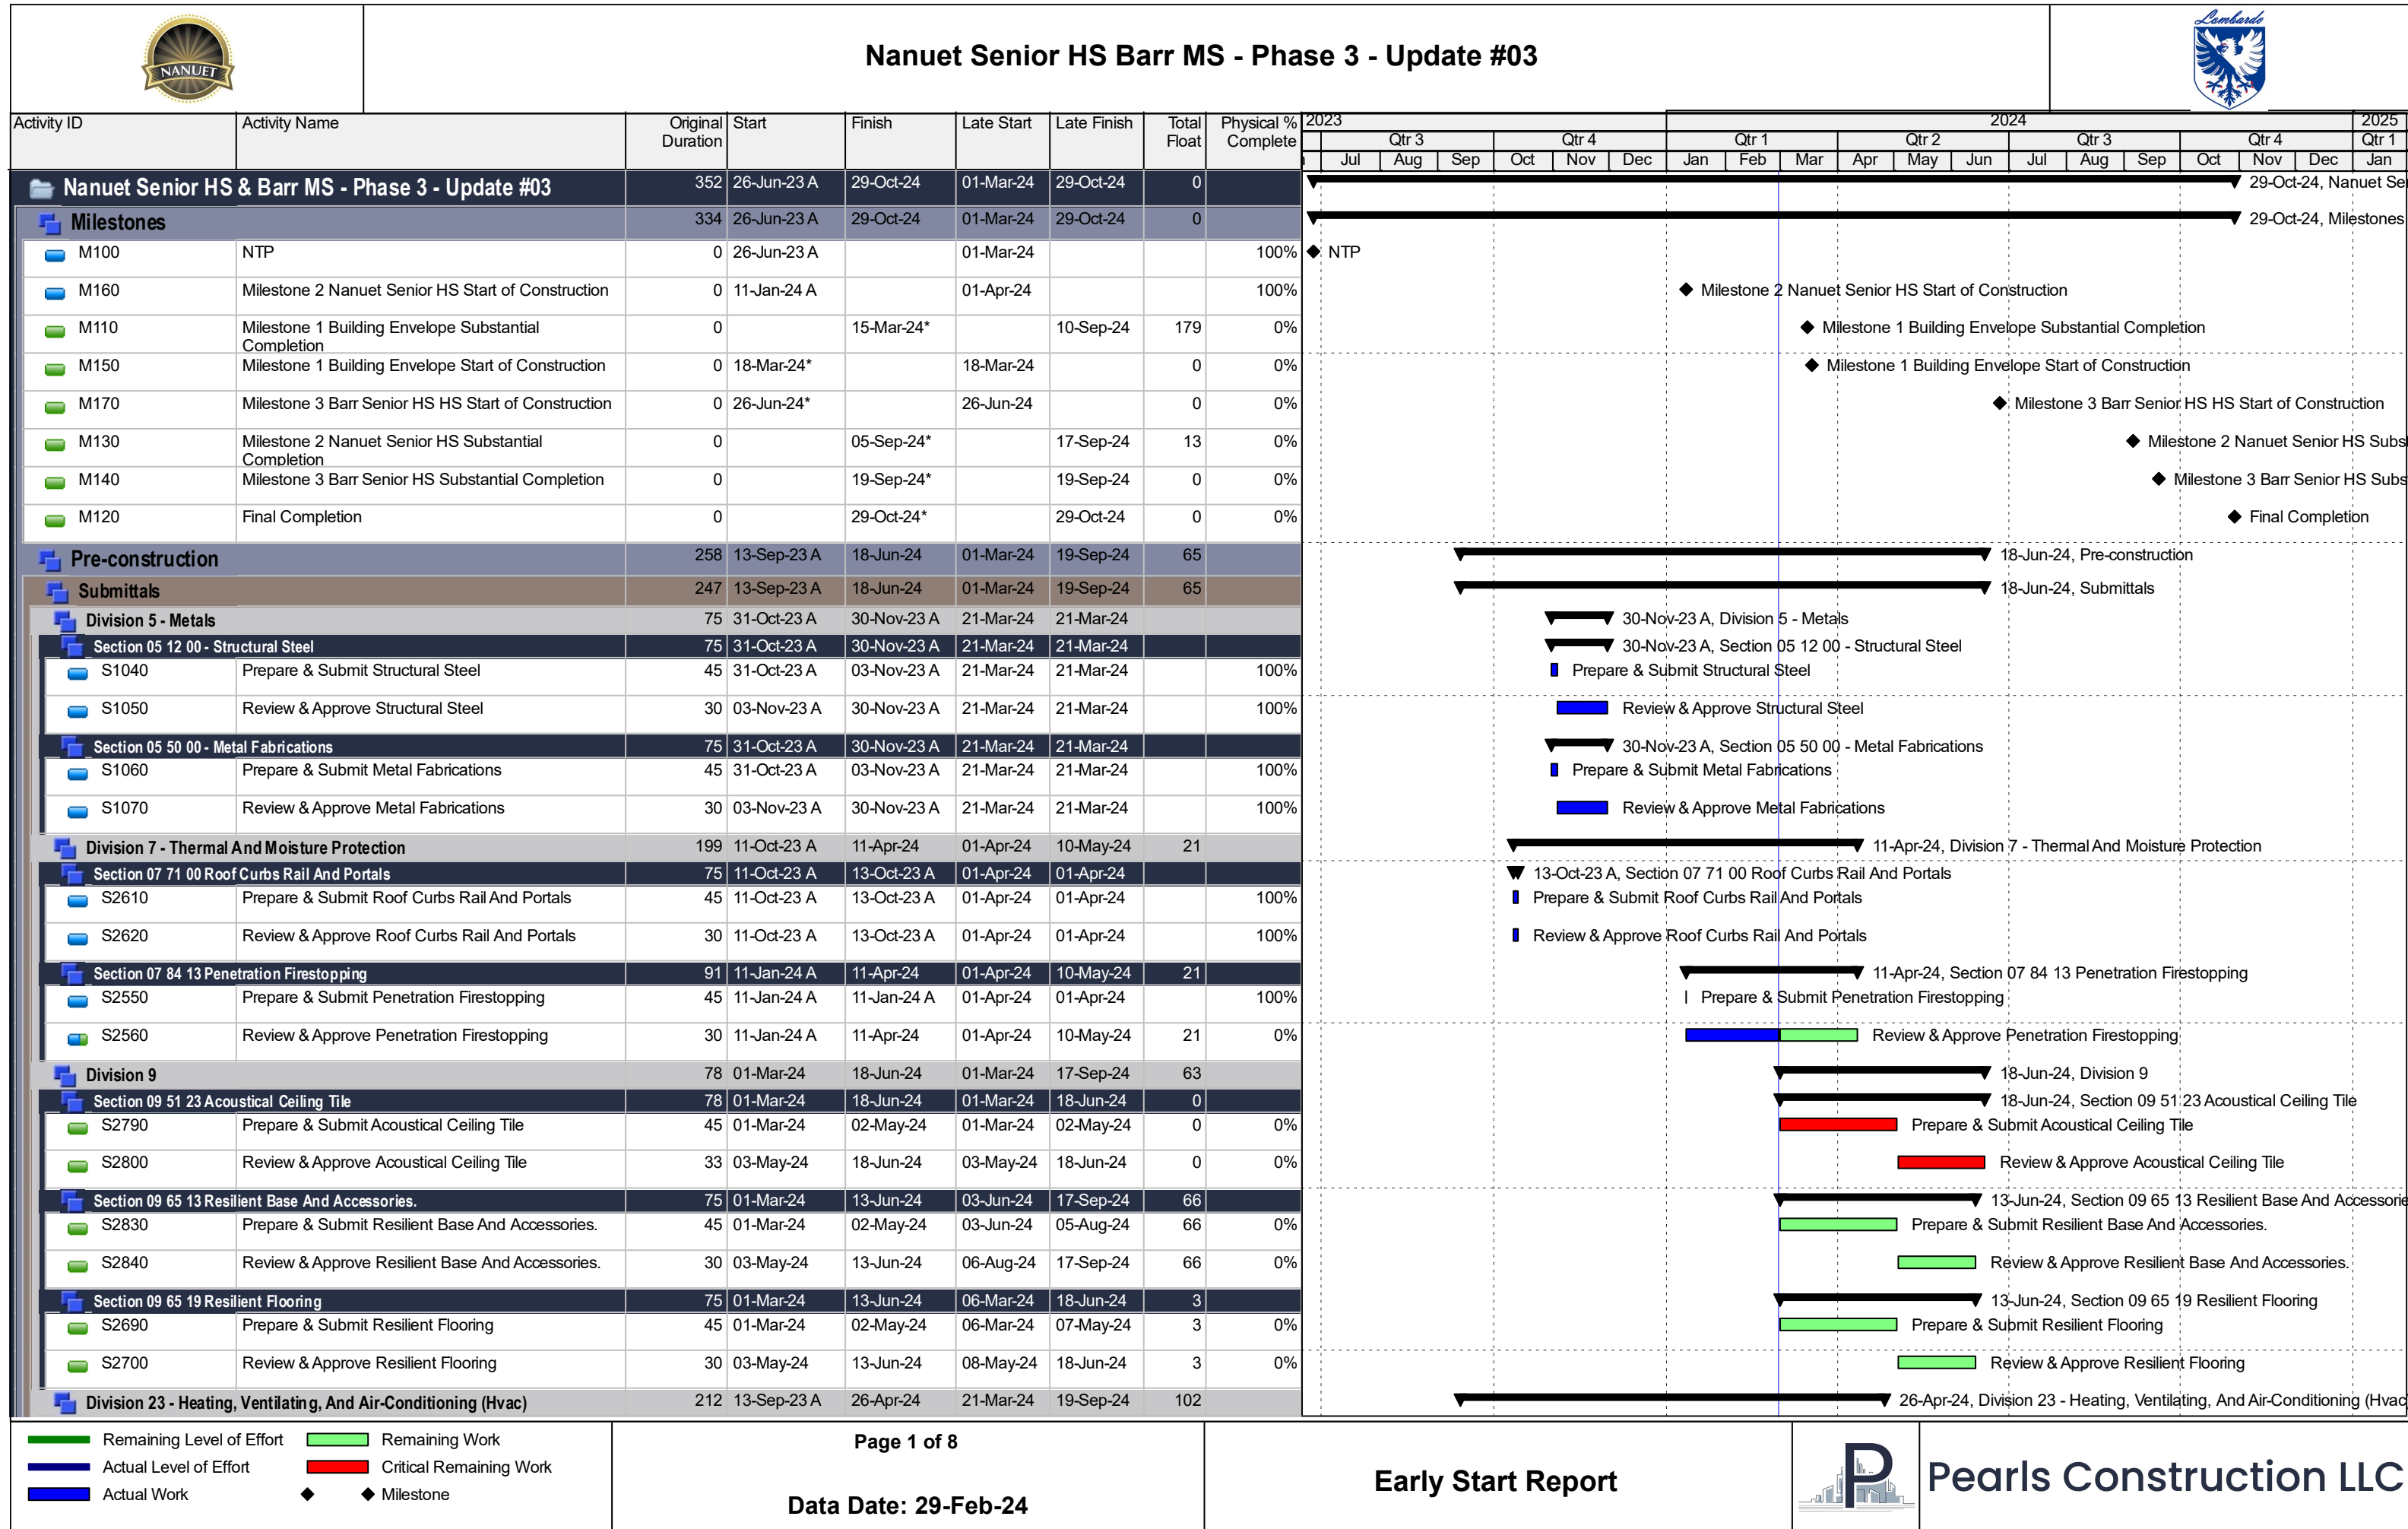



Nanuet Senior HS Barr MS - Phase 3 - Update #03



Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	2023												2024												2025
									Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1						
									Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan						
	 Section 23 05 16 Expansion Fittings And Loops For Hvac Piping	75	14-Sep-23 A	21-Sep-23 A	05-Apr-24	05-Apr-24			 21-Sep-23 A, Section 23 05 16 Expansion Fittings And Loops For Hvac Piping																								
	 S2010 Prepare & Submit Expansion Fittings And Loops For Hvac Piping	45	14-Sep-23 A	21-Sep-23 A	05-Apr-24	05-Apr-24		100%	 Prepare & Submit Expanision FittingsAnd Loops For Hvac Piping																								
	 S2020 Review & Approve Expansion Fittings And Loops For Hvac Piping	30	14-Sep-23 A	21-Sep-23 A	05-Apr-24	05-Apr-24		100%	 Review & Approve Expansion Fittings And Loops For Hvac Piping																								
	 Section 23 05 19 Meters And Gauges For Hvac Piping	75	09-Oct-23 A	28-Nov-23 A	03-Jun-24	03-Jun-24			 28-Nov-23 A, Section 23 05 19 Meters And Gauges For Hvac Piping																								
	 S1990 Prepare & Submit Meters And Gauges For Hvac Piping	45	09-Oct-23 A	28-Nov-23 A	03-Jun-24	03-Jun-24		100%	 Prepare & Submit Meters And Gauges For Hvac Piping																								
	 S2000 Review & Approve Meters And Gauges For Hvac Piping	30	09-Oct-23 A	28-Nov-23 A	03-Jun-24	03-Jun-24		100%	 Review & Approve Meters And Gauges For Hvac Piping																								
	 Section 23 05 48 Vibration Controls For Hvac Piping And Equipment	75	10-Oct-23 A	12-Oct-23 A	21-Mar-24	21-Mar-24			 12-Oct-23 A, Section 23 05 48 Vibration Controls For Hvac Piping And Equipment																								
	 S2110 Prepare & Submit Vibration Controls For Hvac Piping And Equipment	45	10-Oct-23 A	12-Oct-23 A	21-Mar-24	21-Mar-24		100%	 Prepare & Submit Vibration Controls For Hvac Piping And Equipment																								
	 S2120 Review & Approve Vibration Controls For Hvac Piping And Equipment	30	10-Oct-23 A	12-Oct-23 A	21-Mar-24	21-Mar-24		100%	 Review & Approve Vibration Controls For Hvac Piping And Equipment																								
	 Section 23 05 53 Identification For Hvac Piping And Equipment	75	09-Oct-23 A	09-Oct-23 A	05-Apr-24	05-Apr-24			 09-Oct-23 A, Section 23 05 53 Identification For Hvac Piping And Equipment																								
	 S2210 Prepare & Submit Identification For Hvac Piping And Equipment	45	09-Oct-23 A	09-Oct-23 A	05-Apr-24	05-Apr-24		100%	 Prepare & Submit Identification For Hvac Piping And Equipment																								
	 S2220 Review & Approve Identification For Hvac Piping And Equipment	30	09-Oct-23 A	09-Oct-23 A	05-Apr-24	05-Apr-24		100%	 Review & Approve Identification For Hvac Piping And Equipment																								
	 Section 23 05 93 Testing, Adjusting, And Balancing For Hvac	75	09-Oct-23 A	09-Oct-23 A	21-Aug-24	21-Aug-24			 09-Oct-23 A, Section 23 05 93 Testing, Adjusting, And Balancing For Hvac																								
	 S2310 Prepare & Submit Testing, Adjusting, And Balancing For Hvac	45	09-Oct-23 A	09-Oct-23 A	21-Aug-24	21-Aug-24		100%	 Prepare & Submit Testing, Adjusting, And Balancing For Hvac																								
	 S2320 Review & Approve Testing, Adjusting, And Balancing For Hvac	30	09-Oct-23 A	09-Oct-23 A	21-Aug-24	21-Aug-24		100%	 Review & Approve Testing, Adjusting, And Balancing For Hvac																								
	 Section 23 07 13 Duct Insulation	75	20-Sep-23 A	22-Sep-23 A	05-Apr-24	05-Apr-24			 22-Sep-23 A, Section 23 07 13 Duct Insulation																								
	 S2410 Prepare & Submit Duct Insulation	45	20-Sep-23 A	22-Sep-23 A	05-Apr-24	05-Apr-24		100%	 Prepare & Submit Duct Insulation																								
	 S2420 Review & Approve Duct Insulation	30	20-Sep-23 A	22-Sep-23 A	05-Apr-24	05-Apr-24		100%	 Review & Approve Duct Insulation																								
	 Section 23 07 16 Hvac Equipment Insulation	75	20-Sep-23 A	22-Sep-23 A	05-Apr-24	05-Apr-24			 22-Sep-23 A, Section 23 07 16 Hvac Equipment Insulation																								
	 S2510 Prepare & Submit HVAC Equipment Insulation	45	20-Sep-23 A	22-Sep-23 A	05-Apr-24	05-Apr-24		100%	 Prepare & Submit HVAC Equipment Insulation																								
	 S2520 Review & Approve HVAC Equipment Insulation	30	20-Sep-23 A	22-Sep-23 A	05-Apr-24	05-Apr-24		100%	 Review & Approve HVAC Equipment Insulation																								
	 Section 23 07 19 Hvac Piping Insulation	75	20-Sep-23 A	22-Sep-23 A	12-Jun-24	12-Jun-24			 22-Sep-23 A, Section 23 07 19 Hvac Piping Insulation																								
	 S1220 Prepare & Submit HVAC Piping Insulation	45	20-Sep-23 A	22-Sep-23 A	12-Jun-24	12-Jun-24		100%	 Prepare & Submit HVAC Piping Insulation																								
	 S1230 Review & Approve HVAC Piping Insulation	30	20-Sep-23 A	22-Sep-23 A	12-Jun-24	12-Jun-24		100%	 Review & Approve HVAC Piping Insulation																								
	 Section 23 08 00 Commissioning Of Hvac	75	02-Nov-23 A	09-Nov-23 A	05-Sep-24	05-Sep-24			 09-Nov-23 A, Section 23 08 00 Commissioning Of Hvac																								
	 S1970 Prepare & Submit Commissioning Of HVAC	45	02-Nov-23 A	09-Nov-23 A	05-Sep-24	05-Sep-24		100%	 Prepare & Submit Commissioning Of HVAC																								
	 S1980 Review & Approve Commissioning Of HVAC	30	02-Nov-23 A	09-Nov-23 A	05-Sep-24	05-Sep-24		100%	 Review & Approve Commissioning Of HVAC																								
	 Section 23 09 23 Direct-Digital Control System For Hvac	75	15-Dec-23 A	26-Apr-24	10-Jul-24	05-Sep-24	93		 26-Apr-24, Section 23 09 23 Direct-Digital Control System For Hvac																								
	 S2090 Prepare & Submit Direct-Digital Control System For Hvac	45	15-Dec-23 A	26-Apr-24	10-Jul-24	05-Sep-24	93	10%	 Prepare & Submit Direct-Digital Control System For Hvac																								
	 S2100 Review & Approve Direct-Digital Control System For Hvac	30	15-Dec-23 A	08-Apr-24	10-Jul-24	16-Aug-24	93	10%	 Review & Approve Direct-Digital Control System For Hvac																								
	 Section 23 21 13 Hydronic Piping	75	03-Nov-23 A	08-Nov-23 A	05-Aug-24	05-Aug-24			 08-Nov-23 A, Section 23 21 13 Hydronic Piping																								
	 S2190 Prepare & Submit Hydronic Piping	45	03-Nov-23 A	08-Nov-23 A	05-Aug-24	05-Aug-24		100%	 Prepare & Submit Hydronic Piping																								
	 S2200 Review & Approve Hydronic Piping	30	03-Nov-23 A	08-Nov-23 A	05-Aug-24	05-Aug-24		100%	 Review & Approve Hydronic Piping																								
	 Section 23 21 14 Hydronic Specialties	75	26-Oct-23 A	26-Oct-23 A	13-Aug-24	13-Aug-24			 26-Oct-23 A, Section 23 21 14 Hydronic Specialties																								
	 S2290 Prepare & Submit Hydronic Specialties	45	26-Oct-23 A	26-Oct-23 A	13-Aug-24	13-Aug-24		100%	 Prepare & Submit Hydronic Specialties																								
	 S2300 Review & Approve Hydronic Specialties	30	26-Oct-23 A	26-Oct-23 A	13-Aug-24	13-Aug-24		100%	 Review & Approve Hydronic Specialties																								
	 Section 23 21 23 Hydronic Pumps	75	14-Sep-23 A	21-Sep-23 A	13-Aug-24	13-Aug-24			 21-Sep-23 A, Section 23 21 23 Hydronic Pumps																								

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone













Remaining Level of Effort Critical Remaining Work Actual Work Remaining Work Critical Remaining Work Actual Work ◆ ◆ Milestone	Page 3 of 8 Data Date: 29-Feb-24	Early Start Report		Pearls Construction LLC
--	--	----------------------------------	---	---------------------------------------



Nanuet Senior HS Barr MS - Phase 3 - Update #03




Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	2023	2024												2025									
									Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1				
									Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan				
 S2040	Review & Approve Air Cooled Refrigerant Compressor And Condenser Unit	30	22-Nov-23 A	27-Feb-24 A	05-Aug-24	05-Aug-24		100%								Review & Approve Air Cooled Refrigerant Compressor And Condenser Unit															
 Section 23 73 13 Indoor Air-Handling Units		75	13-Sep-23 A	10-Oct-23 A	03-Jul-24	03-Jul-24							 10-Oct-23 A, Section 23 73 13 Indoor Air-Handling Units																		
 S2130	Prepare & Submit IndoorAir-Handling Units	45	13-Sep-23 A	10-Oct-23 A	03-Jul-24	03-Jul-24		100%								Prepare & Submit IndoorAir-Handling Units															
 S2140	Review & Approve Indoor Air-Handling Units	30	13-Sep-23 A	10-Oct-23 A	03-Jul-24	03-Jul-24		100%								Review & Approve Indoor Air-Handling Units															
 Section 23 74 13 Packaged Rooftop Units		75	02-Nov-23 A	22-Nov-23 A	05-Aug-24	05-Aug-24							 22-Nov-23 A, Section 23 74 13 Packaged Rooftop Units																		
 S2230	Prepare & Submit Packaged Rooftop Units	45	02-Nov-23 A	22-Nov-23 A	05-Aug-24	05-Aug-24		100%								Prepare & Submit Packaged Rooftop Units															
 S2240	Review & Approve Packaged Rooftop Units	30	02-Nov-23 A	22-Nov-23 A	05-Aug-24	05-Aug-24		100%								Review & Approve Packaged Rooftop Units															
 Section 23 81 29 Variable Refrigerant Flow Hvac Systems		75	02-Nov-23 A	22-Nov-23 A	05-Aug-24	05-Aug-24							 22-Nov-23 A, Section 23 81 29 Variable Refrigerant Flow Hvac Systems																		
 S2330	Prepare & Submit Variable Refrigerant Flow Hvac Systems	45	02-Nov-23 A	22-Nov-23 A	05-Aug-24	05-Aug-24		100%								Prepare & Submit Variable Refrigerant Flow Hvac Systems															
 S2340	Review & Approve Variable Refrigerant Flow Hvac Systems	30	02-Nov-23 A	22-Nov-23 A	05-Aug-24	05-Aug-24		100%								Review & Approve Variable Refrigerant Flow Hvac Systems															
 Section 23 82 00 Convection Heating And Cooling Units		75	13-Sep-23 A	15-Sep-23 A	05-Aug-24	05-Aug-24							 15-Sep-23 A, Section 23 82 00 Convection Heating And Cooling Units																		
 S2430	Prepare & Submit Convection Heating And Cooling Units	45	13-Sep-23 A	15-Sep-23 A	05-Aug-24	05-Aug-24		100%								Prepare & Submit Convection Heating And Cooling Units															
 S2440	Review & Approve Convection Heating And Cooling Units	30	13-Sep-23 A	15-Sep-23 A	05-Aug-24	05-Aug-24		100%								Review & Approve Convection Heating And Cooling Units															
 Division 26 - Electrical		75	15-Sep-23 A	29-Sep-23 A	15-Apr-24	15-Apr-24							 29-Sep-23 A, Division 26 - Electrical																		
 Section 26 29 23 Variable-Frequency Motor Controllers		75	15-Sep-23 A	29-Sep-23 A	15-Apr-24	15-Apr-24							 29-Sep-23 A, Section 26 29 23 Variable-Frequency Motor Controllers																		
 S1670	Prepare & Submit Variable-Frequency Motor Controllers	45	15-Sep-23 A	29-Sep-23 A	15-Apr-24	15-Apr-24		100%								Prepare & Submit Variable-Frequency Motor Controllers															
 S1680	Review & Approve Variable-Frequency Motor Controllers	30	15-Sep-23 A	29-Sep-23 A	15-Apr-24	15-Apr-24		100%								Review & Approve Variable-Frequency Motor Controllers															
 Procurement		183	13-Oct-23 A	18-Apr-24	21-Mar-24	03-Sep-24	95						 18-Apr-24, Procurement																		
 S1300	Fabricate & Deliver Radaint Runtal Baseboard-MS-1 & 2 - SRS	40	13-Oct-23 A	15-Nov-23 A	21-Aug-24	21-Aug-24		100%								Fabricate & Deliver Radaint Runtal Baseboard-MS-1 & 2 - SRS															
 S1310	Fabricate & Deliver EF-8, 10, 21 & 23 Samtepp	150	13-Oct-23 A	06-Jan-24 A	02-Aug-24	02-Aug-24		100%								Fabricate & Deliver EF-8, 10, 21 & 23 Samtepp															
 S1320	Fabricate & Deliver Dampers RKB	88	13-Oct-23 A	17-Apr-24	17-Jun-24	05-Aug-24	77	60%											Fabricate & Deliver Dampers RKB												
 S1340	Fabricate & Deliver UV-MS- 1-41 D&B	55	13-Oct-23 A	15-Jan-24 A	05-Aug-24	05-Aug-24		100%								Fabricate & Deliver UV-MS- 1-41 D&B															
 S1350	Fabricate & Deliver HP-MS-3-9 D&B	60	13-Oct-23 A	21-Nov-23 A	21-Aug-24	21-Aug-24		100%								Fabricate & Deliver HP-MS-3-9 D&B															
 S1360	Fabricate & Deliver CV-HS-1-11	40	13-Oct-23 A	12-Nov-23 A	03-Jul-24	03-Jul-24		100%								Fabricate & Deliver CV-HS-1-11															
 S1370	Fabricate & Deliver UH-HS-1 GC Sales	20	13-Oct-23 A	08-Nov-23 A	15-Apr-24	15-Apr-24		100%								Fabricate & Deliver UH-HS-1 GC Sales															
 S1380	Fabricate & Deliver CUH- HS-1, 2, 3 GS Sales	40	13-Oct-23 A	30-Nov-23 A	03-Jul-24	03-Jul-24		100%								Fabricate & Deliver CUH- HS-1, 2, 3 GS Sales															
 S1390	Fabricate & Deliver radinat runtal HS R2-1, 2, 3, & 4 SRS	40	13-Oct-23 A	15-Nov-23 A	03-Jul-24	03-Jul-24		100%								Fabricate & Deliver radinat runtal HS R2-1, 2, 3, & 4 SRS															
 S1400	Fabricate & Deliver F-HS-2 & 3 D&B	150	13-Oct-23 A	01-Mar-24	01-Apr-24	01-Apr-24	21	99%								Fabricate & Deliver F-HS-2 & 3 D&B															
 S1410	Fabricate & Deliver L-1 Louver with bird screen RKB	88	13-Oct-23 A	18-Apr-24	14-Jun-24	05-Aug-24	76	60%											Fabricate & Deliver L-1 Louver with bird screen RKB												
 S1420	Fabricate & Deliver RTU-HS- 4 & 5 D&B	110	13-Oct-23 A	23-Feb-24 A	01-Apr-24	01-Apr-24		100%								Fabricate & Deliver RTU-HS- 4 & 5 D&B															
 S1430	Fabricate & Deliver BC-HS-1 & 2 D&B	70	13-Oct-23 A	21-Nov-23 A	21-Mar-24	21-Mar-24		100%								Fabricate & Deliver BC-HS-1 & 2 D&B															
 S1440	Fabricate & Deliver HC-HS-2 to 4 D&B	40	13-Oct-23 A	21-Nov-23 A	15-Apr-24	15-Apr-24		100%								Fabricate & Deliver HC-HS-2 to 4 D&B															
 S1450	Fabricate & Deliver AHU-HS-3 D&B	120	13-Oct-23 A	24-Jan-24 A	03-Jul-24	03-Jul-24		100%								Fabricate & Deliver AHU-HS-3 D&B															
 S1460	Fabricate & Deliver ACCU-HS 2 D&B	60	13-Oct-23 A	01-Dec-23 A	03-Sep-24	03-Sep-24		100%								Fabricate & Deliver ACCU-HS 2 D&B															
 S1470	Fabricate & Deliver CP-HS-2 WE	140	13-Oct-23 A	05-Nov-23 A	15-Apr-24	15-Apr-24		100%								Fabricate & Deliver CP-HS-2 WE															



Nanuet Senior HS Barr MS - Phase 3 - Update #03



Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	2023												2024												2025
									Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1						
									Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan						
 S1480	Fabricate & Deliver HX-HS-2 WE	40	13-Oct-23 A	02-Nov-23 A	15-Apr-24	15-Apr-24		100%																									
 S1490	Fabricate & Deliver P-HS-3, 4, 5 & 6 WE	120	13-Oct-23 A	28-Nov-23 A	15-Apr-24	15-Apr-24		100%																									
 S1500	Fabricate & Deliver B&G Suction Diffuser WE	80	13-Oct-23 A	05-Jan-24 A	12-Jun-24	12-Jun-24		100%																									
 S1510	Fabricate & Deliver B&G Triple Duty Valve WE	100	13-Oct-23 A	06-Jan-24 A	12-Jun-24	12-Jun-24		100%																									
 S1520	Fabricate & Deliver Flex Hose 6"X 24" WE	30	13-Oct-23 A	02-Nov-23 A	15-Apr-24	15-Apr-24		100%																									
 S1530	Fabricate & Deliver EXP-HS-2 & 3 WE	80	13-Oct-23 A	20-Feb-24 A	15-Apr-24	15-Apr-24		100%																									
 S1540	Fabricate & Deliver Flex Hose Exp Loops WE	30	13-Oct-23 A	02-Nov-23 A	15-Apr-24	15-Apr-24		100%																									
 S3200	Fabricate & Deliver FT-MS-1 GC SALES	35	13-Oct-23 A	15-Nov-23 A	05-Aug-24	05-Aug-24		100%																									
 Construction		246	10-Oct-23 A	19-Sep-24	21-Mar-24	19-Sep-24	0		 19-Sep-24, Construction																								
 Mobilization		10	10-Oct-23 A	13-Oct-23 A	21-Mar-24	21-Mar-24			 13-Oct-23 A, Mobilization																								
 C6920	Mobilization & Site Prep. Mobilized demo of cielings	10	10-Oct-23 A	13-Oct-23 A	21-Mar-24	21-Mar-24		100%																									
 Nanuet Senior HS		135	05-Jan-24 A	05-Sep-24	21-Mar-24	17-Sep-24	9		 05-Sep-24, Nanuet Senior HS																								
 Demolition		14	01-Mar-24	20-Mar-24	31-May-24	20-Jun-24	66		 20-Mar-24, Demolition																								
 C5920	Remove Unit Ventilator - First Floor - Nanuet Senior HS	1	01-Mar-24	01-Mar-24	31-May-24	01-Jun-24	64	0%																									
 C7030	Remove HVAC Ducts & Piping - Nanuet Senior HS	14	01-Mar-24	20-Mar-24	01-Jun-24	20-Jun-24	66	0%																									
 C5950	Remove & Salvage Existing Wainscoting Pipe Enclosure - First Floor - Nanuet Senior HS	1	04-Mar-24	04-Mar-24	01-Jun-24	03-Jun-24	64	0%																									
 Basement		127	05-Jan-24 A	27-Jun-24	15-Apr-24	03-Jul-24	4		 27-Jun-24, Basement																								
 Architectural		52	05-Jan-24 A	24-Jun-24	12-Jun-24	28-Jun-24	4		 24-Jun-24, Architectural																								
 C6870	Patch Ceilings - Basement - Nanuet Senior HS	2	05-Jan-24 A	18-Jun-24	12-Jun-24	18-Jun-24	0	25%																									
 C6910	Patch Walls - Basement - Nanuet Senior HS	3	19-Jun-24	21-Jun-24	19-Jun-24	21-Jun-24	0	0%																									
 C6760	Patch Flooring - Basement - Nanuet Senior HS	1	24-Jun-24	24-Jun-24	28-Jun-24	28-Jun-24	4	0%																									
 Mechanical		125	11-Jan-24 A	27-Jun-24	15-Apr-24	03-Jul-24	4		 27-Jun-24, Mechanical																								
 C6600	Install Mechanical Ducts & Pipes Hangers - Basement - Nanuet Senior HS	2	11-Jan-24 A	04-Mar-24	03-Jun-24	03-Jun-24	64	95%																									
 C6610	Install HVAC Ducts & Pipes - Basement - Nanuet Senior HS	10	11-Jan-24 A	20-Mar-24	12-Jun-24	20-Jun-24	66	40%																									
 C6630	Install Above ceiling Terminal Equipment - Basement - Nanuet Senior HS	6	11-Jan-24 A	08-Mar-24	24-Jun-24	28-Jun-24	80	40%																									
 C7120	Install Mechanical Equipment - Basement - Nanuet Senior HS	10	11-Jan-24 A	27-Jun-24	15-Apr-24	03-Jul-24	4	95%																									
 C6640	Mechanical Rough-Ins Inspection - Basement - Nanuet Senior HS	3	25-Jan-24 A	05-Mar-24	26-Jun-24	26-Jun-24	81	95%																									
 C6650	Mechanical Rough-Ins Punchlist - Basement - Nanuet Senior HS	3	05-Mar-24	08-Mar-24	27-Jun-24	01-Jul-24	81	0%																									
 C6620	Insulate HVAC Ducts & Pipes - Basement - Nanuet Senior HS	1	25-Jun-24	25-Jun-24	01-Jul-24	01-Jul-24	4	0%																									
 C6660	Install Grilles & Difussers - Basement - Nanuet Senior HS	2	26-Jun-24	27-Jun-24	02-Jul-24	03-Jul-24	4	0%																									
 First Floor		110	05-Jan-24 A	17-Jul-24	03-Jun-24	17-Jul-24	0		 17-Jul-24, First Floor																								
 Architectural		33	05-Jan-24 A	02-Jul-24	19-Jun-24	02-Jul-24	0		 02-Jul-24, Architectural																								
 C6550	Patch Ceilings - First Floor - Nanuet Senior HS	2	05-Jan-24 A	18-Jun-24	19-Jun-24	21-Jun-24	3	20%																									
 C6590	Patch Walls - First Floor - Nanuet Senior HS	2	24-Jun-24	25-Jun-24	24-Jun-24	25-Jun-24	0	0%																									
 C6440	Patch Flooring - First Floor - Nanuet Senior HS	5	26-Jun-24	02-Jul-24	26-Jun-24	02-Jul-24	0	0%																									

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone



