






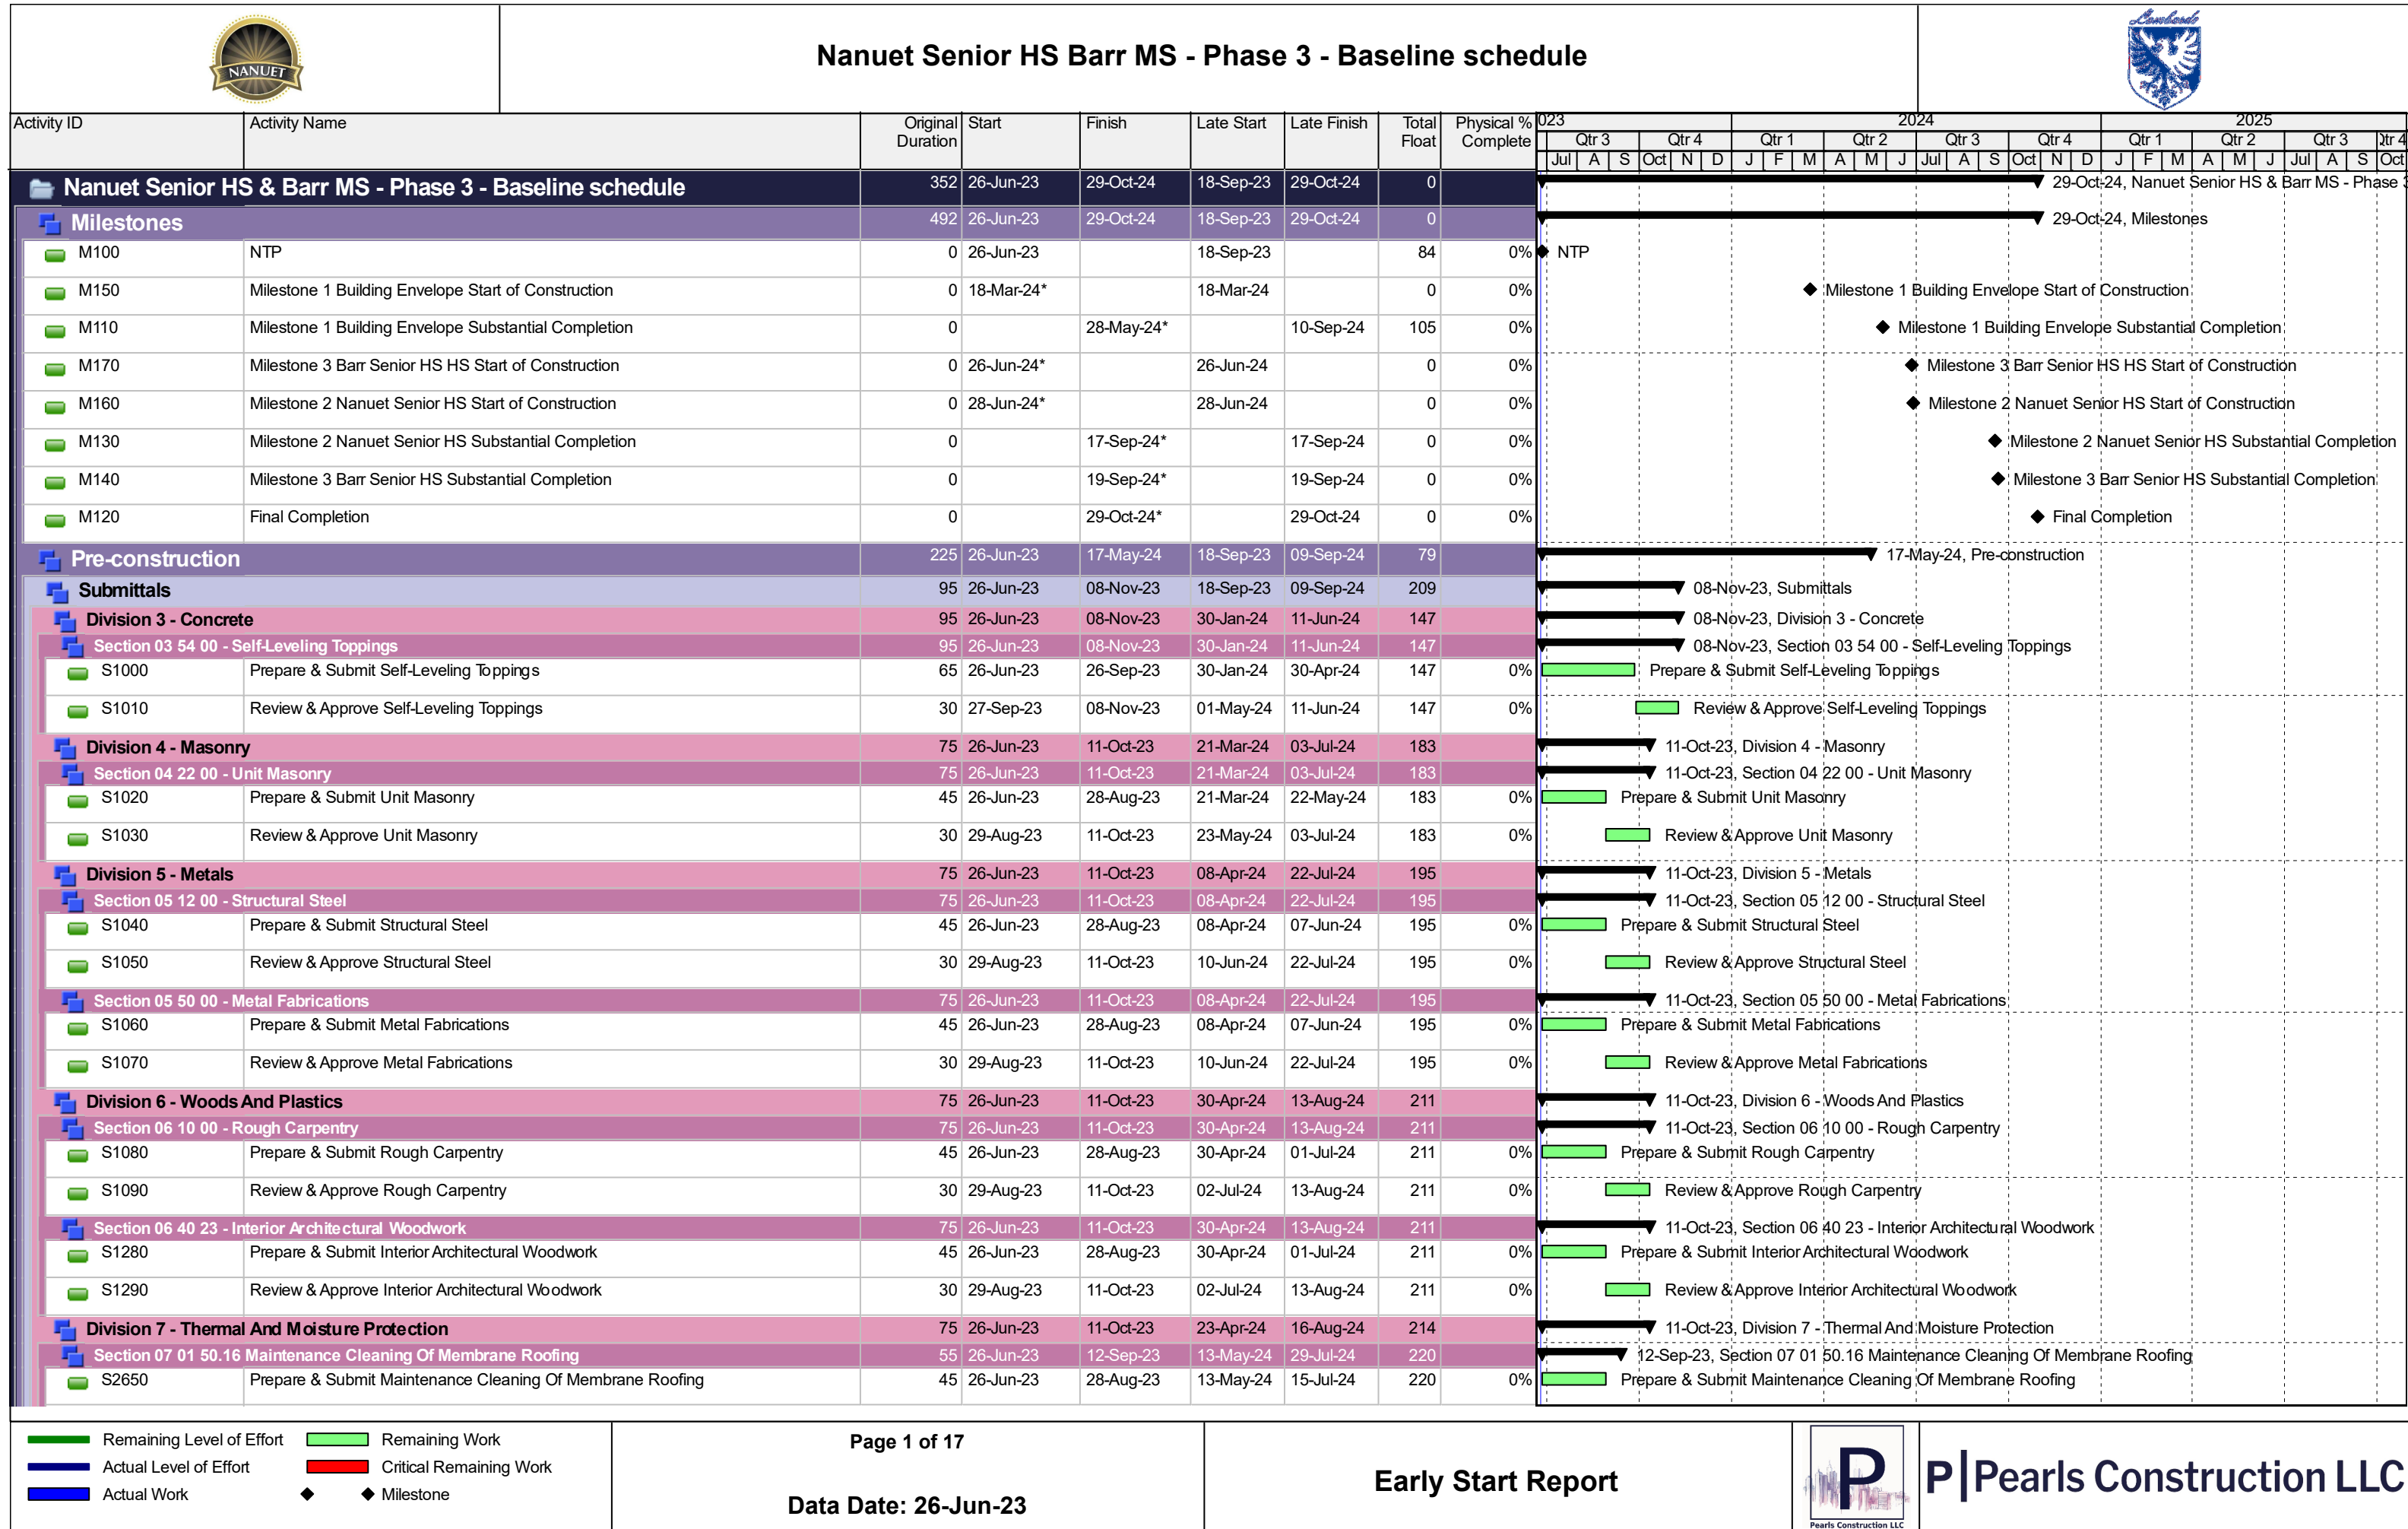

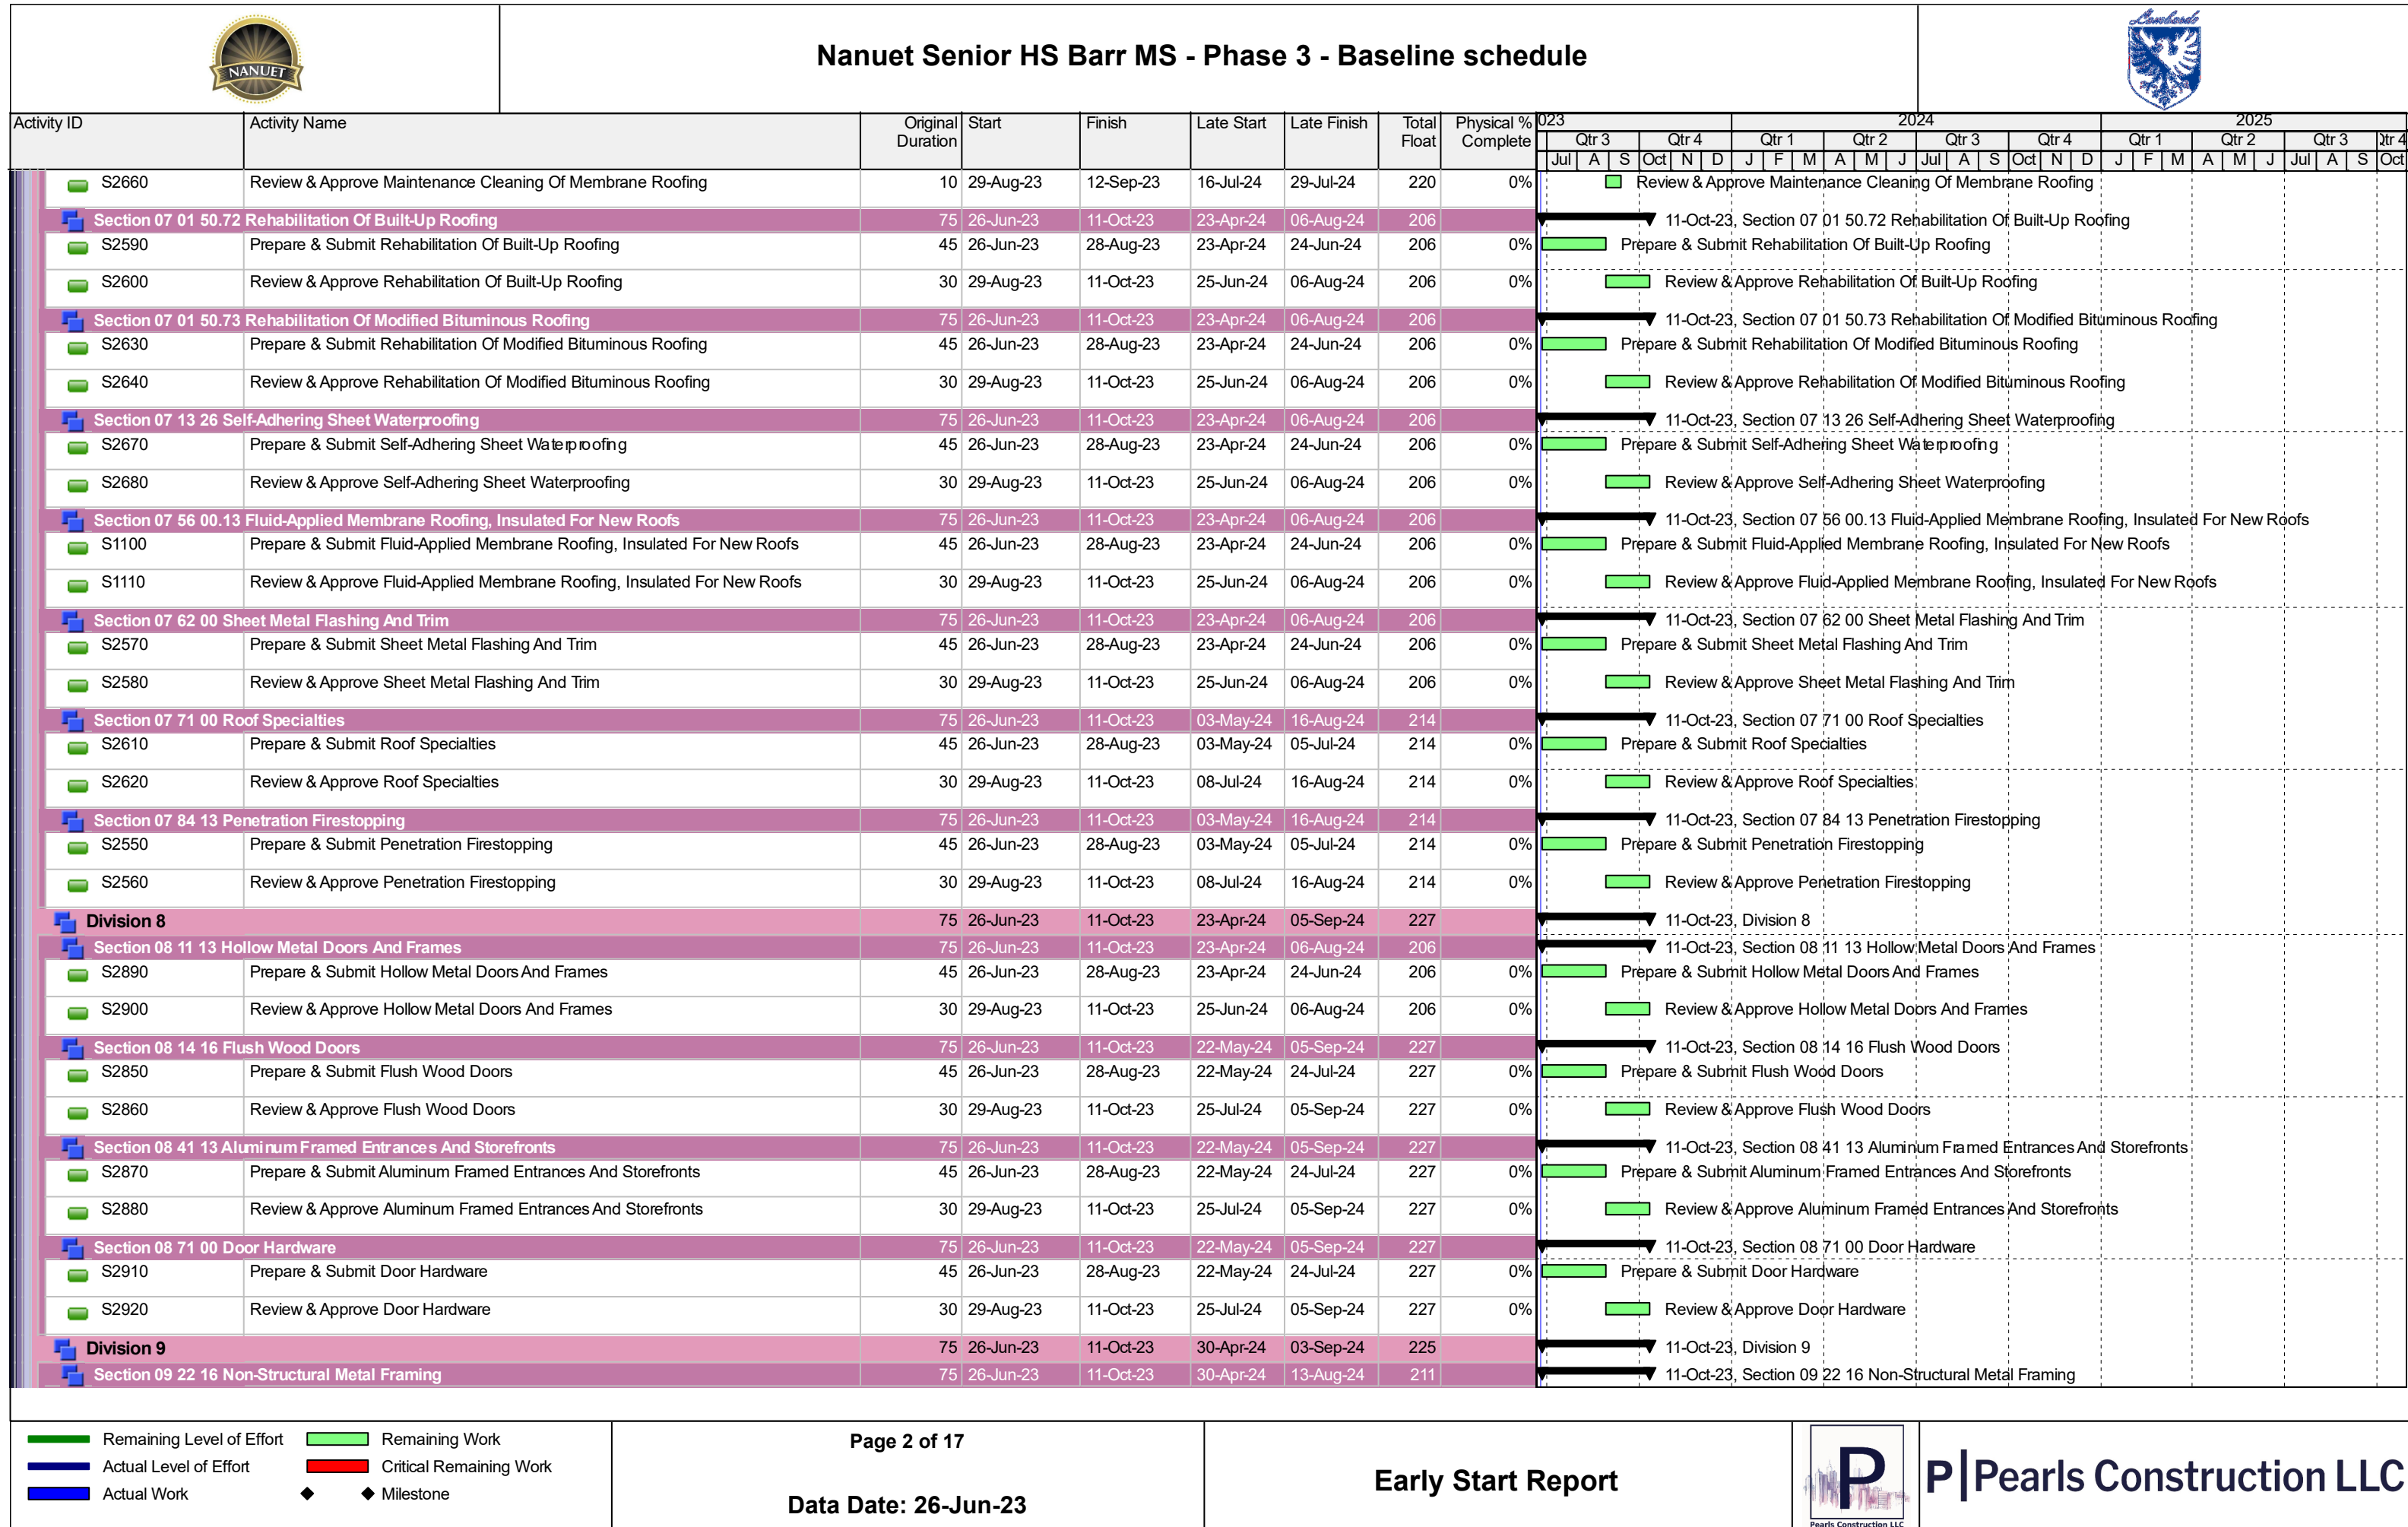

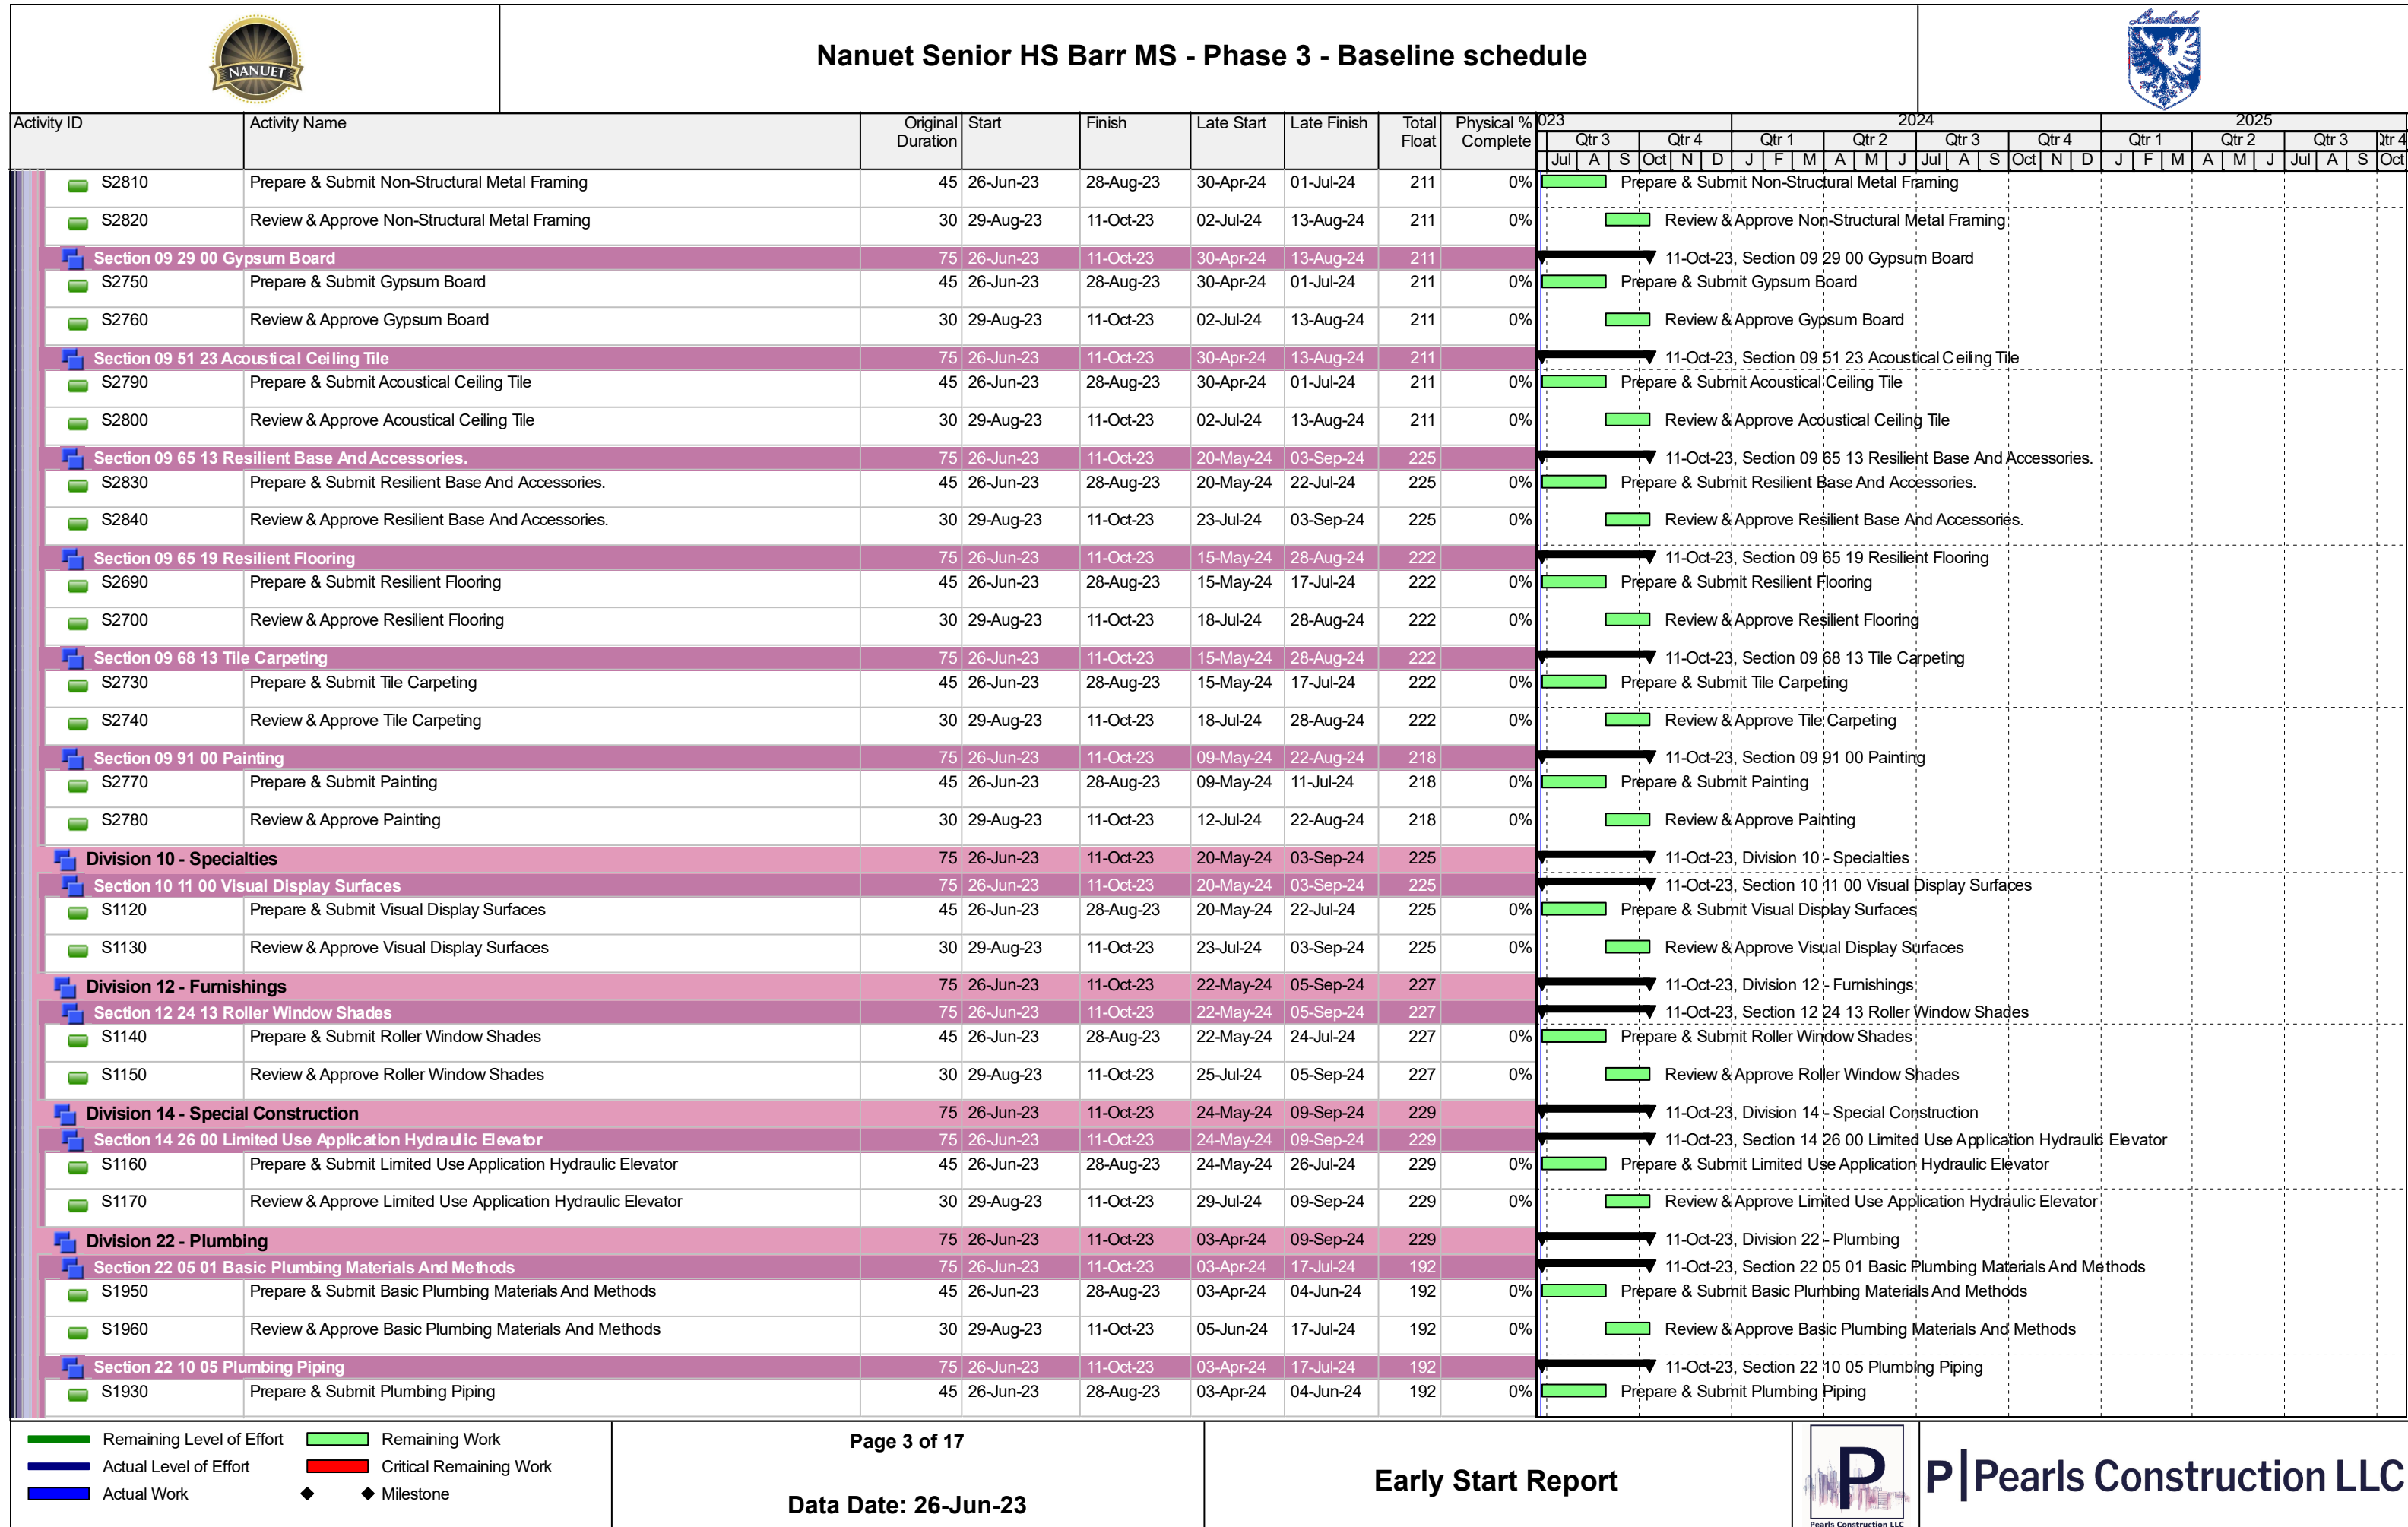

Nanuet Senior HS Barr MS - Phase 3 - Baseline schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	2023							2024							2025																	
									Qtr 3			Qtr 4				Qtr 1			Qtr 2				Qtr 3			Qtr 4				Qtr 1			Qtr 2				Qtr 3			Qtr 4
									Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct				
 S1940	Review & Approve Plumbing Piping	30	29-Aug-23	11-Oct-23	05-Jun-24	17-Jul-24	192	0%																																
 Section 22 10 06 Plumbing Piping Specialties		75	26-Jun-23	11-Oct-23	15-May-24	09-Sep-24	229																																	
 S1910	Prepare & Submit Plumbing Piping Specialties	45	26-Jun-23	28-Aug-23	15-May-24	17-Jul-24	222	0%																																
 S1920	Review & Approve Plumbing Piping Specialties	30	29-Aug-23	11-Oct-23	29-Jul-24	09-Sep-24	229	0%																																
 Section 22 30 00 Plumbing Equipment		75	26-Jun-23	11-Oct-23	03-Apr-24	17-Jul-24	192																																	
 S1200	Prepare & Submit Plumbing Equipment	45	26-Jun-23	28-Aug-23	03-Apr-24	04-Jun-24	192	0%																																
 S1210	Review & Approve Plumbing Equipment	30	29-Aug-23	11-Oct-23	05-Jun-24	17-Jul-24	192	0%																																
 Division 23 - Heating, Ventilating, And Air-Conditioning (Hvac)		75	26-Jun-23	11-Oct-23	18-Sep-23	04-Sep-24	226																																	
 Section 23 05 01 Basic Hvac Materials And Methods		75	26-Jun-23	11-Oct-23	09-Apr-24	23-Jul-24	196																																	
 S2530	Prepare & Submit Basic Hvac Materials And Methods	45	26-Jun-23	28-Aug-23	09-Apr-24	10-Jun-24	196	0%																																
 S2540	Review & Approve Basic Hvac Materials And Methods	30	29-Aug-23	11-Oct-23	11-Jun-24	23-Jul-24	196	0%																																
 Section 23 05 16 Expansion Fittings And Loops For Hvac Piping		75	26-Jun-23	11-Oct-23	09-Apr-24	23-Jul-24	196																																	
 S2010	Prepare & Submit Expansion Fittings And Loops For Hvac Piping	45	26-Jun-23	28-Aug-23	09-Apr-24	10-Jun-24	196	0%																																
 S2020	Review & Approve Expansion Fittings And Loops For Hvac Piping	30	29-Aug-23	11-Oct-23	11-Jun-24	23-Jul-24	196	0%																																
 Section 23 05 19 Meters And Gauges For Hvac Piping		75	26-Jun-23	11-Oct-23	09-Apr-24	23-Jul-24	196																																	
 S1990	Prepare & Submit Meters And Gauges For Hvac Piping	45	26-Jun-23	28-Aug-23	09-Apr-24	10-Jun-24	196	0%																																
 S2000	Review & Approve Meters And Gauges For Hvac Piping	30	29-Aug-23	11-Oct-23	11-Jun-24	23-Jul-24	196	0%																																
 Section 23 05 48 Vibration Controls For Hvac Piping And Equipment		75	26-Jun-23	11-Oct-23	18-Sep-23	08-Jan-24	58																																	
 S2110	Prepare & Submit Vibration Controls For Hvac Piping And Equipment	45	26-Jun-23	28-Aug-23	18-Sep-23	21-Nov-23	58	0%																																
 S2120	Review & Approve Vibration Controls For Hvac Piping And Equipment	30	29-Aug-23	11-Oct-23	22-Nov-23	08-Jan-24	58	0%																																
 Section 23 05 53 Identification For Hvac Piping And Equipment		75	26-Jun-23	11-Oct-23	09-Apr-24	23-Jul-24	196																																	
 S2210	Prepare & Submit Identification For Hvac Piping And Equipment	45	26-Jun-23	28-Aug-23	09-Apr-24	10-Jun-24	196	0%																																
 S2220	Review & Approve Identification For Hvac Piping And Equipment	30	29-Aug-23	11-Oct-23	11-Jun-24	23-Jul-24	196	0%																																
 Section 23 05 93 Testing, Adjusting, And Balancing For Hvac		75	26-Jun-23	11-Oct-23	06-May-24	19-Aug-24	215																																	
 S2310	Prepare & Submit Testing, Adjusting, And Balancing For Hvac	45	26-Jun-23	28-Aug-23	06-May-24	08-Jul-24	215	0%																																
 S2320	Review & Approve Testing, Adjusting, And Balancing For Hvac	30	29-Aug-23	11-Oct-23	09-Jul-24	19-Aug-24	215	0%																																
 Section 23 07 13 Duct Insulation		75	26-Jun-23	11-Oct-23	22-Apr-24	05-Aug-24	205																																	
 S2410	Prepare & Submit Duct Insulation	45	26-Jun-23	28-Aug-23	22-Apr-24	21-Jun-24	205	0%																																
 S2420	Review & Approve Duct Insulation	30	29-Aug-23	11-Oct-23	24-Jun-24	05-Aug-24	205	0%																																
 Section 23 07 16 Hvac Equipment Insulation		75	26-Jun-23	11-Oct-23	13-May-24	26-Aug-24	220																																	
 S2510	Prepare & Submit HVAC Equipment Insulation	45	26-Jun-23	28-Aug-23	13-May-24	15-Jul-24	220	0%																																
 S2520	Review & Approve HVAC Equipment Insulation	30	29-Aug-23	11-Oct-23	16-Jul-24	26-Aug-24	220	0%																																
 Section 23 07 19 Hvac Piping Insulation		75	26-Jun-23	11-Oct-23	04-Apr-24	18-Jul-24	193																																	
 S1220	Prepare & Submit HVAC Piping Insulation	45	26-Jun-23	28-Aug-23	04-Apr-24	05-Jun-24	193	0%																																
 S1230	Review & Approve HVAC Piping Insulation	30	29-Aug-23	11-Oct-23	06-Jun-24	18-Jul-24	193	0%																																
 Section 23 08 00 Commissioning Of Hvac		75	26-Jun-23	11-Oct-23	21-May-24	04-Sep-24	226																																	
 S1970	Prepare & Submit Commissioning Of HVAC	45	26-Jun-23	28-Aug-23	21-May-24	23-Jul-24	226	0%																																

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone





Nanuet Senior HS Barr MS - Phase 3 - Baseline schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	2023										2024										2025										
									Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			
									Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct			
	 S1980	Review & Approve Commissioning Of HVAC	30	29-Aug-23	11-Oct-23	24-Jul-24	04-Sep-24	226	0%		Review & Approve Commissioning Of HVAC																												
	 Section 23 09 23 Direct-Digital Control System For Hvac		75	26-Jun-23	11-Oct-23	15-May-24	28-Aug-24	222			11-Oct-23, Section 23 09 23 Direct-Digital Control System For Hvac																												
	 S2090	Prepare & Submit Direct-Digital Control System For Hvac	45	26-Jun-23	28-Aug-23	15-May-24	17-Jul-24	222	0%		Prepare & Submit Direct-Digital Control System For Hvac																												
	 S2100	Review & Approve Direct-Digital Control System For Hvac	30	29-Aug-23	11-Oct-23	18-Jul-24	28-Aug-24	222	0%		Review & Approve Direct-Digital Control System For Hvac																												
	 Section 23 21 13 Hydronic Piping		75	26-Jun-23	11-Oct-23	11-Apr-24	25-Jul-24	198			11-Oct-23, Section 23 21 13 Hydronic Piping																												
	 S2190	Prepare & Submit Hydronic Piping	45	26-Jun-23	28-Aug-23	11-Apr-24	12-Jun-24	198	0%		Prepare & Subrnit Hydronic Piping																												
	 S2200	Review & Approve Hydronic Piping	30	29-Aug-23	11-Oct-23	13-Jun-24	25-Jul-24	198	0%		Review & Approve Hydronic Piping																												
	 Section 23 21 14 Hydronic Specialties		75	26-Jun-23	11-Oct-23	01-May-24	14-Aug-24	212			11-Oct-23, Section 23 21 14 Hydronic Specialties																												
	 S2290	Prepare & Submit Hydronic Specialties	45	26-Jun-23	28-Aug-23	01-May-24	02-Jul-24	212	0%		Prepare & Submit Hydronic Specialties																												
	 S2300	Review & Approve Hydronic Specialties	30	29-Aug-23	11-Oct-23	03-Jul-24	14-Aug-24	212	0%		Review & Approve Hydronic Specialties																												
	 Section 23 21 23 Hydronic Pumps		75	26-Jun-23	11-Oct-23	01-May-24	14-Aug-24	212			11-Oct-23, Section 23 21 23 Hydronic Pumps																												
	 S2390	Prepare & Submit Hydronic Pumps	45	26-Jun-23	28-Aug-23	01-May-24	02-Jul-24	212	0%		Prepare & Submit Hydronic Pumps																												
	 S2400	Review & Approve Hydronic Pumps	30	29-Aug-23	11-Oct-23	03-Jul-24	14-Aug-24	212	0%		Review & Approve Hydronic Pumps																												
	 Section 23 22 13 Steam And Condensate Heating Piping		75	26-Jun-23	11-Oct-23	11-Apr-24	25-Jul-24	198			11-Oct-23, Section 23 22 13 Steam And Condensate Heating Piping																												
	 S2490	Prepare & Submit Steam And Condensate Heating Piping	45	26-Jun-23	28-Aug-23	11-Apr-24	12-Jun-24	198	0%		Prepare & Submit Steam And Condensate Heating Piping																												
	 S2500	Review & Approve Steam And Condensate Heating Piping	30	29-Aug-23	11-Oct-23	13-Jun-24	25-Jul-24	198	0%		Review & Approve Steam And Condensate Heating Piping																												
	 Section 23 22 14 Steam And Condensate Heating Specialties		75	26-Jun-23	11-Oct-23	11-Apr-24	25-Jul-24	198			11-Oct-23, Section 23 22 14 Steam And Condensate Heating Specialties																												
	 S2050	Prepare & Submit Steam And Condensate Heating Specialties	45	26-Jun-23	28-Aug-23	11-Apr-24	12-Jun-24	198	0%		Prepare & Submit Steam And Condensate Heating Specialties																												
	 S2060	Review & Approve Steam And Condensate Heating Specialties	30	29-Aug-23	11-Oct-23	13-Jun-24	25-Jul-24	198	0%		Review & Approve Steam And Condensate Heating Specialties																												
	 Section 23 23 00 Refrigerant Piping		75	26-Jun-23	11-Oct-23	28-Mar-24	11-Jul-24	188			11-Oct-23, Section 23 23 00 Refrigerant Piping																												
	 S2150	Prepare & Submit Refrigerant Piping	45	26-Jun-23	28-Aug-23	28-Mar-24	30-May-24	188	0%		Prepare & Submit Refrigerant Piping																												
	 S2160	Review & Approve Refrigerant Piping	30	29-Aug-23	11-Oct-23	31-May-24	11-Jul-24	188	0%		Review & Approve Refrigerant Piping																												
	 Section 23 25 00 Hvac Water Treatment		75	26-Jun-23	11-Oct-23	11-Apr-24	25-Jul-24	198			11-Oct-23, Section 23 25 00 Hvac Water Treatment																												
	 S2250	Prepare & Submit Hvac Water Treatment	45	26-Jun-23	28-Aug-23	11-Apr-24	12-Jun-24	198	0%		Prepare & Submit Hvac Water Treatment																												
	 S2260	Review & Approve Hvac Water Treatment	30	29-Aug-23	11-Oct-23	13-Jun-24	25-Jul-24	198	0%		Review & Approve Hvac Water Treatment																												
	 Section 23 31 00 Hvac Ducts And Casings		75	26-Jun-23	11-Oct-23	11-Apr-24	25-Jul-24	198			11-Oct-23, Section 23 31 00 Hvac Ducts And Casings																												
	 S2350	Prepare & Submit Hvac Ducts And Casings	45	26-Jun-23	28-Aug-23	11-Apr-24	12-Jun-24	198	0%		Prepare & Submit Hvac Ducts And Casings																												
	 S2360	Review & Approve Hvac Ducts And Casings	30	29-Aug-23	11-Oct-23	13-Jun-24	25-Jul-24	198	0%		Review & Approve Hvac Ducts And Casings																												
	 Section 23 33 00 Air Duct Accessories		75	26-Jun-23	11-Oct-23	11-Apr-24	25-Jul-24	198			11-Oct-23, Section 23 33 00 Air Duct Accessories																												
	 S2450	Prepare & Submit Air Duct Accessories	45	26-Jun-23	28-Aug-23	11-Apr-24	12-Jun-24	198	0%		Prepare & Submit Air Duct Accessories																												
	 S2460	Review & Approve Air Duct Accessories	30	29-Aug-23	11-Oct-23	13-Jun-24	25-Jul-24	198	0%		Review & Approve Air Duct Accessories																												
	 Section 23 33 19 Duct Silencers		75	26-Jun-23	11-Oct-23	11-Apr-24	25-Jul-24	198			11-Oct-23, Section 23 33 19 Duct Silencers																												
	 S2070	Prepare & Submit Duct Silencers	45	26-Jun-23	28-Aug-23	11-Apr-24	12-Jun-24	198	0%		Prepare & Submit Duct Silencers																												
	 S2080	Review & Approve Duct Silencers	30	29-Aug-23	11-Oct-23	13-Jun-24	25-Jul-24	198	0%		Review & Approve Duct Silencers																												
	 Section 23 34 16 Centrifugal Hvac Fans		75	26-Jun-23	11-Oct-23	11-Apr-24	25-Jul-24	198			11-Oct-23, Section 23 34 16 Centrifugal Hvac Fans																												
	 S2170	Prepare & Submit Centrifugal Hvac Fans	45	26-Jun-23	28-Aug-23	11-Apr-24	12-Jun-24	198	0%		Prepare & Subrnit Centrifugal Hvac Fans																												
	 S2180	Review & Approve Centrifugal Hvac Fans	30	29-Aug-23	11-Oct-23	13-Jun-24	25-Jul-24	198	0%		Review & Approve Centrifugal Hvac Fans																												

Remaining Level of Effort

Actual Level of Effort


Actual Work


Remaining Work

Critical Remaining Work

Milestone



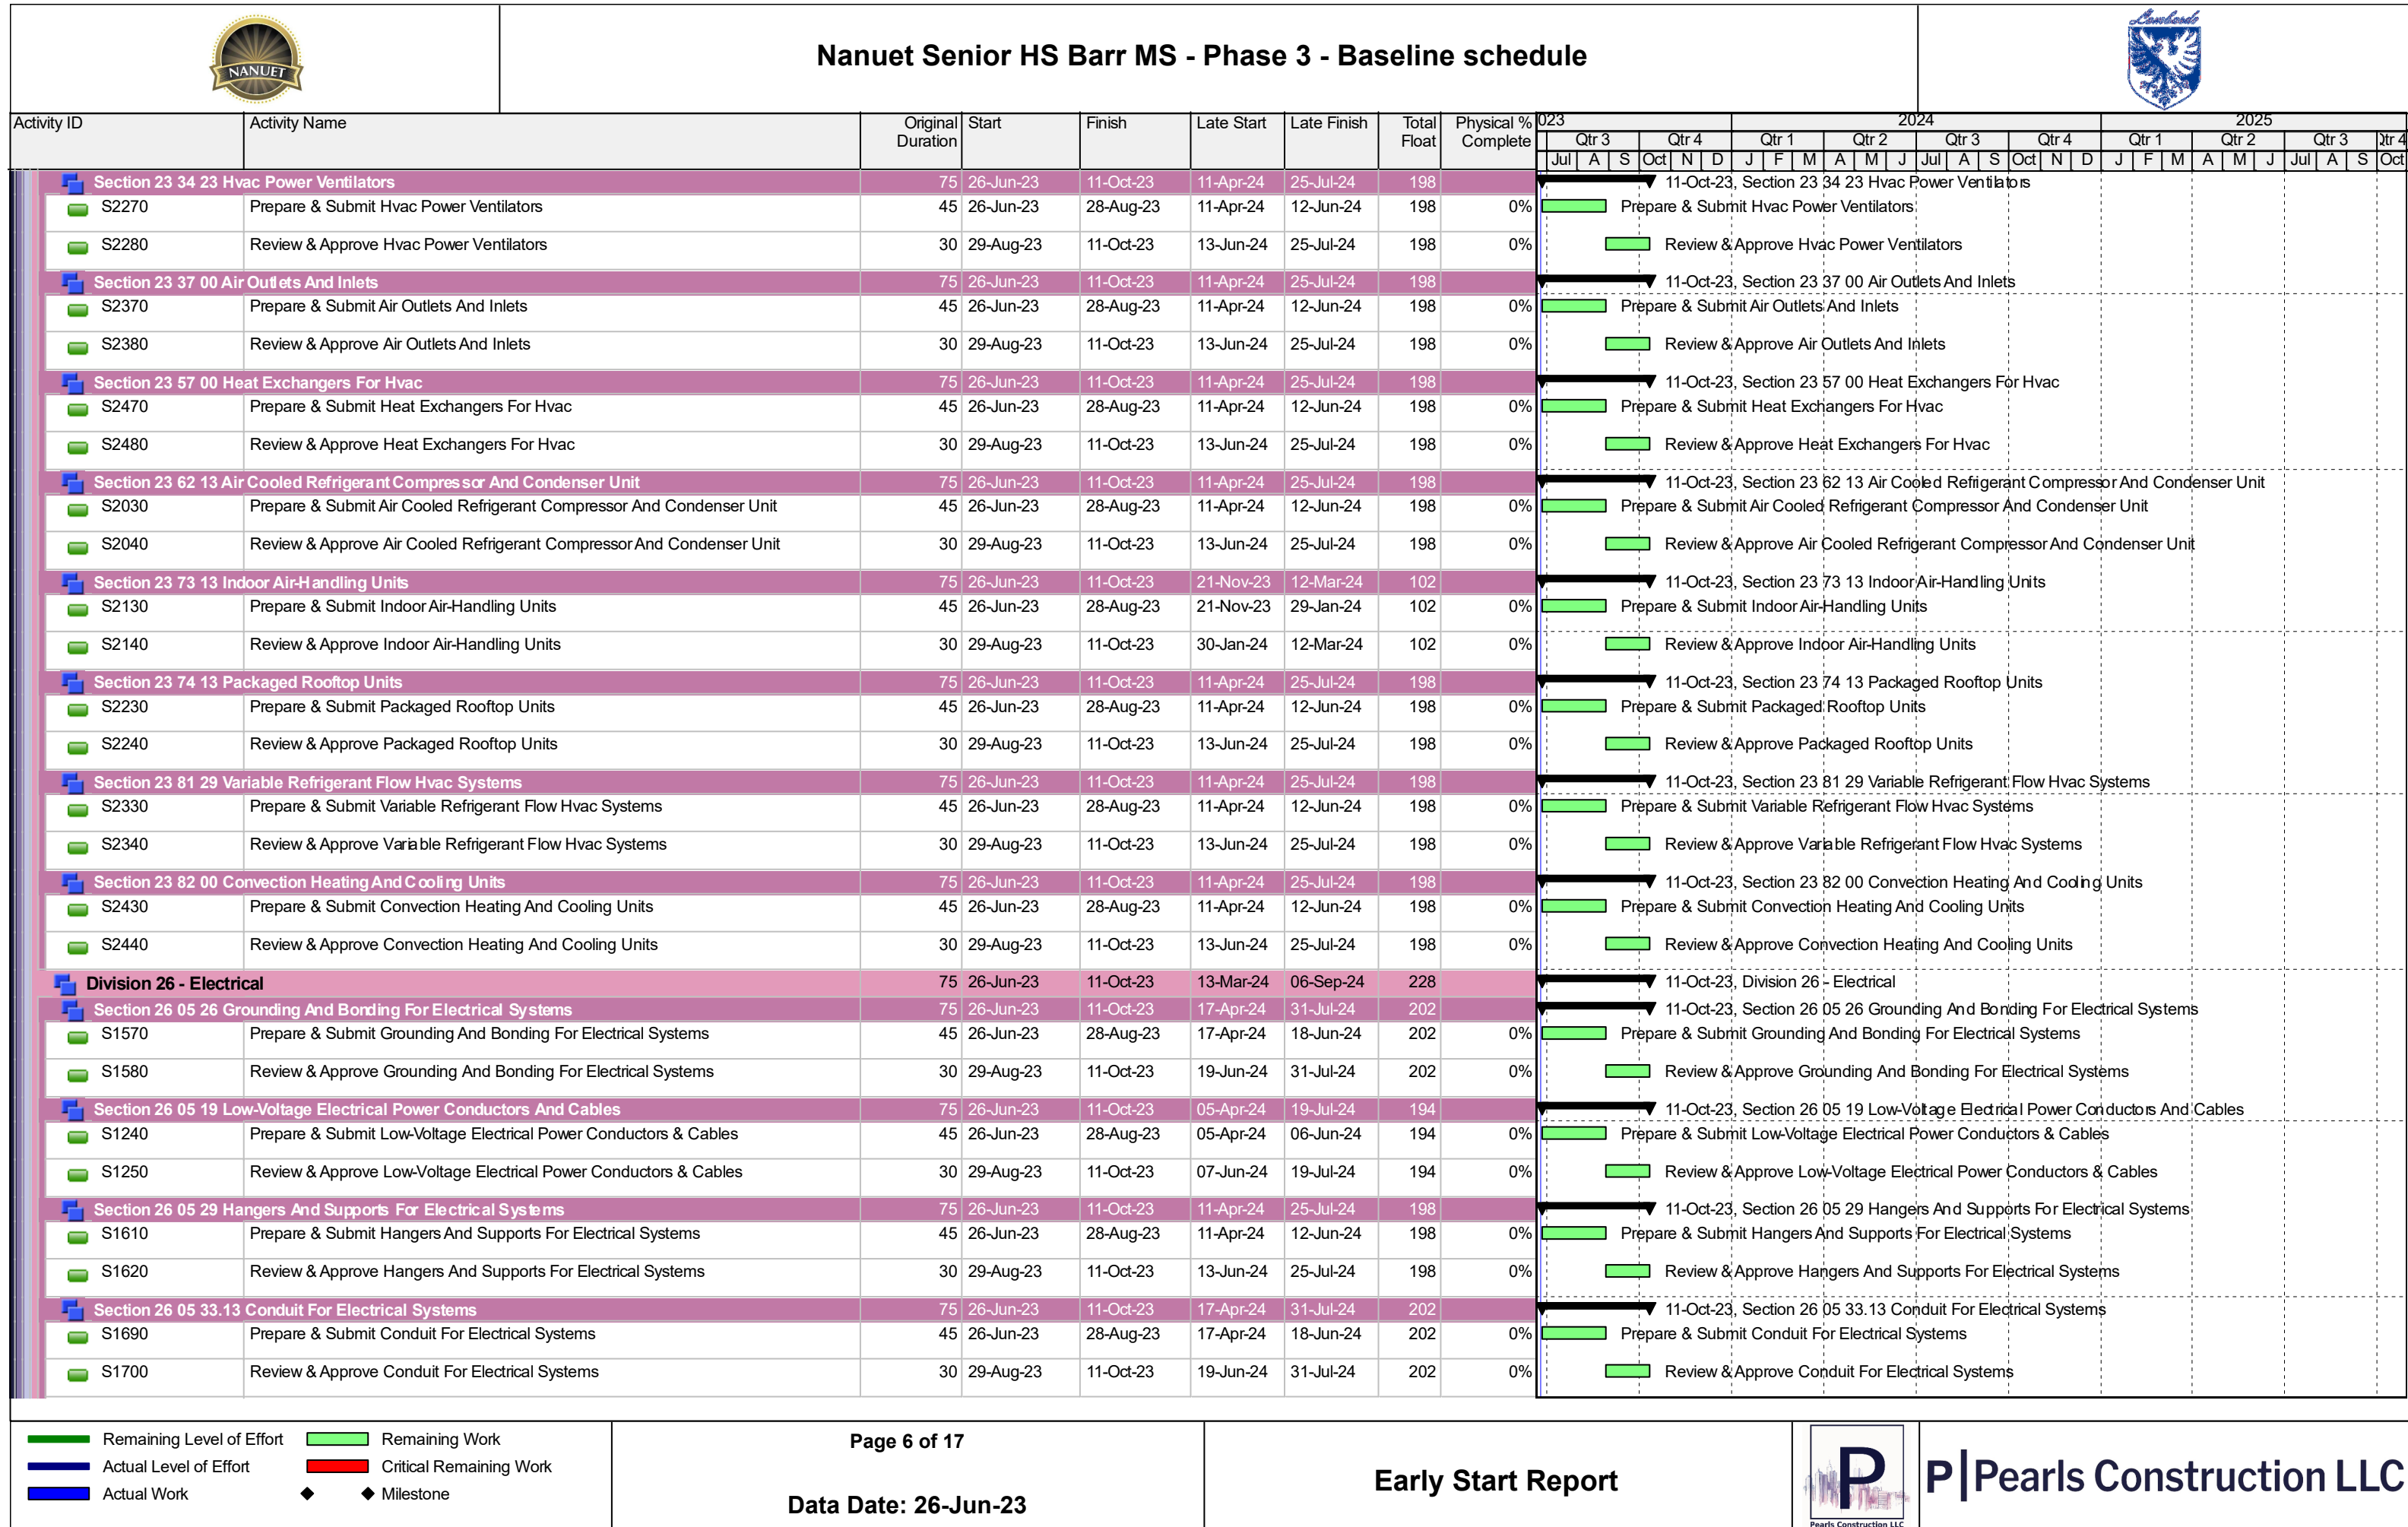

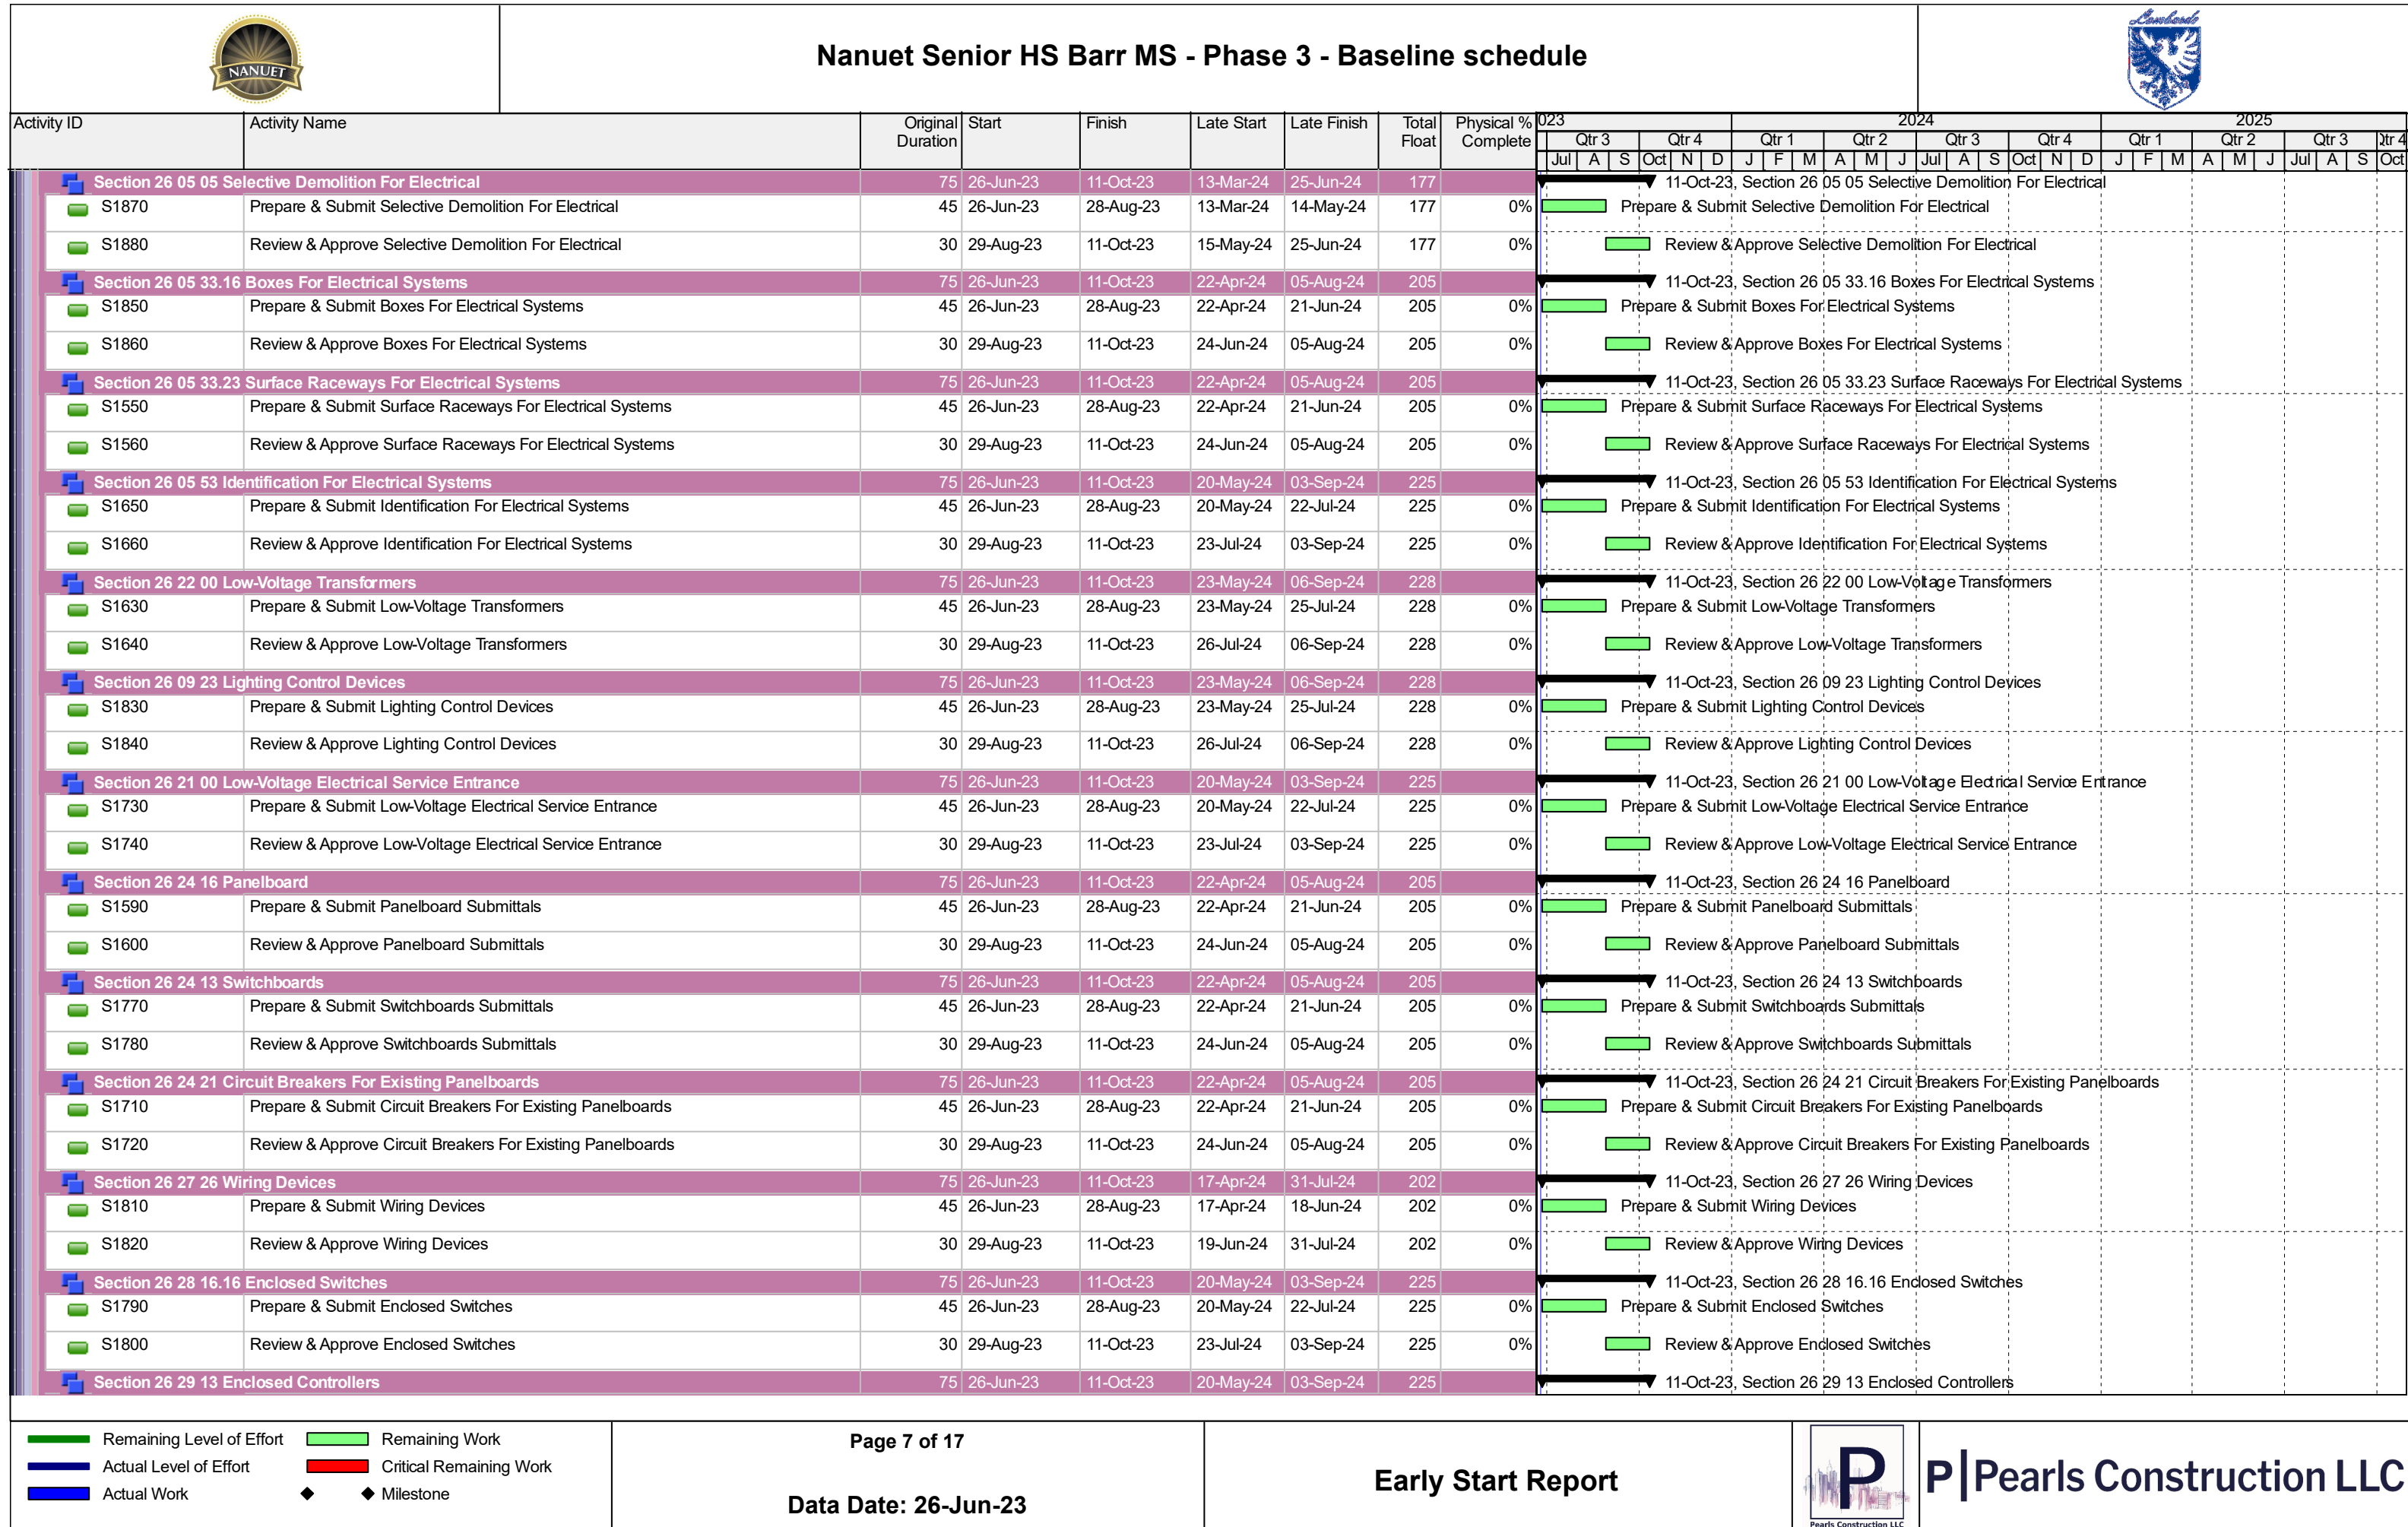



Nanuet Senior HS Barr MS - Phase 3 - Baseline schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	2023			2024												2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
									Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
									Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
	S1750	Prepare & Submit Enclosed Controllers	45	26-Jun-23	28-Aug-23	20-May-24	22-Jul-24	225	0%		Prepare & Submit Enclosed Controllers																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone



Nanuet Senior HS Barr MS - Phase 3 - Baseline schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	023		2024												2025															
									Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4		
									Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct		
S1520	Fabricate & Deliver Flex Hose 6”X 24”	30	12-Oct-23	27-Nov-23	15-Jul-24	23-Aug-24	189	0%																														
S1530	Fabricate & Deliver EXP-HS-2 & 3	80	12-Oct-23	08-Feb-24	03-May-24	23-Aug-24	139	0%																														
S1540	Fabricate & Deliver Flex Hose Exp Loops	30	12-Oct-23	27-Nov-23	15-Jul-24	23-Aug-24	189	0%																														
S3200	Fabricate & Deliver FT-MS-1	35	12-Oct-23	04-Dec-23	12-Jul-24	29-Aug-24	188	0%																														
Construction		167	26-Jan-24	19-Sep-24	03-Jun-24	19-Sep-24	0																															
Mobilization		10	26-Jan-24	08-Feb-24	12-Jun-24	25-Jun-24	97																															
C6920	Mobilization & Site Prep.	10	26-Jan-24	08-Feb-24	12-Jun-24	25-Jun-24	97	0%																														
Nanuet Senior HS		130	18-Mar-24	17-Sep-24	28-Jun-24	17-Sep-24	0																															
Demolition		14	28-Jun-24	18-Jul-24	28-Jun-24	18-Jul-24	0																															
C5910	Remove Spandrel Panels In Existing Storefront Window System - Basement - Nanuet Senior HS	1	28-Jun-24	28-Jun-24	28-Jun-24	28-Jun-24	0	0%																														
C7030	Remove HVAC Ducts & Piping - Nanuet Senior HS	14	28-Jun-24	18-Jul-24	28-Jun-24	18-Jul-24	0	0%																														
C5920	Remove Unit Ventilator - First Floor - Nanuet Senior HS	1	01-Jul-24	01-Jul-24	01-Jul-24	01-Jul-24	0	0%																														
C5950	Remove & Salvage Existing Wainscoting Pipe Enclosure - First Floor - Nanuet Senior HS	1	02-Jul-24	02-Jul-24	02-Jul-24	02-Jul-24	0	0%																														
C5930	Remove Spandrel Panels In Existing Storefront Window System - Second Floor - Nanuet Senior HS	1	03-Jul-24	03-Jul-24	03-Jul-24	03-Jul-24	0	0%																														
Asbestos Abatement Nanuet Senior HS		83	18-Mar-24	11-Jul-24	05-Jul-24	29-Jul-24	12																															
C5830	Perform Asbestos Abatement @ Roof - Nanuet Senior HS	15	18-Mar-24	05-Apr-24	09-Jul-24	29-Jul-24	80	0%																														
C5820	Perform Asbestos Abatement @ Second Floor - Nanuet Senior HS	5	05-Jul-24	11-Jul-24	05-Jul-24	11-Jul-24	0	0%																														
Basement		43	12-Jul-24	11-Sep-24	12-Jul-24	11-Sep-24	0																															
Architectural		43	12-Jul-24	11-Sep-24	12-Jul-24	11-Sep-24	0																															
C6760	Patch Flooring - Basement - Nanuet Senior HS	1	12-Jul-24	12-Jul-24	12-Jul-24	12-Jul-24	0	0%																														
C6930	Layout & Install Ceiling Framing - Basement - Nanuet Senior HS	1	15-Jul-24	15-Jul-24	14-Aug-24	14-Aug-24	22	0%																														
C6790	Priming & First Coat Painting - Basement - Nanuet Senior HS	5	14-Aug-24	20-Aug-24	15-Aug-24	21-Aug-24	1	0%																														
C6860	Install Ceilings - Basement - Nanuet Senior HS	4	14-Aug-24	19-Aug-24	14-Aug-24	19-Aug-24	0	0%																														
C6870	Finish Ceilings - Basement - Nanuet Senior HS	2	20-Aug-24	21-Aug-24	20-Aug-24	21-Aug-24	0	0%																														
C6800	Final Coat Painting - Basement - Nanuet Senior HS	4	22-Aug-24	27-Aug-24	23-Aug-24	28-Aug-24	1	0%																														
C6910	Install Flooring - Basement - Nanuet Senior HS	3	28-Aug-24	30-Aug-24	29-Aug-24	03-Sep-24	1	0%																														
C6830	Install Doors & Hardware - Basement - Nanuet Senior HS	2	03-Sep-24	04-Sep-24	06-Sep-24	09-Sep-24	3	0%																														
C6880	Install Specialities - Basement - Nanuet Senior HS	4	03-Sep-24	06-Sep-24	04-Sep-24	09-Sep-24	1	0%																														
C6840	Final Touch-ups - Basement - Nanuet Senior HS	2	10-Sep-24	11-Sep-24	10-Sep-24	11-Sep-24	0	0%																														
Mechanical		40	15-Jul-24	09-Sep-24	15-Jul-24	09-Sep-24	0																															
C6600	Install Mechanical Ducts & Pipes Hangers - Basement - Nanuet Senior HS	1	15-Jul-24	15-Jul-24	15-Jul-24	15-Jul-24	0	0%																														
C6630	Install Above ceiling Terminal Equipment - Basement - Nanuet Senior HS	4	16-Jul-24	19-Jul-24	16-Jul-24	19-Jul-24	0	0%																														
C6610	Install HVAC Ducts & Pipes - Basement - Nanuet Senior HS	8	19-Jul-24	30-Jul-24	19-Jul-24	30-Jul-24	0	0%																														
C6620	Insulate HVAC Ducts & Pipes - Basement - Nanuet Senior HS	5	31-Jul-24	06-Aug-24	31-Jul-24	06-Aug-24	0	0%																														
C6640	Mechanical Rough-Ins Inspection - Basement - Nanuet Senior HS	2	07-Aug-24	08-Aug-24	07-Aug-24	08-Aug-24	0	0%																														

Remaining Level of Effort


Actual Level of Effort


Actual Work

Remaining Work

Critical Remaining Work


Milestone

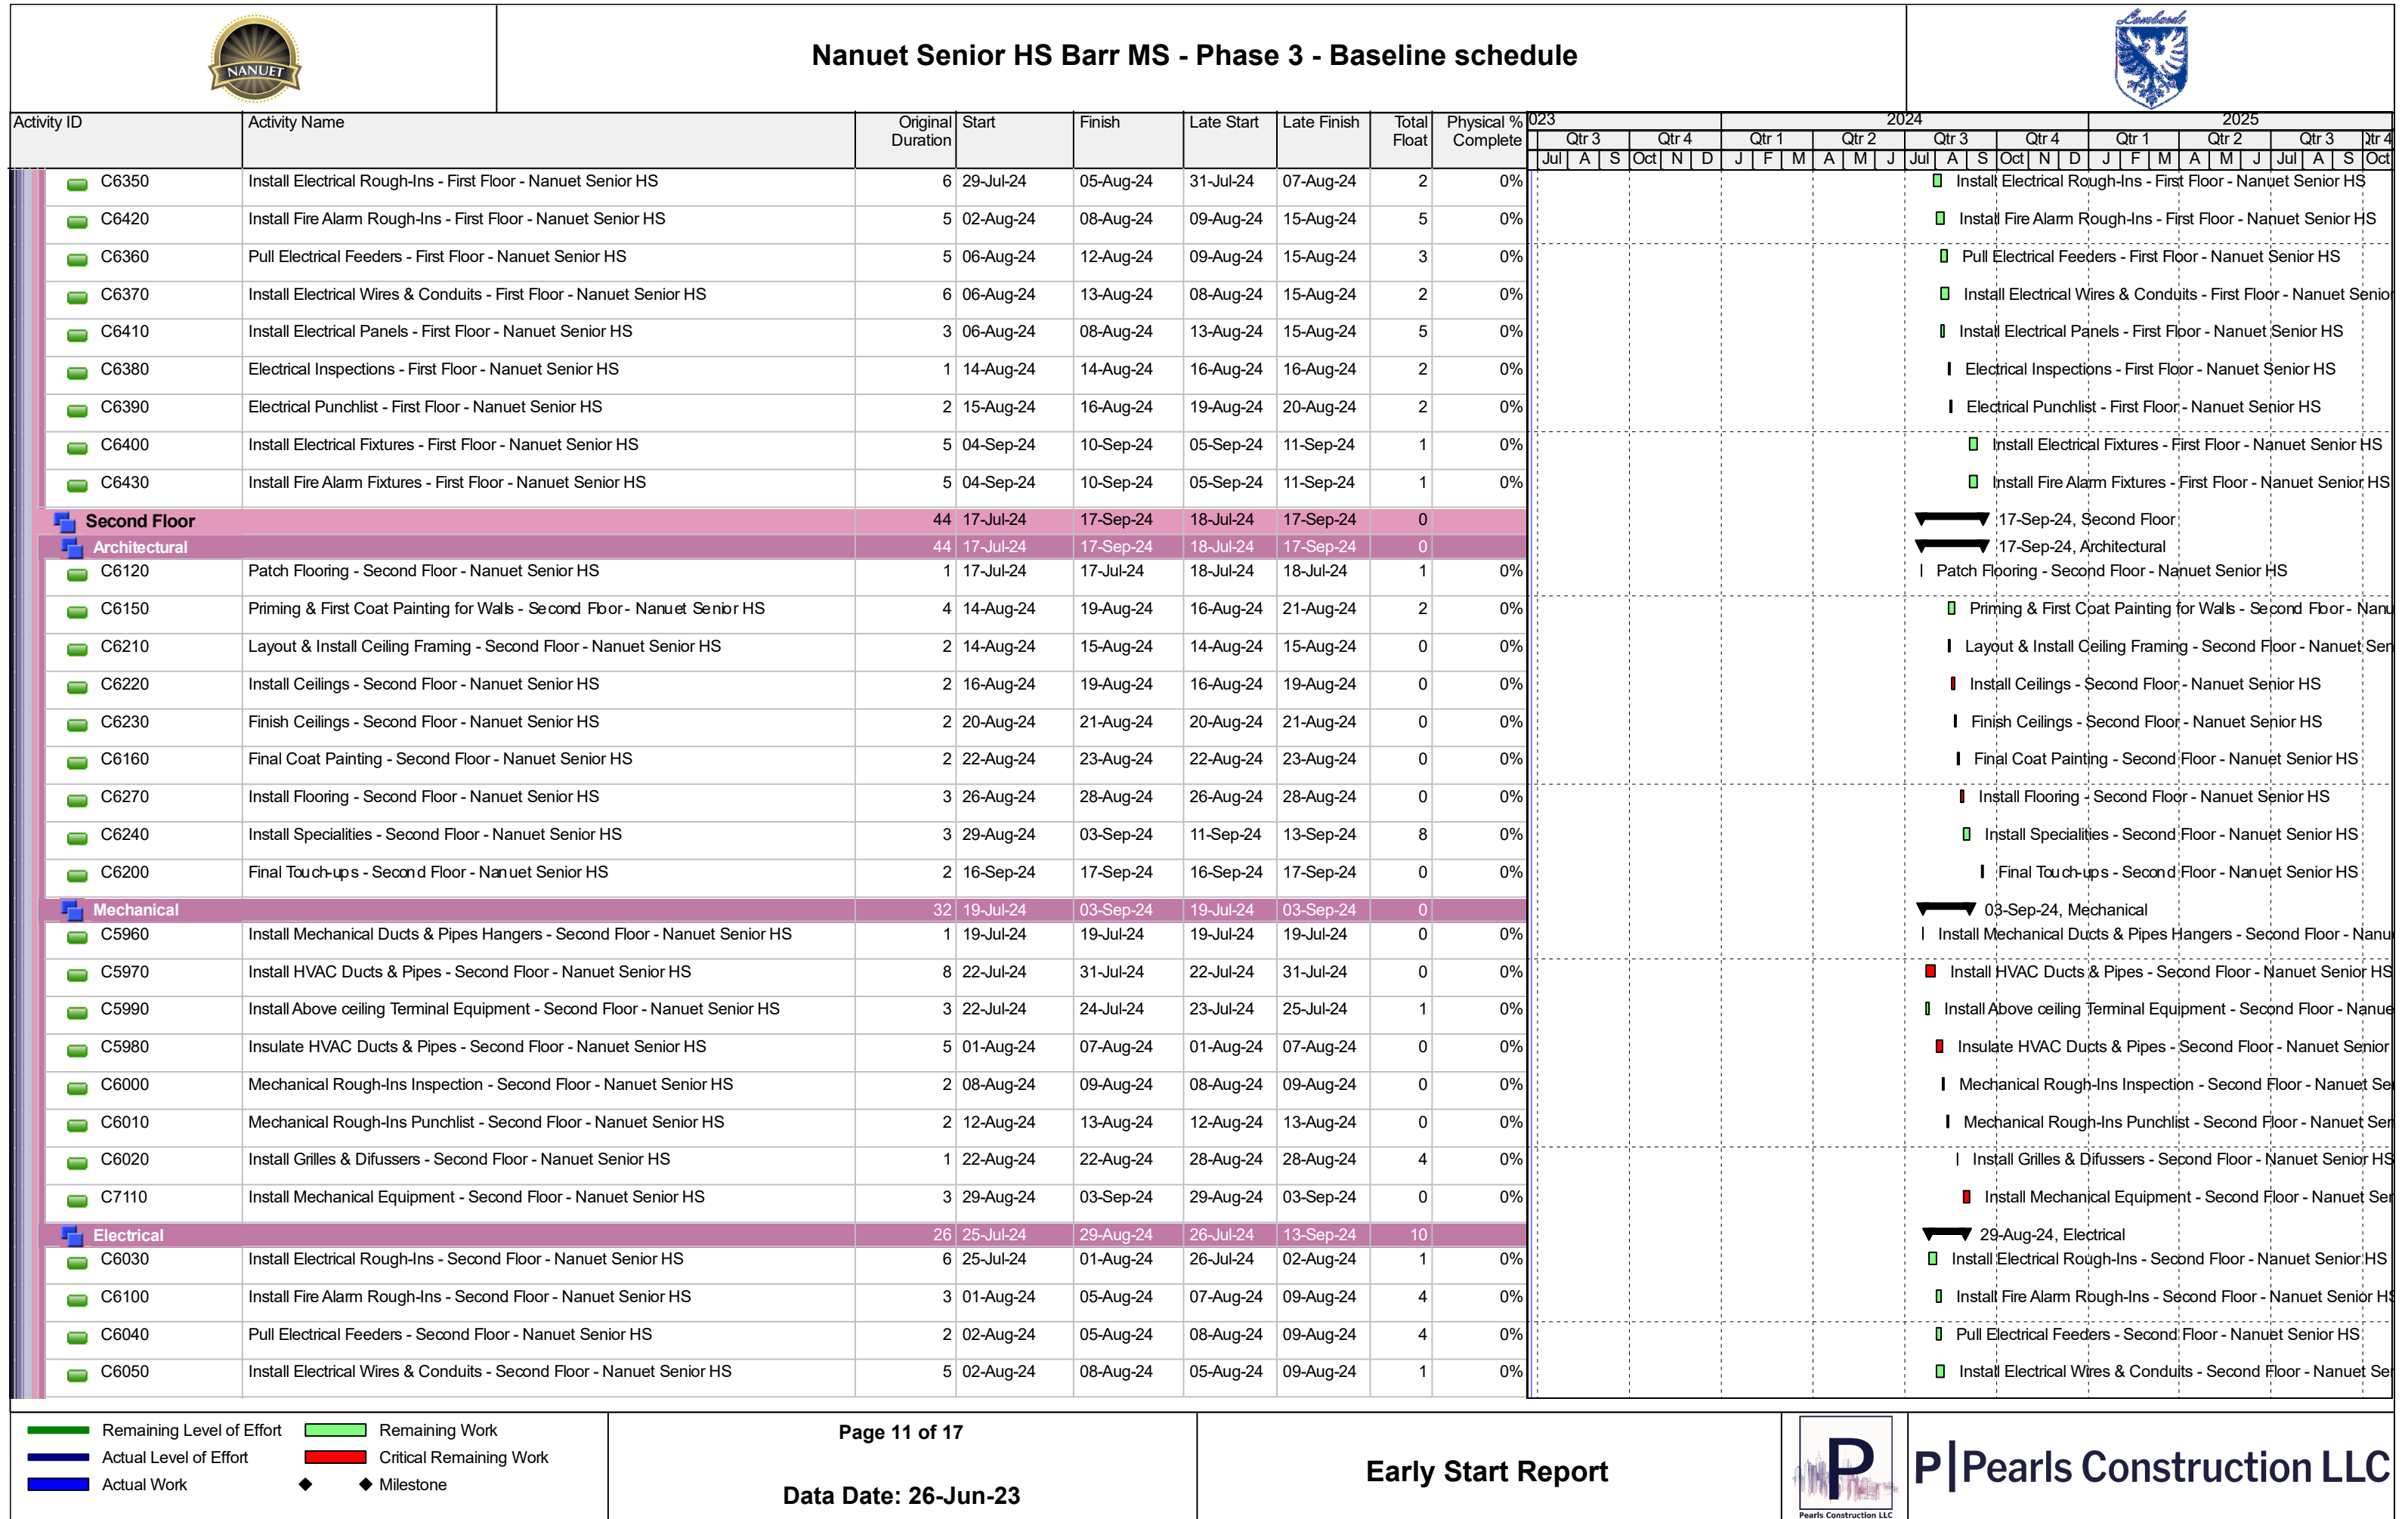


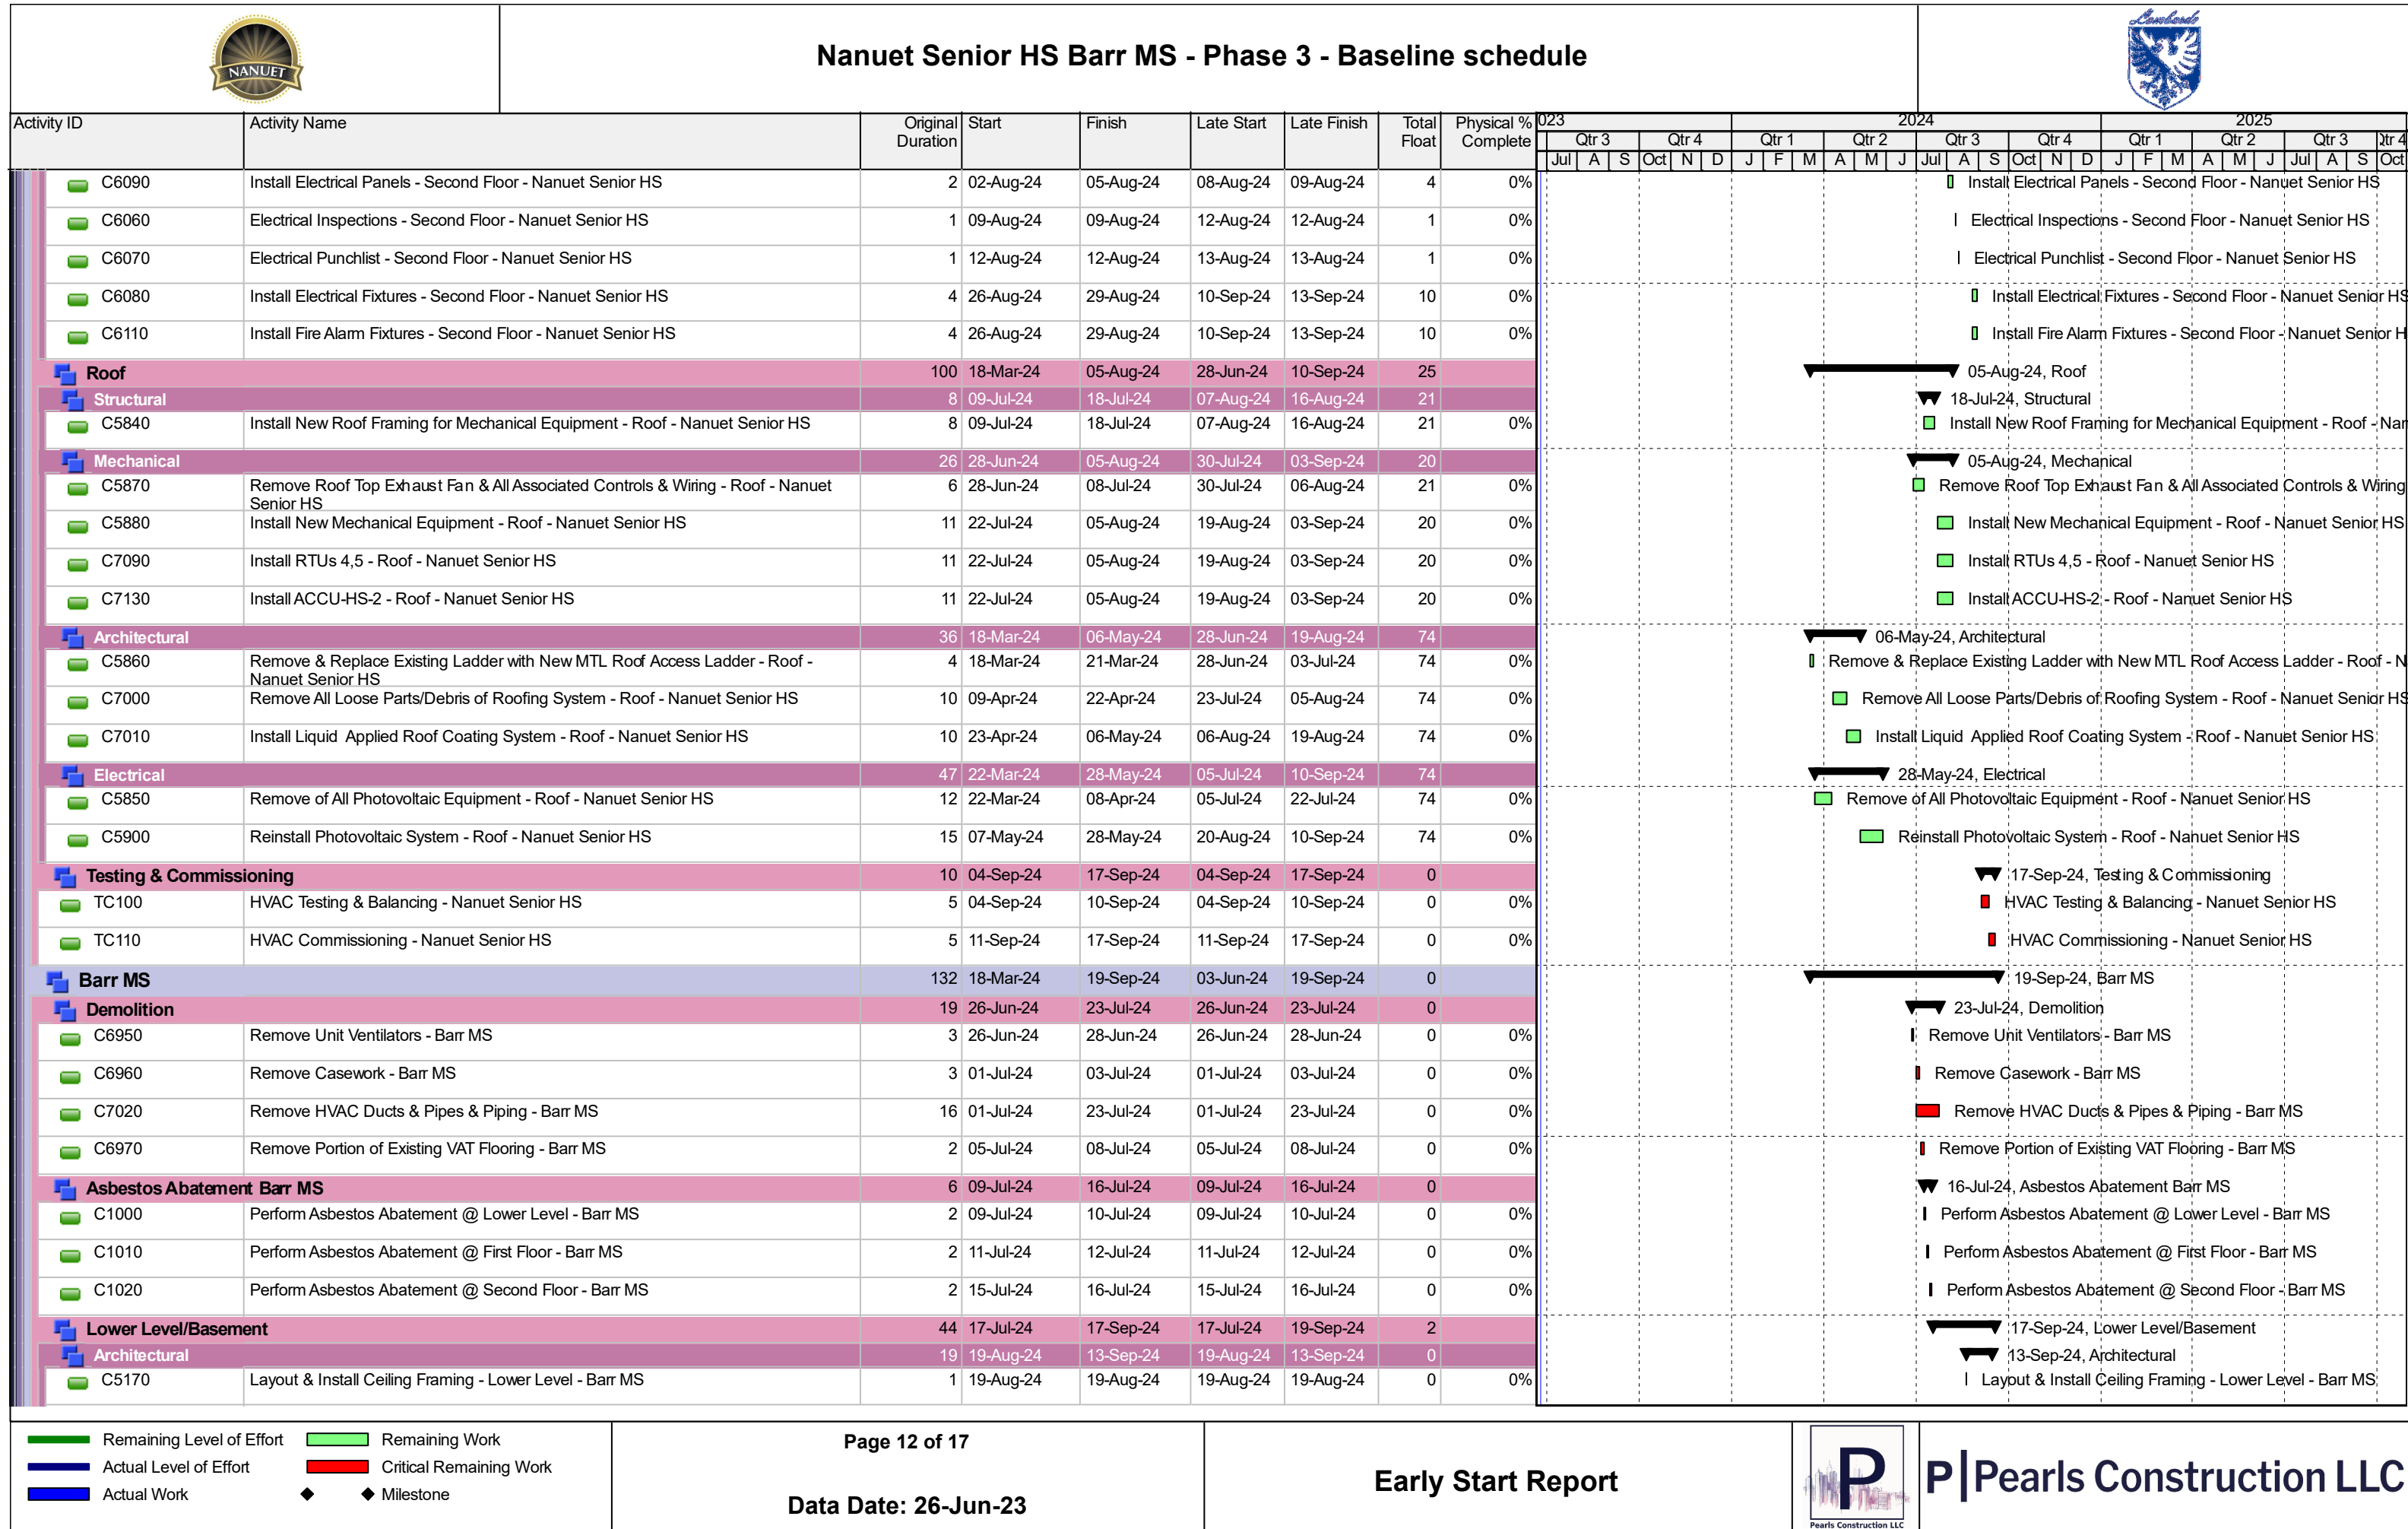




 Remaining Level of Effort  Remaining Work
 Actual Level of Effort  Critical Remaining Work
 Actual Work  Milestone

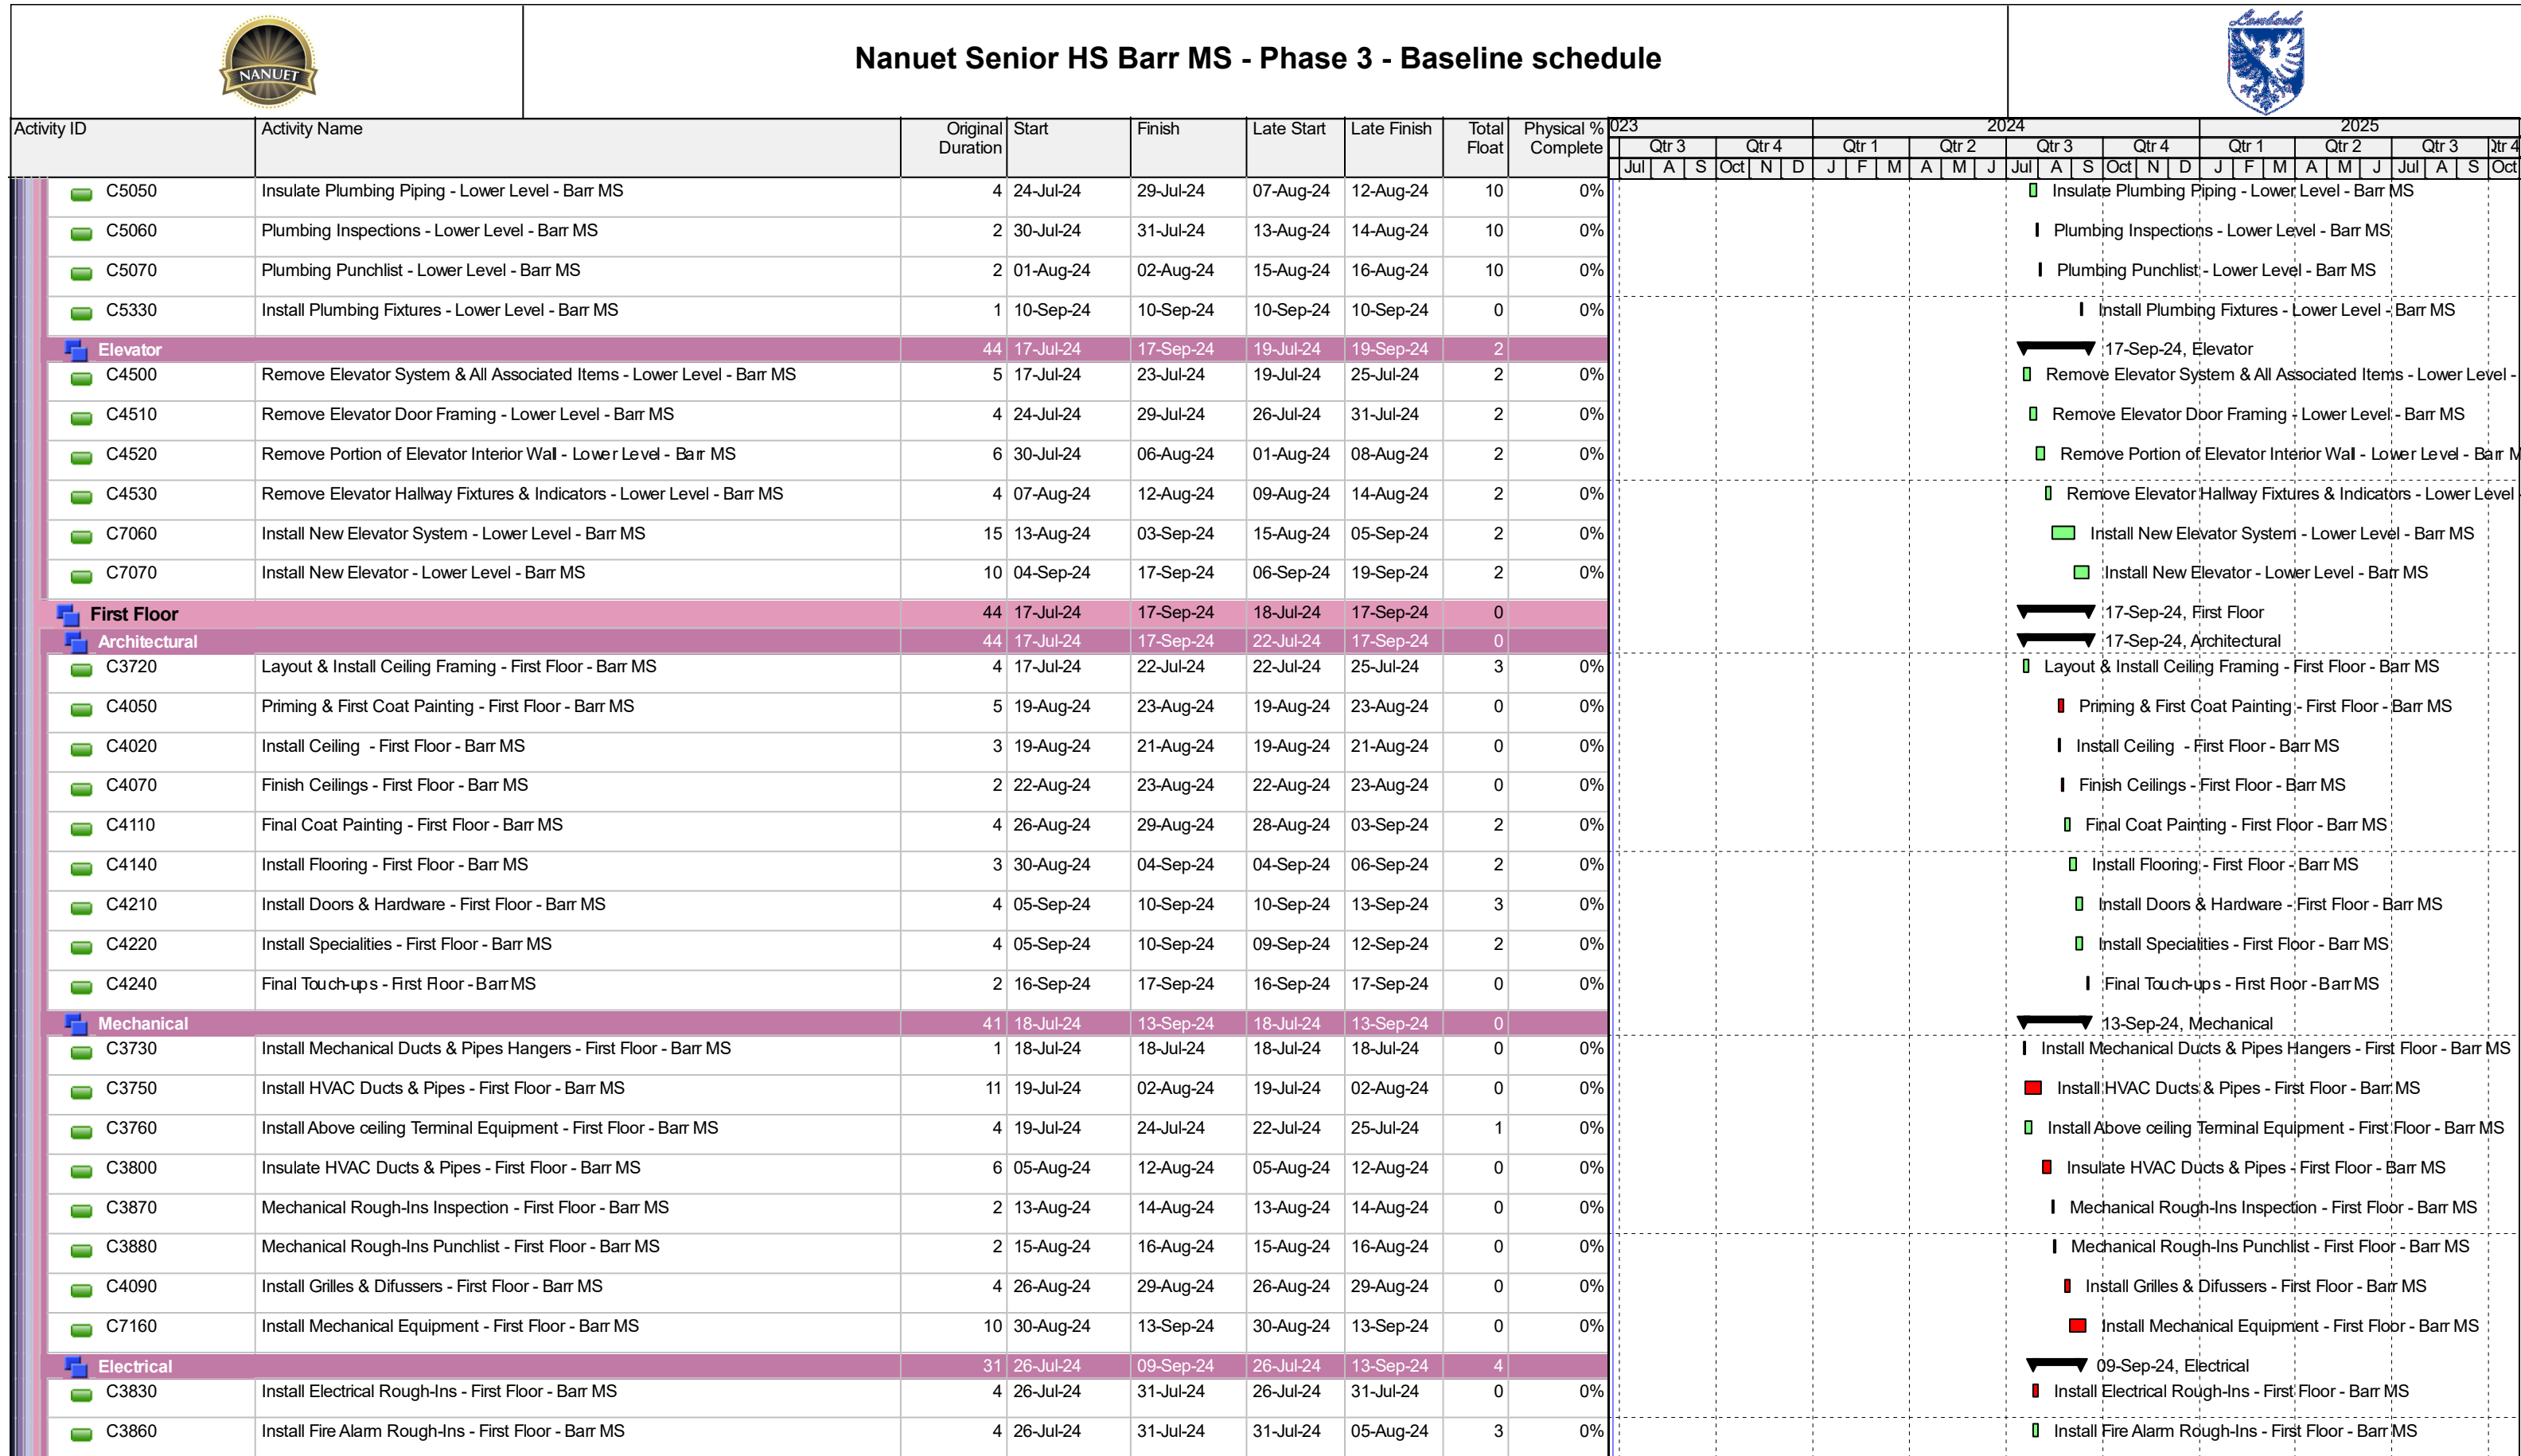

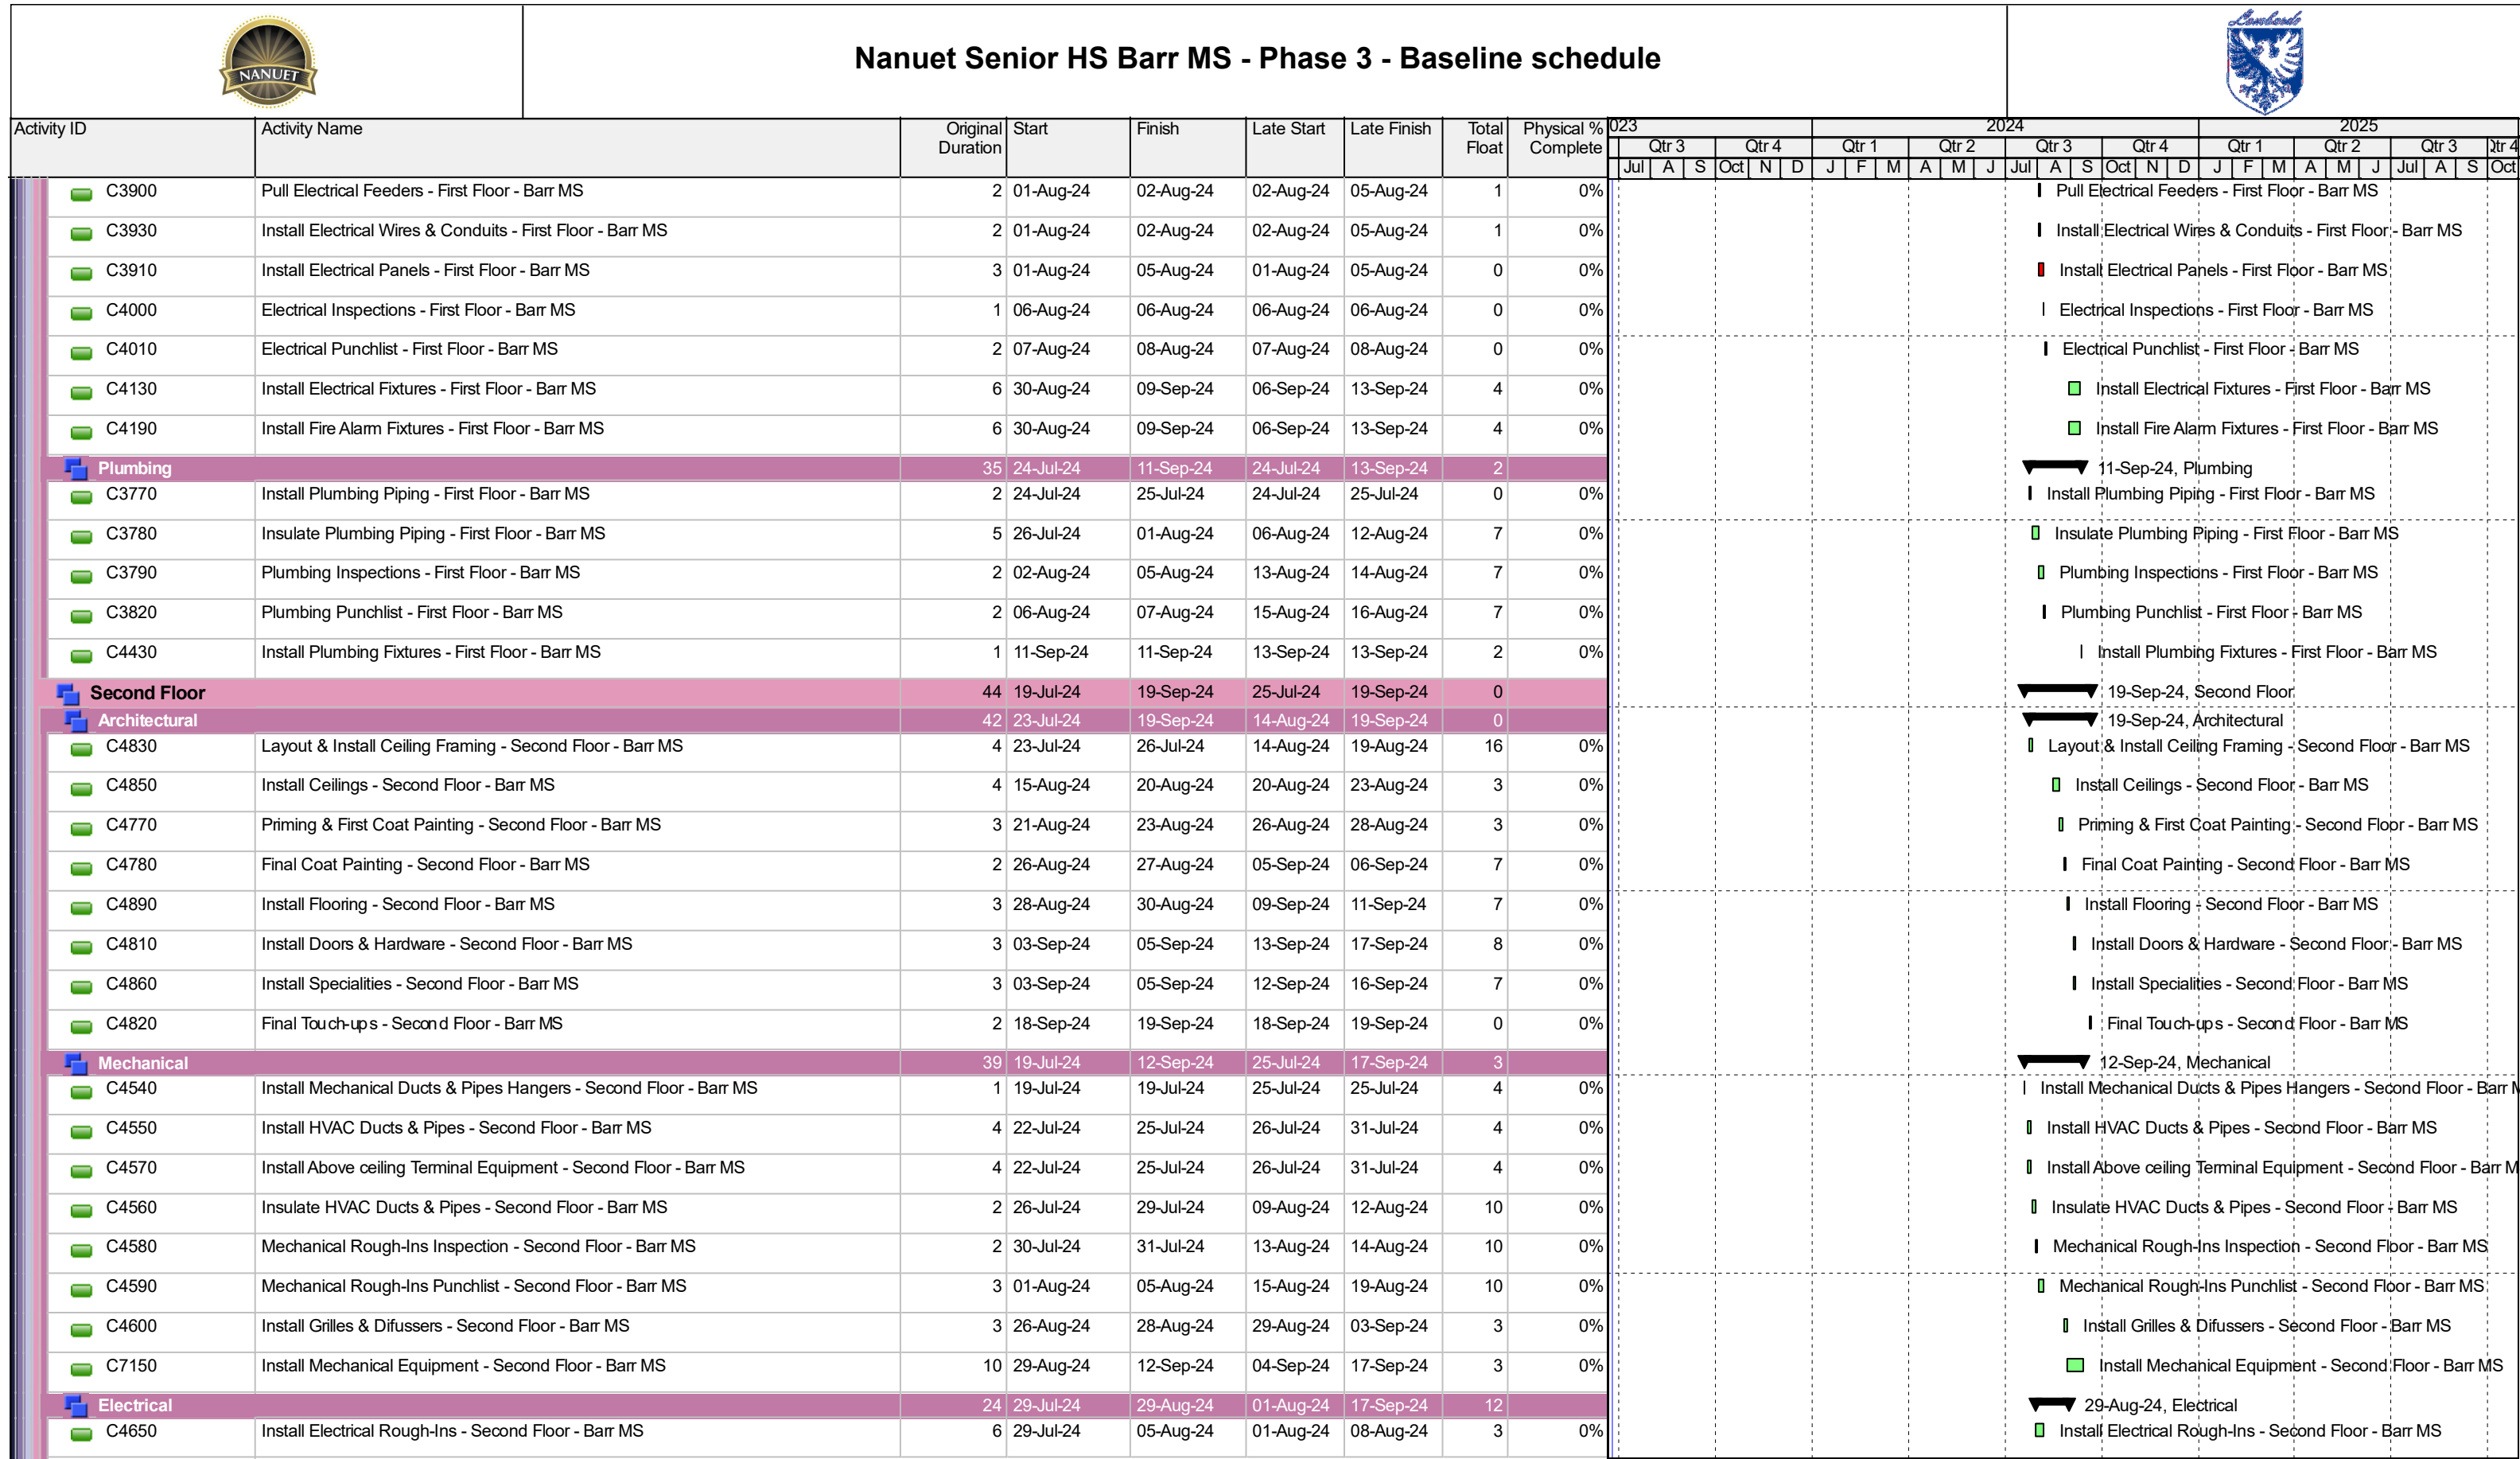

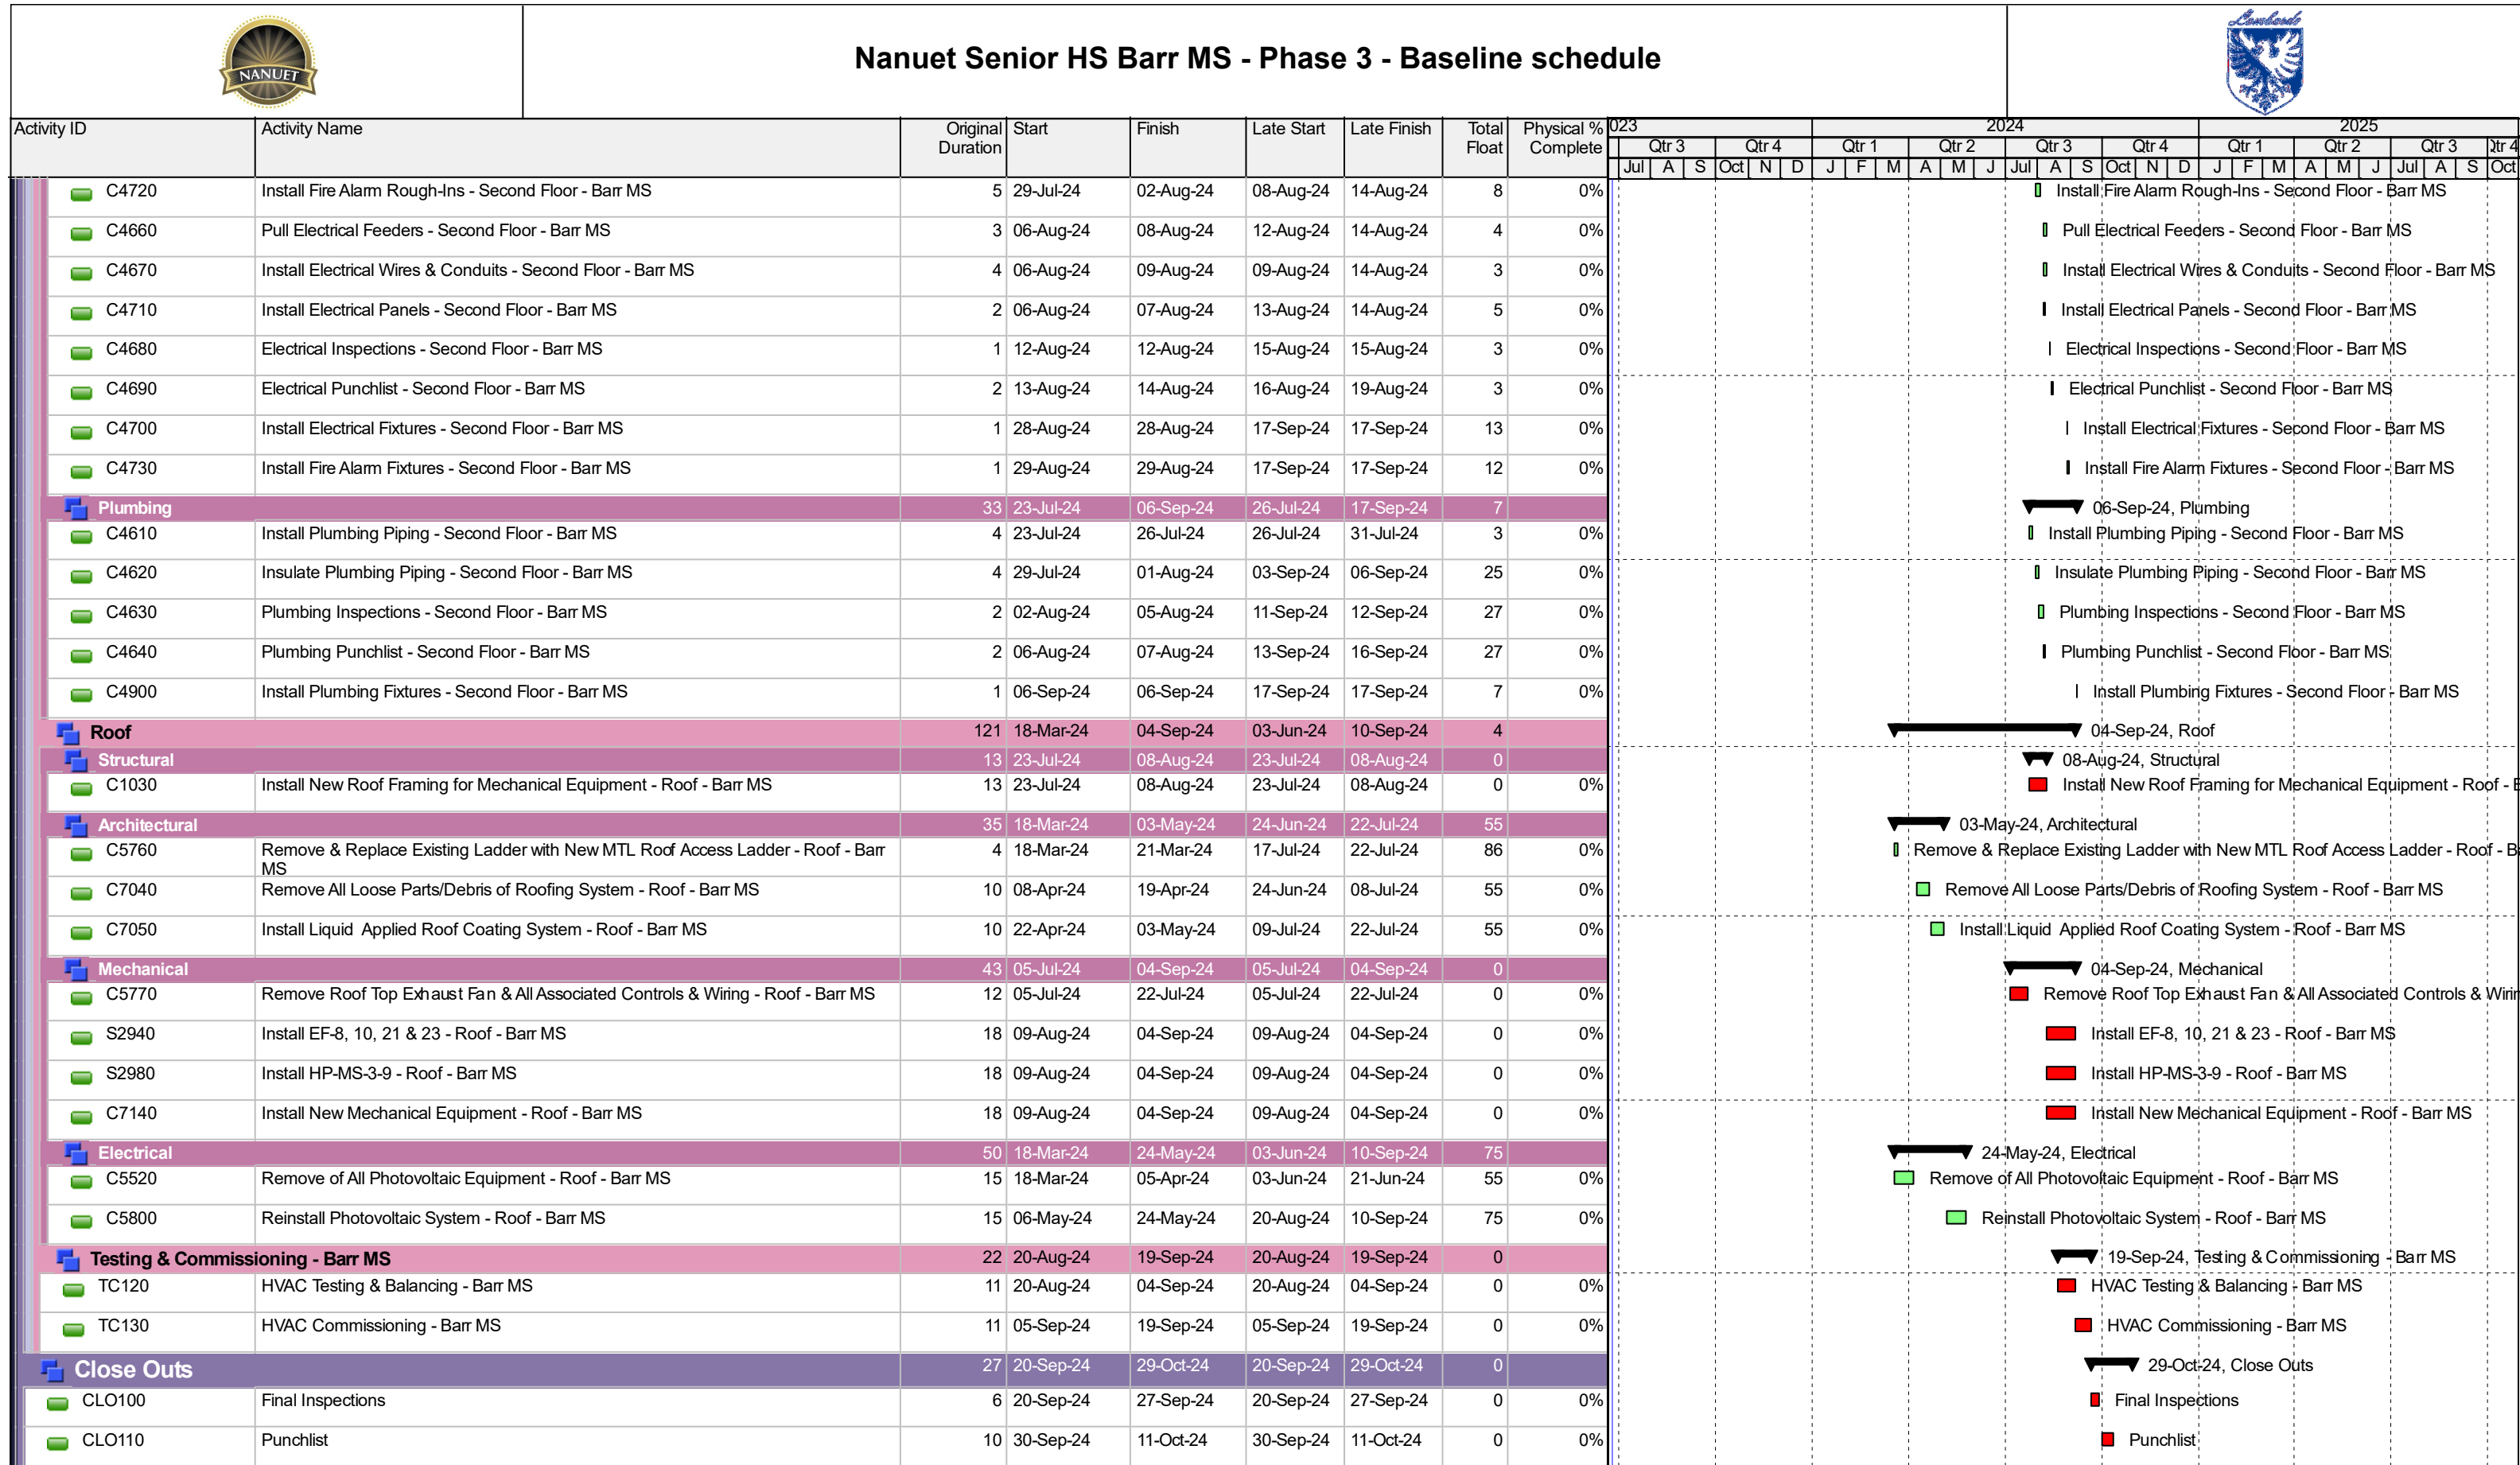



Nanuet Senior HS Barr MS - Phase 3 - Baseline schedule

