

SUBMITTAL COVERSHEET **Nanuet UFSD –Phase 3 Projects**

Architect:
KSQ Architects
215 W 40th Street, 15th Floor
New York, NY 10018

Owner:
Nanuet Union Free School District
101 Church Street
Nanuet, NY 10954

Construction Manager:
Jacobs
One Penn Plaza, 54th floor
New York, NY 10019

Contractor: Joe Lombardo Plumbing & Heating of Rockland Inc

Contract: Ron Lombardo

Address: 321 Spook Rock Road Suite 109A
Suffern, New York 10901

845-357-6537

Telephone:

Fax: 845-357-8529

School Name: Nanuet Union Free School District Phase 3 Bond Projects @ Barr Middle School & Nanuet High School

Type of Submittal:

Re-submittal: ☐ No ☐ Yes

☐ Shop Drawings ☐ Product Data ☐ Schedule ☐ Sample ☐
☐ Test Report ☐ Certificate ☐ Color Sample ☐ Warranty ☐

Submittal Description:

LOMBARDO'S PROJECT MILESTONE SCHEDULE

Product Name:

Manufacturer:

**Subcontractor/
Supplier:**

References:

Spec. Section No.: 011100

Drawing No(s):

Paragraph:

Rm. or Detail No(s):

Architect's/ Engineer's Review Stamp

Contractor Review Statement:

These documents have been checked for accuracy and coordinated with job conditions and Contract requirements by this office and have been found to comply with the provisions of the Contract Documents.

Ronald J. Lombardo

10.5.23

Name:

Date:

Company Name:

Joe Lombardo Plumbing & Heating of Rockland Inc.

Remarks:

Nanuet Senior HS Barr MS - Phase 3 - Baseline schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	2023												2024												2025											
									Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4								
									Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct								
📁 Nanuet Senior HS & Barr MS - Phase 3 - Baseline schedule		352	26-Jun-23	29-Oct-24	18-Sep-23	29-Oct-24	0		29-Oct-24, Nanuet Senior HS & Barr MS - Phase 3																																			
📁 Milestones		492	26-Jun-23	29-Oct-24	18-Sep-23	29-Oct-24	0		29-Oct-24, Milestones																																			
📁 M100	NTP	0	26-Jun-23		18-Sep-23		84	0%	📍 NTP																																			
📁 M150	Milestone 1 Building Envelope Start of Construction	0	18-Mar-24*		18-Mar-24		0	0%	📍 Milestone 1 Building Envelope Start of Construction																																			
📁 M110	Milestone 1 Building Envelope Substantial Completion	0		28-May-24*		10-Sep-24	105	0%	📍 Milestone 1 Building Envelope Substantial Completion																																			
📁 M170	Milestone 3 Barr Senior HS HS Start of Construction	0	26-Jun-24*		26-Jun-24		0	0%	📍 Milestone 3 Barr Senior HS HS Start of Construction																																			
📁 M160	Milestone 2 Nanuet Senior HS Start of Construction	0	28-Jun-24*		28-Jun-24		0	0%	📍 Milestone 2 Nanuet Senior HS Start of Construction																																			
📁 M130	Milestone 2 Nanuet Senior HS Substantial Completion	0		17-Sep-24*		17-Sep-24	0	0%	📍 Milestone 2 Nanuet Senior HS Substantial Completion																																			
📁 M140	Milestone 3 Barr Senior HS Substantial Completion	0		19-Sep-24*		19-Sep-24	0	0%	📍 Milestone 3 Barr Senior HS Substantial Completion																																			
📁 M120	Final Completion	0		29-Oct-24*		29-Oct-24	0	0%	📍 Final Completion																																			
📁 Pre-construction		225	26-Jun-23	17-May-24	18-Sep-23	09-Sep-24	79		17-May-24, Pre-construction																																			
📁 Submittals		95	26-Jun-23	08-Nov-23	18-Sep-23	09-Sep-24	209		➡ 08-Nov-23, Submittals																																			
📁 Division 3 - Concrete		95	26-Jun-23	08-Nov-23	30-Jan-24	11-Jun-24	147		➡ 08-Nov-23, Division 3 - Concrete																																			
📁 Section 03 54 00 - Self-Leveling Toppings		95	26-Jun-23	08-Nov-23	30-Jan-24	11-Jun-24	147		➡ 08-Nov-23, Section 03 54 00 - Self-Leveling Toppings																																			
📁 S1000	Prepare & Submit Self-Leveling Toppings	65	26-Jun-23	26-Sep-23	30-Jan-24	30-Apr-24	147	0%	🟢 Prepare & Submit Self-Leveling Toppings																																			
📁 S1010	Review & Approve Self-Leveling Toppings	30	27-Sep-23	08-Nov-23	01-May-24	11-Jun-24	147	0%	🟢 Review & Approve Self-Leveling Toppings																																			
📁 Division 4 - Masonry		75	26-Jun-23	11-Oct-23	21-Mar-24	03-Jul-24	183		➡ 11-Oct-23, Division 4 - Masonry																																			
📁 Section 04 22 00 - Unit Masonry		75	26-Jun-23	11-Oct-23	21-Mar-24	03-Jul-24	183		➡ 11-Oct-23, Section 04 22 00 - Unit Masonry																																			
📁 S1020	Prepare & Submit Unit Masonry	45	26-Jun-23	28-Aug-23	21-Mar-24	22-May-24	183	0%	🟢 Prepare & Submit Unit Masonry																																			
📁 S1030	Review & Approve Unit Masonry	30	29-Aug-23	11-Oct-23	23-May-24	03-Jul-24	183	0%	🟢 Review & Approve Unit Masonry																																			
📁 Division 5 - Metals		75	26-Jun-23	11-Oct-23	08-Apr-24	22-Jul-24	195		➡ 11-Oct-23, Division 5 - Metals																																			
📁 Section 05 12 00 - Structural Steel		75	26-Jun-23	11-Oct-23	08-Apr-24	22-Jul-24	195		➡ 11-Oct-23, Section 05 12 00 - Structural Steel																																			
📁 S1040	Prepare & Submit Structural Steel	45	26-Jun-23	28-Aug-23	08-Apr-24	07-Jun-24	195	0%	🟢 Prepare & Submit Structural Steel																																			
📁 S1050	Review & Approve Structural Steel	30	29-Aug-23	11-Oct-23	10-Jun-24	22-Jul-24	195	0%	🟢 Review & Approve Structural Steel																																			
📁 Section 05 50 00 - Metal Fabrications		75	26-Jun-23	11-Oct-23	08-Apr-24	22-Jul-24	195		➡ 11-Oct-23, Section 05 50 00 - Metal Fabrications																																			
📁 S1060	Prepare & Submit Metal Fabrications	45	26-Jun-23	28-Aug-23	08-Apr-24	07-Jun-24	195	0%	🟢 Prepare & Submit Metal Fabrications																																			
📁 S1070	Review & Approve Metal Fabrications	30	29-Aug-23	11-Oct-23	10-Jun-24	22-Jul-24	195	0%	🟢 Review & Approve Metal Fabrications																																			
📁 Division 6 - Woods And Plastics		75	26-Jun-23	11-Oct-23	30-Apr-24	13-Aug-24	211		➡ 11-Oct-23, Division 6 - Woods And Plastics																																			
📁 Section 06 10 00 - Rough Carpentry		75	26-Jun-23	11-Oct-23	30-Apr-24	13-Aug-24	211		➡ 11-Oct-23, Section 06 10 00 - Rough Carpentry																																			
📁 S1080	Prepare & Submit Rough Carpentry	45	26-Jun-23	28-Aug-23	30-Apr-24	01-Jul-24	211	0%	🟢 Prepare & Submit Rough Carpentry																																			
📁 S1090	Review & Approve Rough Carpentry	30	29-Aug-23	11-Oct-23	02-Jul-24	13-Aug-24	211	0%	🟢 Review & Approve Rough Carpentry																																			
📁 Section 06 40 23 - Interior Architectural Woodwork		75	26-Jun-23	11-Oct-23	30-Apr-24	13-Aug-24	211		➡ 11-Oct-23, Section 06 40 23 - Interior Architectural Woodwork																																			
📁 S1280	Prepare & Submit Interior Architectural Woodwork	45	26-Jun-23	28-Aug-23	30-Apr-24	01-Jul-24	211	0%	🟢 Prepare & Submit Interior Architectural Woodwork																																			
📁 S1290	Review & Approve Interior Architectural Woodwork	30	29-Aug-23	11-Oct-23	02-Jul-24	13-Aug-24	211	0%	🟢 Review & Approve Interior Architectural Woodwork																																			
📁 Division 7 - Thermal And Moisture Protection		75	26-Jun-23	11-Oct-23	23-Apr-24	16-Aug-24	214		➡ 11-Oct-23, Division 7 - Thermal And Moisture Protection																																			
📁 Section 07 01 50.16 Maintenance Cleaning Of Membrane Roofing		55	26-Jun-23	12-Sep-23	13-May-24	29-Jul-24	220		➡ 12-Sep-23, Section 07 01 50.16 Maintenance Cleaning Of Membrane Roofing																																			
📁 S2650	Prepare & Submit Maintenance Cleaning Of Membrane Roofing	45	26-Jun-23	28-Aug-23	13-May-24	15-Jul-24	220	0%	🟢 Prepare & Submit Maintenance Cleaning Of Membrane Roofing																																			

 Remaining Level of Effort  Remaining Work
 Actual Level of Effort  Critical Remaining Work
 Actual Work  Milestone

Page 1 of 17

Data Date: 26-Jun-23

Early Start Report



P | Pearls Construction LLC

Nanuet Senior HS Barr MS - Phase 3 - Baseline schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	2023												2024												2025											
									Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4								
									Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct								
 S2660	Review & Approve Maintenance Cleaning Of Membrane Roofing	10	29-Aug-23	12-Sep-23	16-Jul-24	29-Jul-24	220	0%		Review & Approve Maintenance Cleaning Of Membrane Roofing																																		
 Section 07 01 50.72 Rehabilitation Of Built-Up Roofing		75	26-Jun-23	11-Oct-23	23-Apr-24	06-Aug-24	206			11-Oct-23, Section 07 01 50.72 Rehabilitation Of Built-Up Roofing																																		
 S2590	Prepare & Submit Rehabilitation Of Built-Up Roofing	45	26-Jun-23	28-Aug-23	23-Apr-24	24-Jun-24	206	0%		Prepare & Submit Rehabilitation Of Built-Up Roofing																																		
 S2600	Review & Approve Rehabilitation Of Built-Up Roofing	30	29-Aug-23	11-Oct-23	25-Jun-24	06-Aug-24	206	0%		Review & Approve Rehabilitation Of Built-Up Roofing																																		
 Section 07 01 50.73 Rehabilitation Of Modified Bituminous Roofing		75	26-Jun-23	11-Oct-23	23-Apr-24	06-Aug-24	206			11-Oct-23, Section 07 01 50.73 Rehabilitation Of Modified Bituminous Roofing																																		
 S2630	Prepare & Submit Rehabilitation Of Modified Bituminous Roofing	45	26-Jun-23	28-Aug-23	23-Apr-24	24-Jun-24	206	0%		Prepare & Submit Rehabilitation Of Modified Bituminous Roofing																																		
 S2640	Review & Approve Rehabilitation Of Modified Bituminous Roofing	30	29-Aug-23	11-Oct-23	25-Jun-24	06-Aug-24	206	0%		Review & Approve Rehabilitation Of Modified Bituminous Roofing																																		
 Section 07 13 26 Self-Adhering Sheet Waterproofing		75	26-Jun-23	11-Oct-23	23-Apr-24	06-Aug-24	206			11-Oct-23, Section 07 13 26 Self-Adhering Sheet Waterproofing																																		
 S2670	Prepare & Submit Self-Adhering Sheet Waterproofing	45	26-Jun-23	28-Aug-23	23-Apr-24	24-Jun-24	206	0%		Prepare & Submit Self-Adhering Sheet Waterproofing																																		
 S2680	Review & Approve Self-Adhering Sheet Waterproofing	30	29-Aug-23	11-Oct-23	25-Jun-24	06-Aug-24	206	0%		Review & Approve Self-Adhering Sheet Waterproofing																																		
 Section 07 56 00.13 Fluid-Applied Membrane Roofing, Insulated For New Roofs		75	26-Jun-23	11-Oct-23	23-Apr-24	06-Aug-24	206			11-Oct-23, Section 07 56 00.13 Fluid-Applied Membrane Roofing, Insulated For New Roofs																																		
 S1100	Prepare & Submit Fluid-Applied Membrane Roofing, Insulated For New Roofs	45	26-Jun-23	28-Aug-23	23-Apr-24	24-Jun-24	206	0%		Prepare & Submit Fluid-Applied Membrane Roofing, Insulated For New Roofs																																		
 S1110	Review & Approve Fluid-Applied Membrane Roofing, Insulated For New Roofs	30	29-Aug-23	11-Oct-23	25-Jun-24	06-Aug-24	206	0%		Review & Approve Fluid-Applied Membrane Roofing, Insulated For New Roofs																																		
 Section 07 62 00 Sheet Metal Flashing And Trim		75	26-Jun-23	11-Oct-23	23-Apr-24	06-Aug-24	206			11-Oct-23, Section 07 62 00 Sheet Metal Flashing And Trim																																		
 S2570	Prepare & Submit Sheet Metal Flashing And Trim	45	26-Jun-23	28-Aug-23	23-Apr-24	24-Jun-24	206	0%		Prepare & Submit Sheet Metal Flashing And Trim																																		
 S2580	Review & Approve Sheet Metal Flashing And Trim	30	29-Aug-23	11-Oct-23	25-Jun-24	06-Aug-24	206	0%		Review & Approve Sheet Metal Flashing And Trim																																		
 Section 07 71 00 Roof Specialties		75	26-Jun-23	11-Oct-23	03-May-24	16-Aug-24	214			11-Oct-23, Section 07 71 00 Roof Specialties																																		
 S2610	Prepare & Submit Roof Specialties	45	26-Jun-23	28-Aug-23	03-May-24	05-Jul-24	214	0%		Prepare & Submit Roof Specialties																																		
 S2620	Review & Approve Roof Specialties	30	29-Aug-23	11-Oct-23	08-Jul-24	16-Aug-24	214	0%		Review & Approve Roof Specialties																																		
 Section 07 84 13 Penetration Firestopping		75	26-Jun-23	11-Oct-23	03-May-24	16-Aug-24	214			11-Oct-23, Section 07 84 13 Penetration Firestopping																																		
 S2550	Prepare & Submit Penetration Firestopping	45	26-Jun-23	28-Aug-23	03-May-24	05-Jul-24	214	0%		Prepare & Submit Penetration Firestopping																																		
 S2560	Review & Approve Penetration Firestopping	30	29-Aug-23	11-Oct-23	08-Jul-24	16-Aug-24	214	0%		Review & Approve Penetration Firestopping																																		
 Division 8		75	26-Jun-23	11-Oct-23	23-Apr-24	05-Sep-24	227			11-Oct-23, Division 8																																		
 Section 08 11 13 Hollow Metal Doors And Frames		75	26-Jun-23	11-Oct-23	23-Apr-24	06-Aug-24	206			11-Oct-23, Section 08 11 13 Hollow Metal Doors And Frames																																		
 S2890	Prepare & Submit Hollow Metal Doors And Frames	45	26-Jun-23	28-Aug-23	23-Apr-24	24-Jun-24	206	0%		Prepare & Submit Hollow Metal Doors And Frames																																		
 S2900	Review & Approve Hollow Metal Doors And Frames	30	29-Aug-23	11-Oct-23	25-Jun-24	06-Aug-24	206	0%		Review & Approve Hollow Metal Doors And Frames																																		
 Section 08 14 16 Flush Wood Doors		75	26-Jun-23	11-Oct-23	22-May-24	05-Sep-24	227			11-Oct-23, Section 08 14 16 Flush Wood Doors																																		
 S2850	Prepare & Submit Flush Wood Doors	45	26-Jun-23	28-Aug-23	22-May-24	24-Jul-24	227	0%		Prepare & Submit Flush Wood Doors																																		
 S2860	Review & Approve Flush Wood Doors	30	29-Aug-23	11-Oct-23	25-Jul-24	05-Sep-24	227	0%		Review & Approve Flush Wood Doors																																		
 Section 08 41 13 Aluminum Framed Entrances And Storefronts		75	26-Jun-23	11-Oct-23	22-May-24	05-Sep-24	227			11-Oct-23, Section 08 41 13 Aluminum Framed Entrances And Storefronts																																		
 S2870	Prepare & Submit Aluminum Framed Entrances And Storefronts	45	26-Jun-23	28-Aug-23	22-May-24	24-Jul-24	227	0%		Prepare & Submit Aluminum Framed Entrances And Storefronts																																		
 S2880	Review & Approve Aluminum Framed Entrances And Storefronts	30	29-Aug-23	11-Oct-23	25-Jul-24	05-Sep-24	227	0%		Review & Approve Aluminum Framed Entrances And Storefronts																																		
 Section 08 71 00 Door Hardware		75	26-Jun-23	11-Oct-23	22-May-24	05-Sep-24	227			11-Oct-23, Section 08 71 00 Door Hardware																																		
 S2910	Prepare & Submit Door Hardware	45	26-Jun-23	28-Aug-23	22-May-24	24-Jul-24	227	0%		Prepare & Submit Door Hardware																																		
 S2920	Review & Approve Door Hardware	30	29-Aug-23	11-Oct-23	25-Jul-24	05-Sep-24	227	0%		Review & Approve Door Hardware																																		
 Division 9		75	26-Jun-23	11-Oct-23	30-Apr-24	03-Sep-24	225			11-Oct-23, Division 9																																		
 Section 09 22 16 Non-Structural Metal Framing		75	26-Jun-23	11-Oct-23	30-Apr-24	13-Aug-24	211			11-Oct-23, Section 09 22 16 Non-Structural Metal Framing																																		

 Remaining Level of Effort  Remaining Work
 Actual Level of Effort  Critical Remaining Work
 Actual Work  Milestone





Nanuet Senior HS Barr MS - Phase 3 - Baseline schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	2023							2024								2025													
									Qtr 3			Qtr 4				Qtr 1			Qtr 2		Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4	
									Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	
 S2810	Prepare & Submit Non-Structural Metal Framing	45	26-Jun-23	28-Aug-23	30-Apr-24	01-Jul-24	211	0%		Prepare & Submit Non-Structural Metal Framing																											
 S2820	Review & Approve Non-Structural Metal Framing	30	29-Aug-23	11-Oct-23	02-Jul-24	13-Aug-24	211	0%		Review & Approve Non-Structural Metal Framing																											
Section 09 29 00 Gypsum Board		75	26-Jun-23	11-Oct-23	30-Apr-24	13-Aug-24	211			11-Oct-23, Section 09 29 00 Gypsum Board																											
 S2750	Prepare & Submit Gypsum Board	45	26-Jun-23	28-Aug-23	30-Apr-24	01-Jul-24	211	0%		Prepare & Submit Gypsum Board																											
 S2760	Review & Approve Gypsum Board	30	29-Aug-23	11-Oct-23	02-Jul-24	13-Aug-24	211	0%		Review & Approve Gypsum Board																											
Section 09 51 23 Acoustical Ceiling Tile		75	26-Jun-23	11-Oct-23	30-Apr-24	13-Aug-24	211			11-Oct-23, Section 09 51 23 Acoustical Ceiling Tile																											
 S2790	Prepare & Submit Acoustical Ceiling Tile	45	26-Jun-23	28-Aug-23	30-Apr-24	01-Jul-24	211	0%		Prepare & Submit Acoustical Ceiling Tile																											
 S2800	Review & Approve Acoustical Ceiling Tile	30	29-Aug-23	11-Oct-23	02-Jul-24	13-Aug-24	211	0%		Review & Approve Acoustical Ceiling Tile																											
Section 09 65 13 Resilient Base And Accessories.		75	26-Jun-23	11-Oct-23	20-May-24	03-Sep-24	225			11-Oct-23, Section 09 65 13 Resilient Base And Accessories.																											
 S2830	Prepare & Submit Resilient Base And Accessories.	45	26-Jun-23	28-Aug-23	20-May-24	22-Jul-24	225	0%		Prepare & Submit Resilient Base And Accessories.																											
 S2840	Review & Approve Resilient Base And Accessories.	30	29-Aug-23	11-Oct-23	23-Jul-24	03-Sep-24	225	0%		Review & Approve Resilient Base And Accessories.																											
Section 09 65 19 Resilient Flooring		75	26-Jun-23	11-Oct-23	15-May-24	28-Aug-24	222			11-Oct-23, Section 09 65 19 Resilient Flooring																											
 S2690	Prepare & Submit Resilient Flooring	45	26-Jun-23	28-Aug-23	15-May-24	17-Jul-24	222	0%		Prepare & Submit Resilient Flooring																											
 S2700	Review & Approve Resilient Flooring	30	29-Aug-23	11-Oct-23	18-Jul-24	28-Aug-24	222	0%		Review & Approve Resilient Flooring																											
Section 09 68 13 Tile Carpeting		75	26-Jun-23	11-Oct-23	15-May-24	28-Aug-24	222			11-Oct-23, Section 09 68 13 Tile Carpeting																											
 S2730	Prepare & Submit Tile Carpeting	45	26-Jun-23	28-Aug-23	15-May-24	17-Jul-24	222	0%		Prepare & Submit Tile Carpeting																											
 S2740	Review & Approve Tile Carpeting	30	29-Aug-23	11-Oct-23	18-Jul-24	28-Aug-24	222	0%		Review & Approve Tile Carpeting																											
Section 09 91 00 Painting		75	26-Jun-23	11-Oct-23	09-May-24	22-Aug-24	218			11-Oct-23, Section 09 91 00 Painting																											
 S2770	Prepare & Submit Painting	45	26-Jun-23	28-Aug-23	09-May-24	11-Jul-24	218	0%		Prepare & Submit Painting																											
 S2780	Review & Approve Painting	30	29-Aug-23	11-Oct-23	12-Jul-24	22-Aug-24	218	0%		Review & Approve Painting																											
Division 10 - Specialties		75	26-Jun-23	11-Oct-23	20-May-24	03-Sep-24	225			11-Oct-23, Division 10 - Specialties																											
Section 10 11 00 Visual Display Surfaces		75	26-Jun-23	11-Oct-23	20-May-24	03-Sep-24	225			11-Oct-23, Section 10 11 00 Visual Display Surfaces																											
 S1120	Prepare & Submit Visual Display Surfaces	45	26-Jun-23	28-Aug-23	20-May-24	22-Jul-24	225	0%		Prepare & Submit Visual Display Surfaces																											
 S1130	Review & Approve Visual Display Surfaces	30	29-Aug-23	11-Oct-23	23-Jul-24	03-Sep-24	225	0%		Review & Approve Visual Display Surfaces																											
Division 12 - Furnishings		75	26-Jun-23	11-Oct-23	22-May-24	05-Sep-24	227			11-Oct-23, Division 12 - Furnishings																											
Section 12 24 13 Roller Window Shades		75	26-Jun-23	11-Oct-23	22-May-24	05-Sep-24	227			11-Oct-23, Section 12 24 13 Roller Window Shades																											
 S1140	Prepare & Submit Roller Window Shades	45	26-Jun-23	28-Aug-23	22-May-24	24-Jul-24	227	0%		Prepare & Submit Roller Window Shades																											
 S1150	Review & Approve Roller Window Shades	30	29-Aug-23	11-Oct-23	25-Jul-24	05-Sep-24	227	0%		Review & Approve Roller Window Shades																											
Division 14 - Special Construction		75	26-Jun-23	11-Oct-23	24-May-24	09-Sep-24	229			11-Oct-23, Division 14 - Special Construction																											
Section 14 26 00 Limited Use Application Hydraulic Elevator		75	26-Jun-23	11-Oct-23	24-May-24	09-Sep-24	229			11-Oct-23, Section 14 26 00 Limited Use Application Hydraulic Elevator																											
 S1160	Prepare & Submit Limited Use Application Hydraulic Elevator	45	26-Jun-23	28-Aug-23	24-May-24	26-Jul-24	229	0%		Prepare & Submit Limited Use Application Hydraulic Elevator																											
 S1170	Review & Approve Limited Use Application Hydraulic Elevator	30	29-Aug-23	11-Oct-23	29-Jul-24	09-Sep-24	229	0%		Review & Approve Limited Use Application Hydraulic Elevator																											
Division 22 - Plumbing		75	26-Jun-23	11-Oct-23	03-Apr-24	09-Sep-24	229			11-Oct-23, Division 22 - Plumbing																											
Section 22 05 01 Basic Plumbing Materials And Methods		75	26-Jun-23	11-Oct-23	03-Apr-24	17-Jul-24	192			11-Oct-23, Section 22 05 01 Basic Plumbing Materials And Methods																											
 S1950	Prepare & Submit Basic Plumbing Materials And Methods	45	26-Jun-23	28-Aug-23	03-Apr-24	04-Jun-24	192	0%		Prepare & Submit Basic Plumbing Materials And Methods																											
 S1960	Review & Approve Basic Plumbing Materials And Methods	30	29-Aug-23	11-Oct-23	05-Jun-24	17-Jul-24	192	0%		Review & Approve Basic Plumbing Materials And Methods																											
Section 22 10 05 Plumbing Piping		75	26-Jun-23	11-Oct-23	03-Apr-24	17-Jul-24	192			11-Oct-23, Section 22 10 05 Plumbing Piping																											
 S1930	Prepare & Submit Plumbing Piping	45	26-Jun-23	28-Aug-23	03-Apr-24	04-Jun-24	192	0%		Prepare & Submit Plumbing Piping																											

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone







NO PLUMBING IN OUR CONTRACT

LEAVE ALL GOOD 30



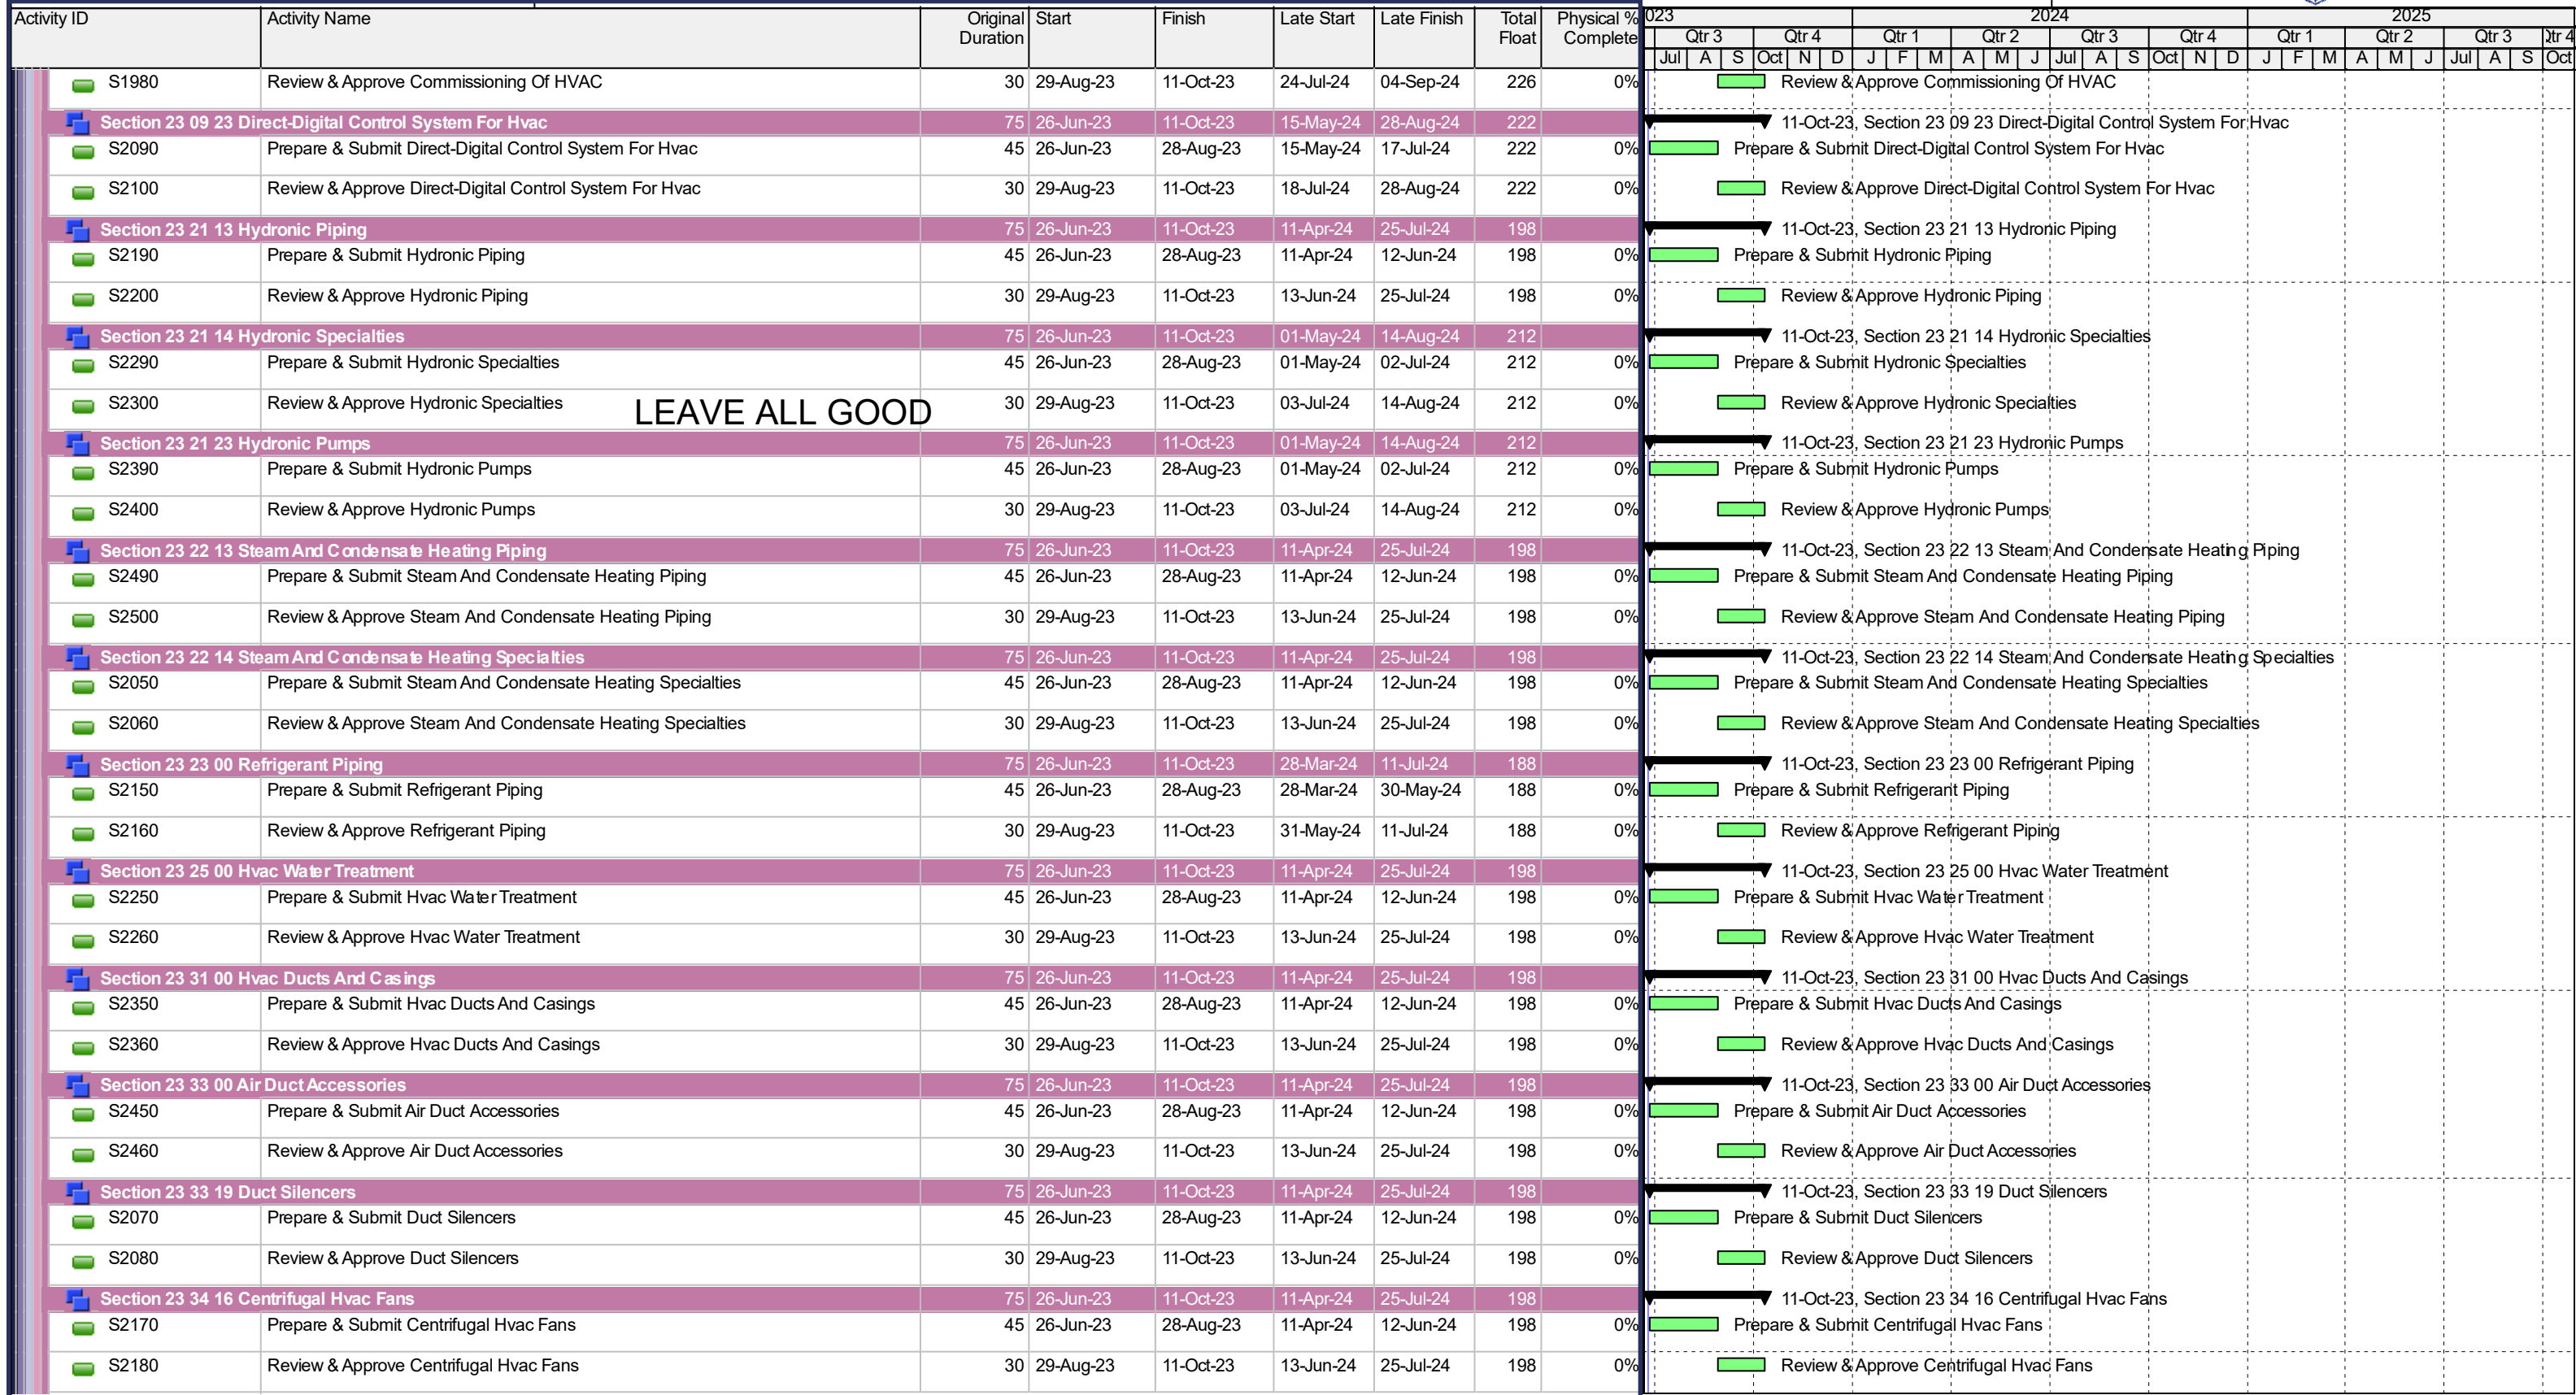

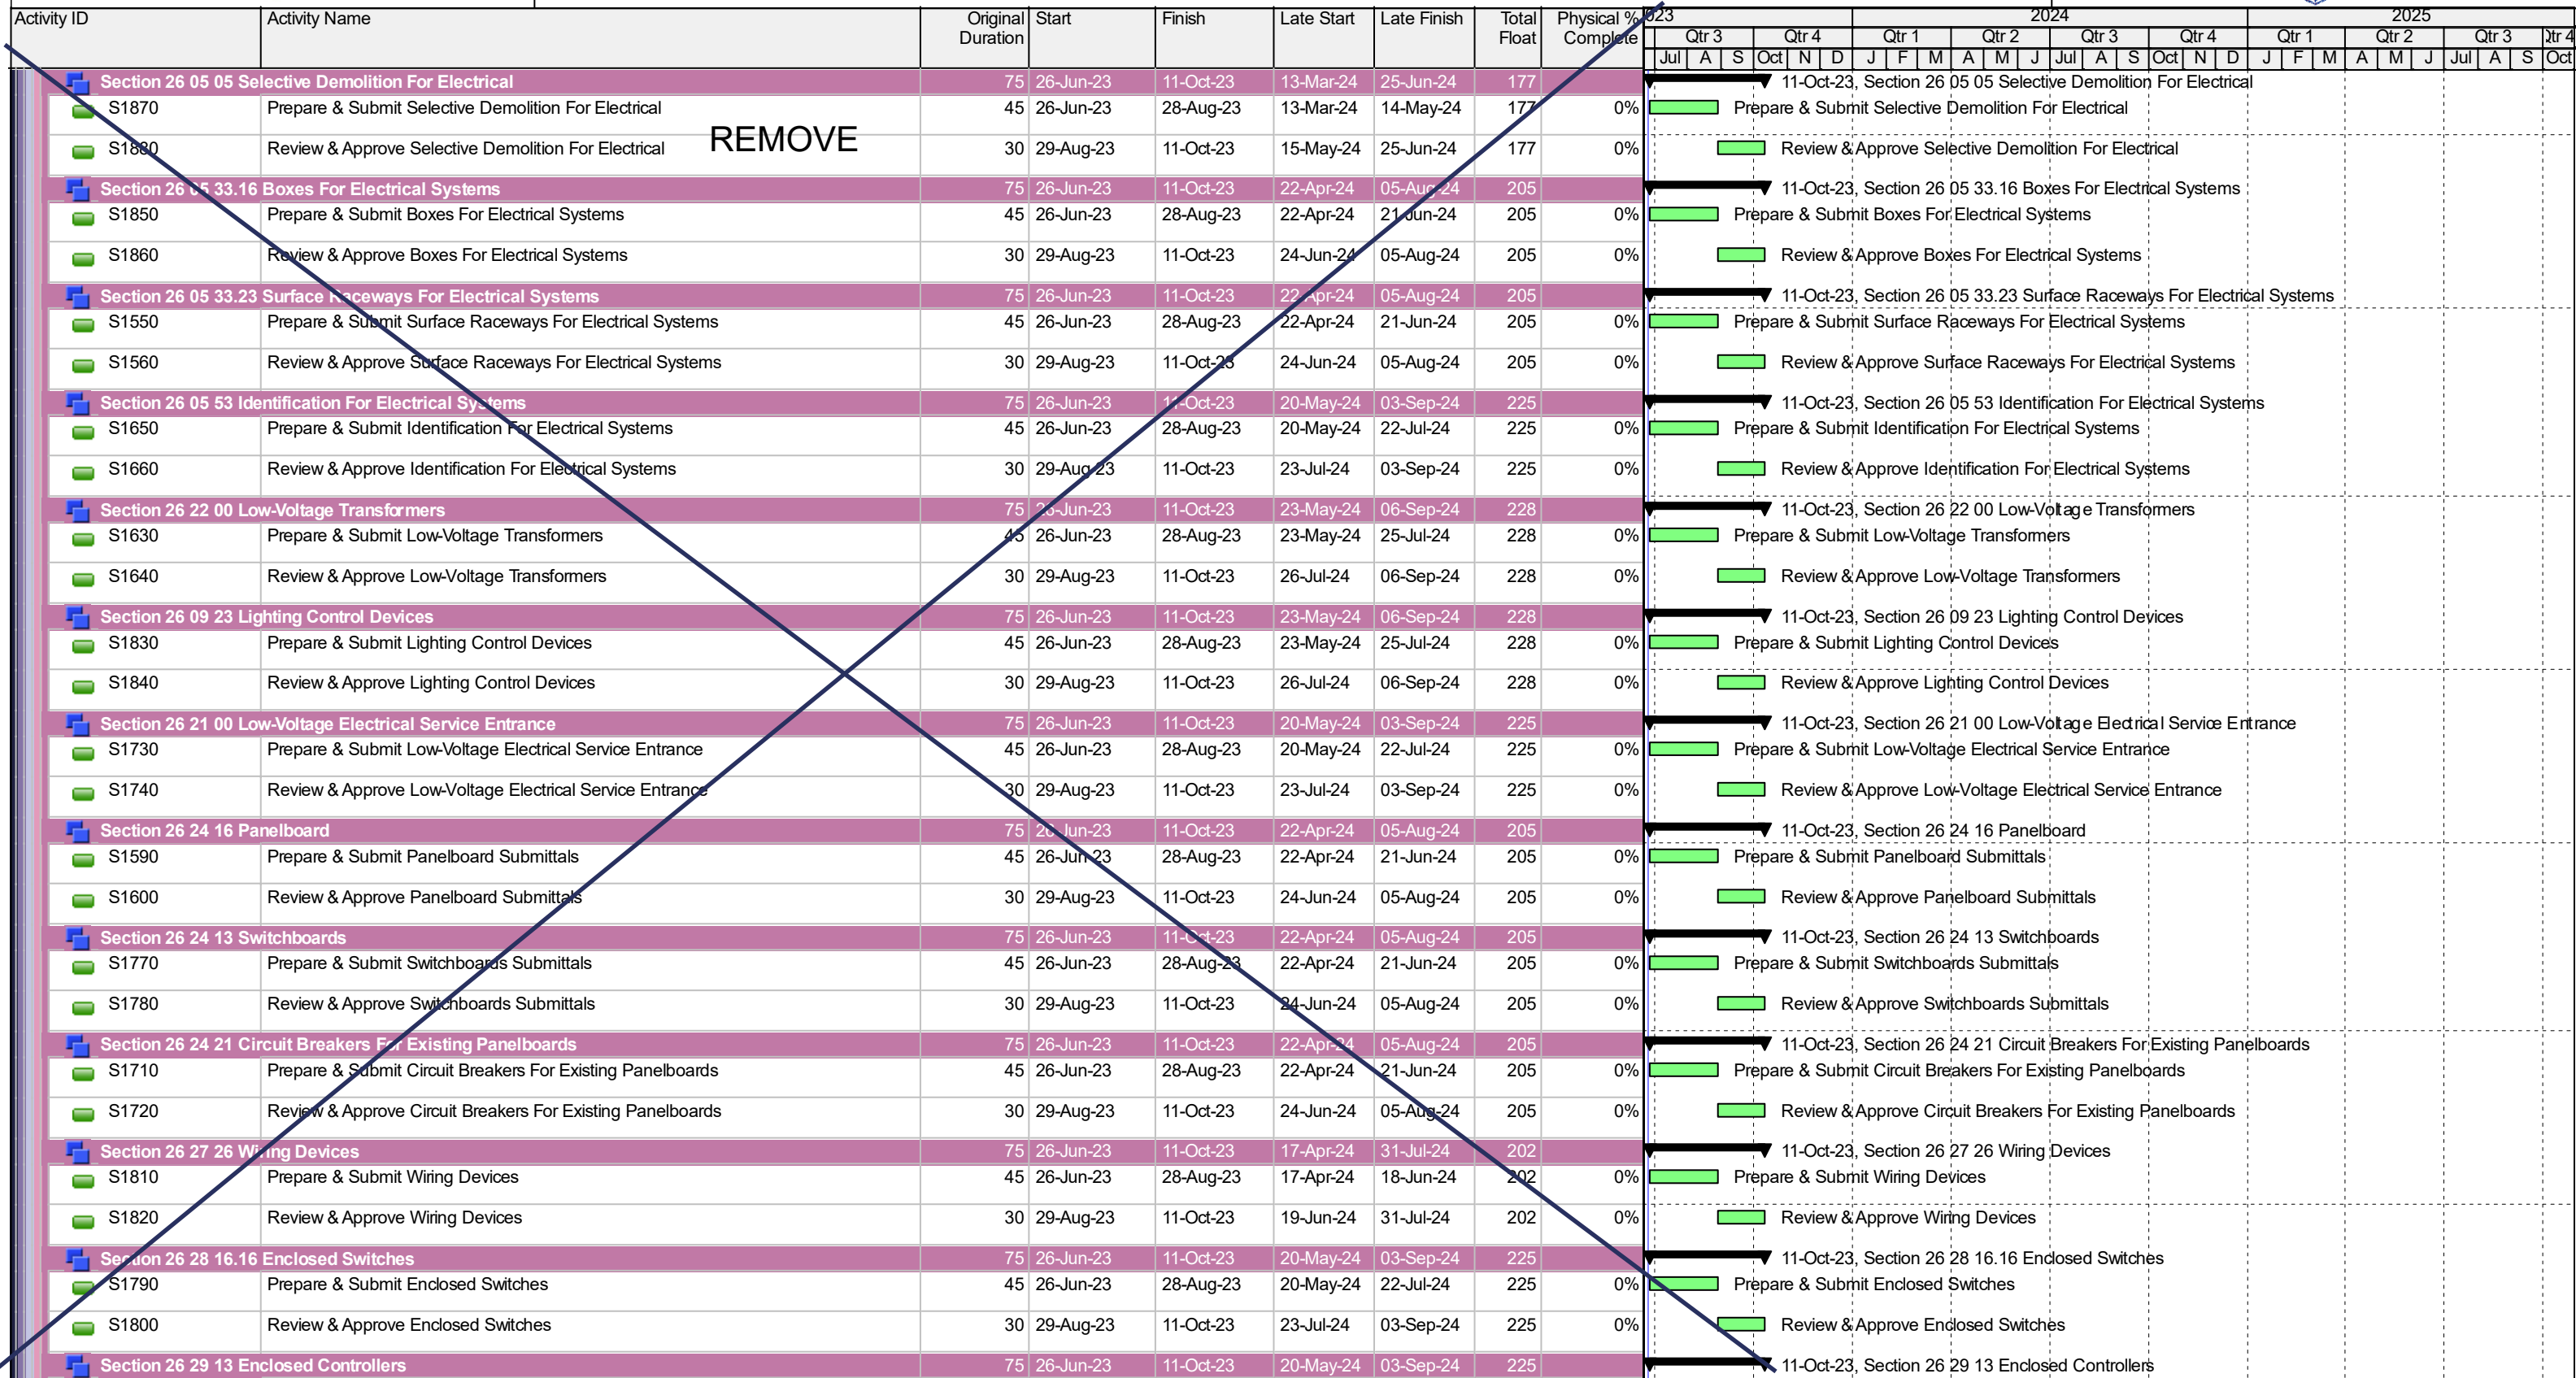



Nanuet Senior HS Barr MS - Phase 3 - Baseline schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	2023		2024												2025											
									Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1		Qtr 2		Qtr 3		Qtr 4	
									Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A
 S1750	Prepare & Submit Enclosed Controllers	45	26-Jun-23	28-Aug-23	20-May-24	22-Jul-24	225	0%		Prepare & Submit Enclosed Controllers																								
 S1760	Review & Approve Enclosed Controllers	30	29-Aug-23	11-Oct-23	23-Jul-24	03-Sep-24	225	0%		Review & Approve Enclosed Controllers																								
 Section 26 29 23 Variable-Frequency Motor Controllers																																		
 S1670	Prepare & Submit Variable-Frequency Motor Controllers	45	26-Jun-23	28-Aug-23	20-May-24	22-Jul-24	225	0%		Prepare & Submit Variable-Frequency Motor Controllers																								
 S1680	Review & Approve Variable-Frequency Motor Controllers	30	29-Aug-23	11-Oct-23	23-Jul-24	03-Sep-24	225	0%		Review & Approve Variable-Frequency Motor Controllers																								
 Section 26 51 00 Interior Lighting																																		
 S1890	Prepare & Submit Interior Lighting	45	26-Jun-23	28-Aug-23	23-May-24	25-Jul-24	228	0%		Prepare & Submit Interior Lighting																								
 S1900	Review & Approve Interior Lighting	30	29-Aug-23	11-Oct-23	26-Jul-24	06-Sep-24	228	0%		Review & Approve Interior Lighting																								
 Division 27 - Communications																																		
 Section 27 10 00 Structured Cabling-Voice And Data- Inside																																		
 S1260	Prepare & Submit Structured Cabling-Voice And Data- Inside	45	26-Jun-23	28-Aug-23	17-Apr-24	18-Jun-24	202	0%		Prepare & Submit Structured Cabling-Voice And Data- Inside																								
 S1270	Review & Approve Structured Cabling-Voice And Data- Inside	30	29-Aug-23	11-Oct-23	19-Jun-24	31-Jul-24	202	0%		Review & Approve Structured Cabling-Voice And Data- Inside																								
 Procurement																																		
 S1300	Fabricate & Deliver R-MS-1 & 2	40	12-Oct-23	11-Dec-23	09-Jul-24	03-Sep-24	185	0%		 Fabricate & Deliver R-MS-1 & 2																								
 S1310	Fabricate & Deliver EF-8, 10, 21 & 23	150	12-Oct-23	17-May-24	09-Jan-24	08-Aug-24	58	0%		 Fabricate & Deliver EF-8, 10, 21 & 23																								
 S1320	Fabricate & Deliver Dampers	88	12-Oct-23	21-Feb-24	26-Apr-24	28-Aug-24	134	0%		 Fabricate & Deliver Dampers																								
 S1340	Fabricate & Deliver UV-MS- 1-41	55	12-Oct-23	03-Jan-24	13-Jun-24	29-Aug-24	168	0%		 Fabricate & Deliver UV-MS- 1-41																								
 S1350	Fabricate & Deliver HP-MS-3-9	60	12-Oct-23	10-Jan-24	16-May-24	08-Aug-24	148	0%		 Fabricate & Deliver HP-MS-3-9																								
 S1360	Fabricate & Deliver CV-HS-1-11	40	12-Oct-23	11-Dec-23	03-Jul-24	28-Aug-24	182	0%		 Fabricate & Deliver CV-HS-1-11																								
 S1370	Fabricate & Deliver UH-HS-1	20	12-Oct-23	08-Nov-23	29-Jul-24	23-Aug-24	199	0%		 Fabricate & Deliver UH-HS-1																								
 S1380	Fabricate & Deliver CUH- HS-1, 2, 3	40	12-Oct-23	11-Dec-23	03-Jul-24	28-Aug-24	182	0%		 Fabricate & Deliver CUH- HS-1, 2, 3																								
 S1390	Fabricate & Deliver R2-1, 2, 3, & 4	40	12-Oct-23	11-Dec-23	03-Jul-24	28-Aug-24	182	0%		 Fabricate & Deliver R2-1, 2, 3, & 4																								
 S1400	Fabricate & Deliver F-HS-2 & 3	150	12-Oct-23	17-May-24	18-Jan-24	16-Aug-24	64	0%		 Fabricate & Deliver F-HS-2 & 3																								
 S1410	Fabricate & Deliver L-1 Louver with bird screen	88	12-Oct-23	21-Feb-24	29-Apr-24	29-Aug-24	135	0%		 Fabricate & Deliver L-1 Louver with bird screen																								
 S1420	Fabricate & Deliver RTU-HS- 4 & 5	110	12-Oct-23	22-Mar-24	15-Mar-24	16-Aug-24	104	0%		 Fabricate & Deliver RTU-HS- 4 & 5																								
 S1430	Fabricate & Deliver BC-HS-1 & 2	70	12-Oct-23	25-Jan-24	06-Mar-24	11-Jun-24	97	0%		 Fabricate & Deliver BC-HS-1 & 2																								
 S1440	Fabricate & Deliver HC-HS-2 to 4	40	12-Oct-23	11-Dec-23	28-Jun-24	23-Aug-24	179	0%		 Fabricate & Deliver HC-HS-2 to 4																								
 S1450	Fabricate & Deliver AHU-HS-3	120	12-Oct-23	05-Apr-24	13-Mar-24	28-Aug-24	102	0%		 Fabricate & Deliver AHU-HS-3																								
 S1460	Fabricate & Deliver ACCU-HS 2	60	12-Oct-23	10-Jan-24	24-May-24	16-Aug-24	154	0%		 Fabricate & Deliver ACCU-HS 2																								
 S1470	Fabricate & Deliver CP-HS-2	140	12-Oct-23	03-May-24	08-Feb-24	23-Aug-24	79	0%		 Fabricate & Deliver CP-HS-2																								
 S1480	Fabricate & Deliver HX-HS-2	40	12-Oct-23	11-Dec-23	28-Jun-24	23-Aug-24	179	0%		 Fabricate & Deliver HX-HS-2																								
 S1490	Fabricate & Deliver P-HS-3 & 4	120	12-Oct-23	05-Apr-24	08-Mar-24	23-Aug-24	99	0%		 Fabricate & Deliver P-HS-3 & 4																								
 S1500	Fabricate & Deliver B&G Suction Diffuser	80	12-Oct-23	08-Feb-24	28-Mar-24	18-Jul-24	113	0%		 Fabricate & Deliver B&G Suction Diffuser																								
 S1510	Fabricate & Deliver B&G Triple Duty Valve	100	12-Oct-23	08-Mar-24	29-Feb-24	18-Jul-24	93	0%		 Fabricate & Deliver B&G Triple Duty Valve																								

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone





Nanuet Senior HS Barr MS - Phase 3 - Baseline schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	2023												2024												2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
									Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														
									Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														
S1520	Fabricate & Deliver Flex Hose 6"X 24"	30	12-Oct-23	27-Nov-23	15-Jul-24	23-Aug-24	189	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										

IS THIS SCOPE YOUR INCLUDING FOR THE MECHANICAL WORK IF IT IS THEN LEAVE IN IN ALL THE LOCATONS I SAID REMOVE CEILINGS REMOVE AND REPLACARE ONLY IN AREAS OF MECH WORK THE NOTES ON DWGS STATE WHERE



Nanuet Senior HS Barr MS - Phase 3 - Baseline schedule



Activity ID		Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	2023												2024												2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
										Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												
										Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												
	C6650	Mechanical Rough-Ins Punchlist - Basement - Nanuet Senior HS	3	09-Aug-24	13-Aug-24	09-Aug-24	13-Aug-24	0	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								

Remaining Level of Effort

Actual Level of Effort


Actual Work

Remaining Work

Critical Remaining Work

Milestone



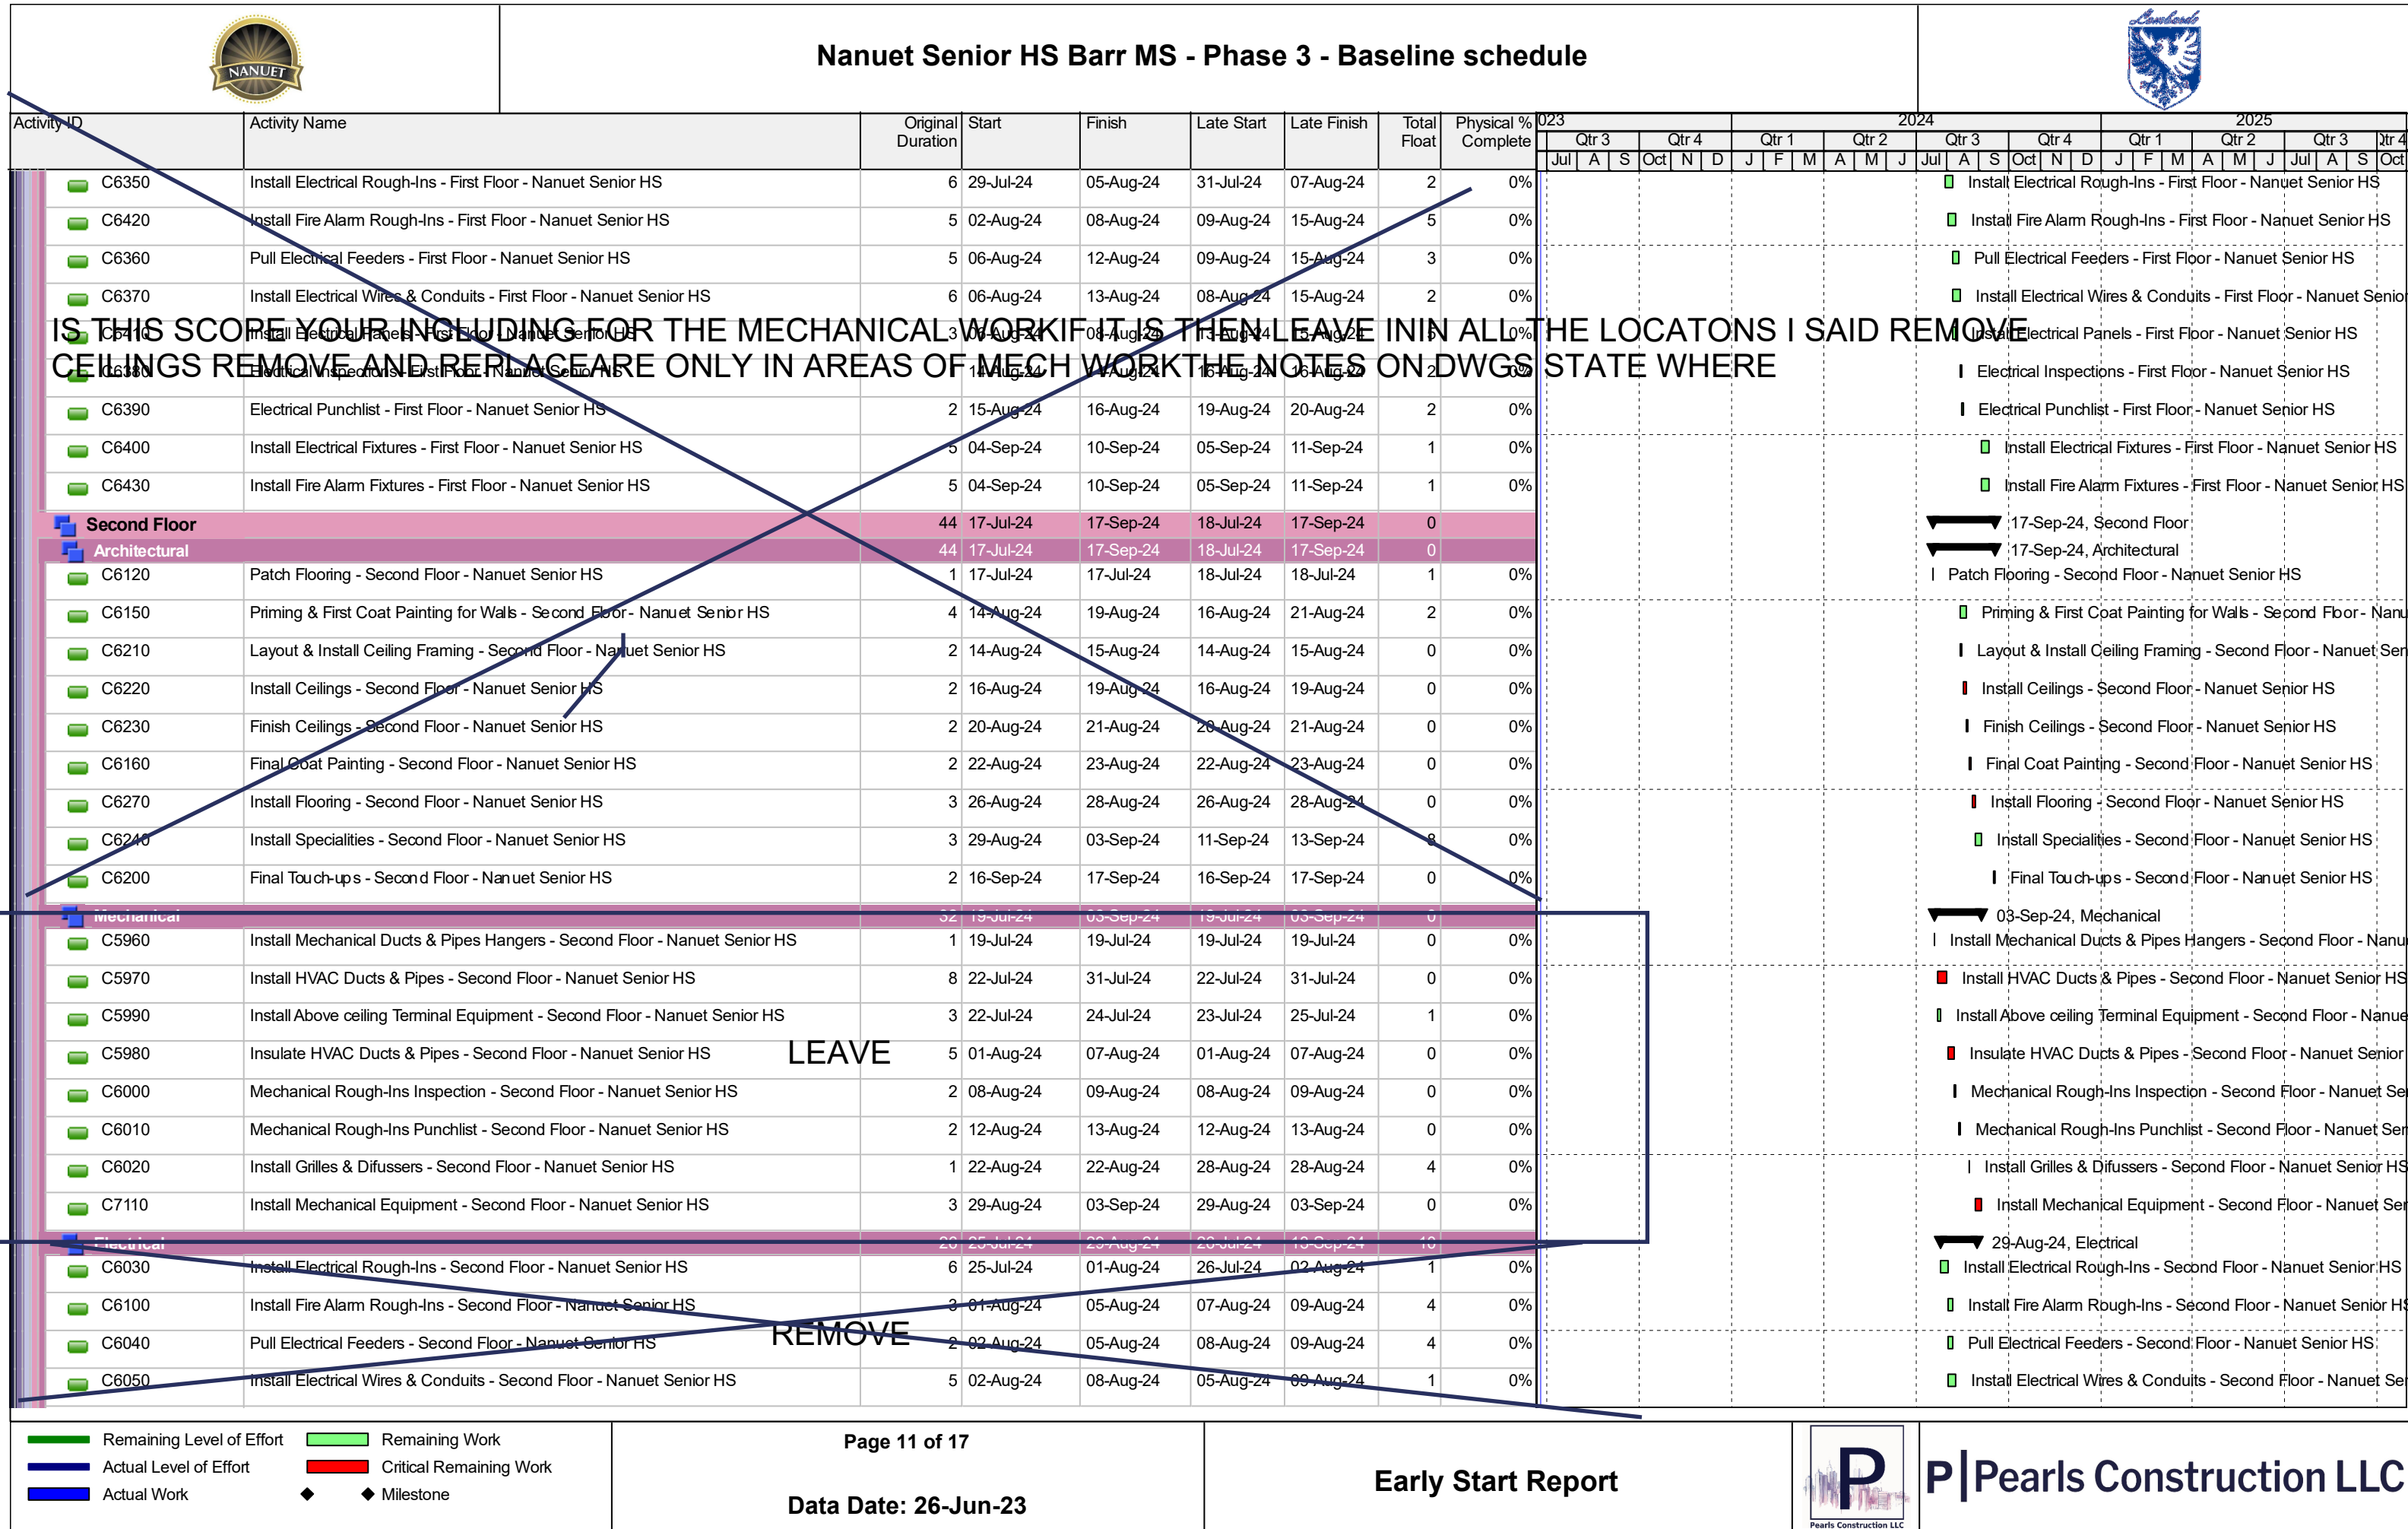

Nanuet Senior HS Barr MS - Phase 3 - Baseline schedule

[illegible]

 Remaining Level of Effort
 Remaining Work
 Actual Level of Effort
 Critical Remaining Work
 Actual Work
 ◆ ◆ Milestone





Nanuet Senior HS Barr MS - Phase 3 - Baseline schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	2023												2024												2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
									Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
									Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
 C5260	Install Ceiling - Lower Level - Barr MS	3	19-Aug-24	21-Aug-24	19-Aug-24	21-Aug-24	0	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		

IS THIS SCOPE YOUR INCLUDING
FOR THE MECHANICAL WORK
IF IT IS THEN LEAVE IN
IN ALL THE LOCATIONS I SAID REMOVE
CEILING REMOVE AND REPLACE
ARE ONLY IN AREAS OF MECH WORK
THE NOTES ON DWGS
STATE WHERE

LEAVE

NO PLUMBING IN OUR CONTRACT

- Remaining Level of Effort

Actual Level of Effort

Actual Work
- Remaining Work

Critical Remaining Work

Milestone





Nanuet Senior HS Barr MS - Phase 3 - Baseline schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	2023												2024												2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
									Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
									Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
 C5050	Insulate Plumbing Piping - Lower Level - Barr MS	4	24-Jul-24	29-Jul-24	07-Aug-24	12-Aug-24	10	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone





Nanuet Senior HS Barr MS - Phase 3 - Baseline schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	2023												2024												2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
									Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
									Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
 C3900	Pull Electrical Feeders - First Floor - Barr MS	2	01-Aug-24	02-Aug-24	02-Aug-24	05-Aug-24	1	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				</

REMOVE

NO PLUMBING IN OUR CONTRACT

IS THIS SCOPE YOUR INCLUDING FOR THE MECHANICAL WORK IF IT IS THEN LEAVE IN ALL THE LOCATONS I SAID REMOVE CEILINGS REMOVE AND REPLACE ARE ONLY IN AREAS OF MECH WORK THE NOTES ON DWGS STATE WHERE

LEAVE

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone





Nanuet Senior HS Barr MS - Phase 3 - Baseline schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	2023												2024												2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
									Qtr 3				Qtr 4				Qtr 1				Qtr 2				Qtr 3				Qtr 4				Qtr 1				Qtr 2				Qtr 3				Qtr 4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
									Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
 C4720	Install Fire Alarm Rough-Ins - Second Floor - Barr MS	5	29-Jul-24	02-Aug-24	08-Aug-24	14-Aug-24	8	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									

- Remaining Level of Effort

Actual Level of Effort

Actual Work
- Remaining Work

Critical Remaining Work

Milestone



