


Consigli Construction Company
Iona College - School of Health Sciences
A05 - Remaining Work with Last Update as of 03-Apr-22



Consigli Construction Company
Iona College - School of Health Sciences
A05 - Remaining Work with Last Update as of 03-Apr-22

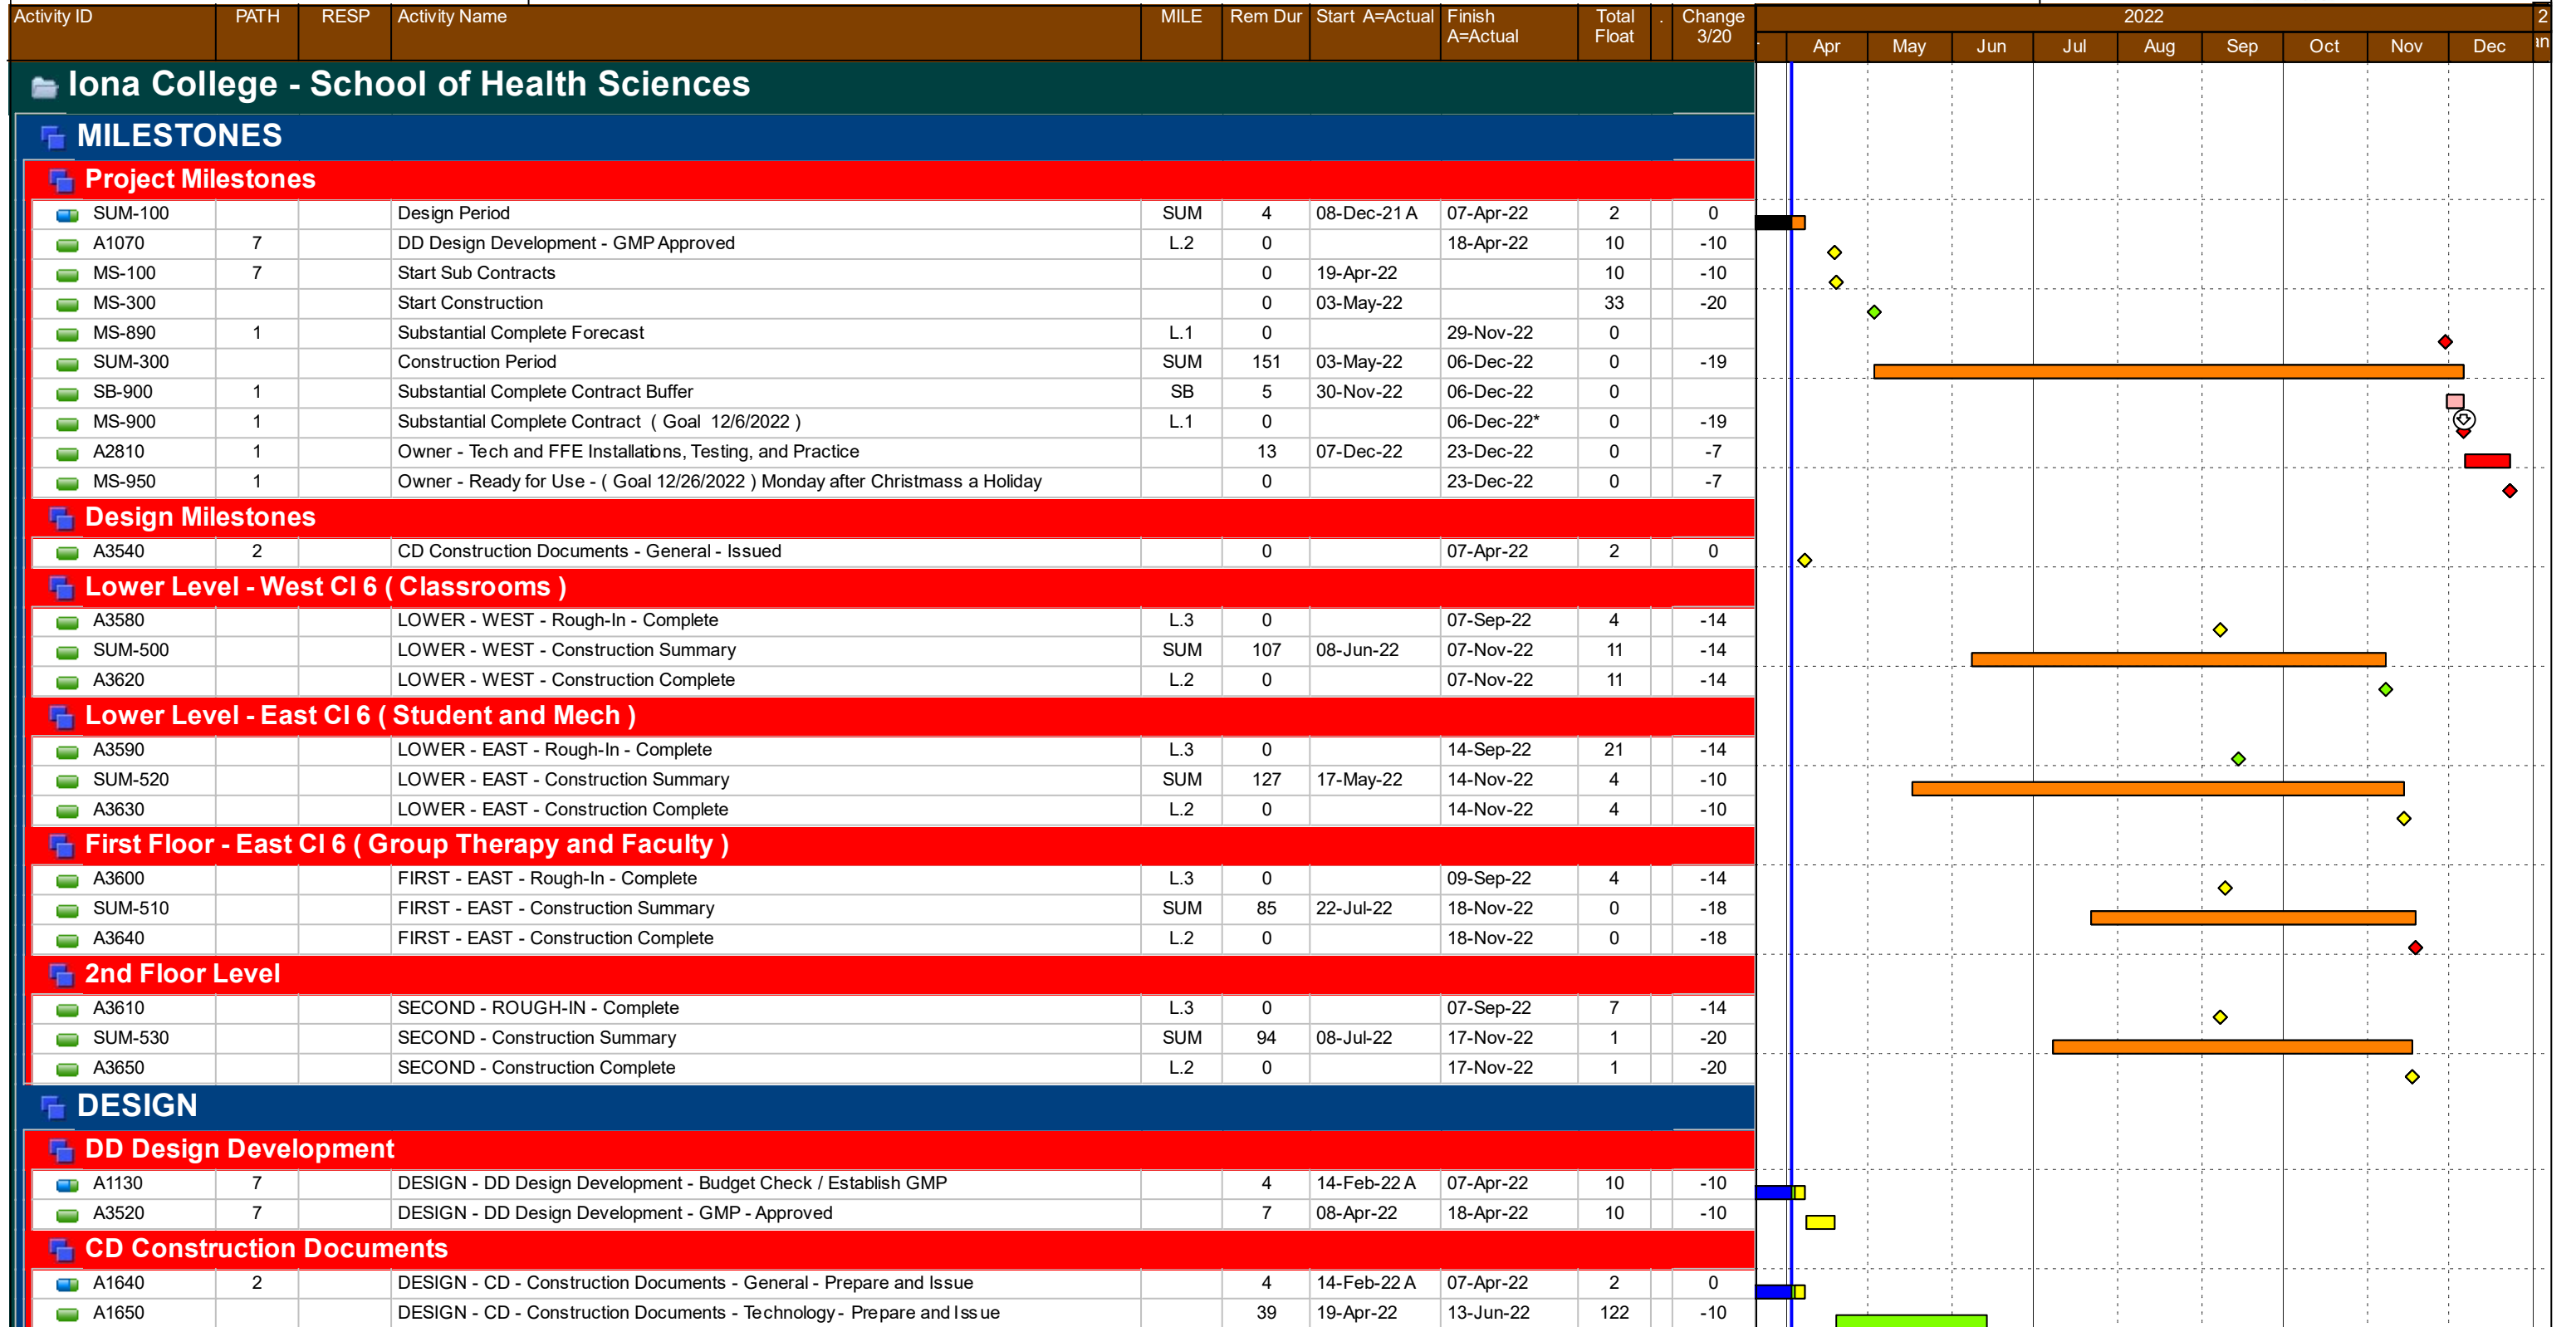

Activity ID	PATH	RESP	Activity Name	MILE	Rem Dur	Start A=Actual	Finish A=Actual	Total Float	Change 3/20	2022												2 in
										Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec				
 A1660			DESIGN - CD - Construction Documents - FFE - Prepare and Issue		40	19-Apr-22	14-Jun-22	121	-10													
 PROCUREMENT																						
 Bid Packages 1																						
 02 4119 Selective Demo																						
 N01-100		DEMO	PROC PKG 1 - DEMO - Buyout and Issue OAL		10	04-Apr-22	15-Apr-22	33														
 N01-200		DEMO	PROC PKG 1 - DEMO - Review and Returned Signed OAL		5	18-Apr-22	22-Apr-22	33														
 A1670		DEMO	PROC PKG 1 - DEMO - Issue Letter of Intent		1	25-Apr-22	25-Apr-22	33	-21													
 A1710		DEMO	PROC PKG 1 - DEMO - Site Prep and Mobilization		5	26-Apr-22	02-May-22	33	-21													
 05 Structural Steel for Demo																						
 N01-101	6	STL	PROC PKG 1 - STRU STEEL for DEMO - Buyout and Issue OAL		10	04-Apr-22	15-Apr-22	8														
 N01-201	6	STL	PROC PKG 1 - STRU STEEL for DEMO - Review and Returned Signed OAL		5	18-Apr-22	22-Apr-22	8														
 A1720	6	STL	PROC PKG 1 - STRU STEEL for DEMO - Issue Letter of Intent		1	25-Apr-22	25-Apr-22	8	-21													
 A1730	6	STL	PROC PKG 1 - STRU STEEL for DEMO - Submittal - Prepare and Submit		10	26-Apr-22	09-May-22	8	-21													
 A1740	6	STL	PROC PKG 1 - STRU STEEL for DEMO - Submittal - Review and Approve		5	10-May-22	16-May-22	8	-21													
 A1760	6	STL	PROC PKG 1 - STRU STEEL for DEMO - Fab and Deliver		10	17-May-22	31-May-22	8	-21													
 08 4113 Storefront (Alum Framed Windows)																						
 N01-117	1	STOR	PROC PKG 1 - STOREFRONT - Buyout and Issue OAL		10	04-Apr-22	15-Apr-22	0														
 N01-217	1	STOR	PROC PKG 1 - STOREFRONT - Review and Returned Signed OAL		5	18-Apr-22	22-Apr-22	0														
 B1030	1	STOR	PROC PKG 1 - STOREFRONT - Issue Letter of Intent		1	25-Apr-22	25-Apr-22	0	-21													
 B1040	1	STOR	PROC PKG 1 - STOREFRONT - Submittal - Prepare and Submit		20	26-Apr-22	23-May-22	0	-21													
 B1050	1	STOR	PROC PKG 1 - STOREFRONT - Submittal - Review and Approve		10	24-May-22	07-Jun-22	0	-21													
 B1060	1	STOR	PROC PKG 1 - STOREFRONT - Fab and Deliver (10 - 11 weeks)		55	08-Jun-22	24-Aug-22	0	-21													
 08 5113 Windows																						
 N01-109	5	GLAS	PROC PKG 1 - ALUM FRAMED WINDOWS - Buyout and Issue OAL		10	04-Apr-22	15-Apr-22	8														
 N01-209	5	GLAS	PROC PKG 1 - ALUM FRAMED WINDOWS - Review and Returned Signed OAL		5	18-Apr-22	22-Apr-22	8														
 A3750	5	GLAS	PROC PKG 1 - ALUM FRAMED WINDOWS - Issue Letter of Intent		1	25-Apr-22	25-Apr-22	8	-21													
 A3760	5	GLAS	PROC PKG 1 - ALUM FRAMED WINDOWS - Submittal - Prepare and Submit		20	26-Apr-22	23-May-22	8	-21													
 A3770	5	GLAS	PROC PKG 1 - ALUM FRAMED WINDOWS - Submittal - Review and Approve		10	24-May-22	07-Jun-22	8	-21													
 A3780	5	GLAS	PROC PKG 1 - ALUM FRAMED WINDOWS - Fab and Deliver (5 - 7 weeks)		35	08-Jun-22	27-Jul-22	8	-21													
 Switchgear																						
 B1370	4	OWN	PROC PKG 1 - ELEC - SWITCHGEAR - Owner Approval Letter		3	11-Mar-22 A	06-Apr-22	7	-10													
 A2790	4	ELEC	PROC PKG 1 - ELEC - SWITCHGEAR - Fab and Deliver (30 Weeks + 1 wk ship) was 2£		155	07-Apr-22	14-Nov-22	7	-30													
 03 Concrete																						
 Slabs																						
 N01-119		CONC	PROC - CONC - Buyout and Issue OAL		10	08-Apr-22	21-Apr-22	48														
 N01-219		CONC	PROC - CONC - Review and Returned Signed OAL		5	22-Apr-22	28-Apr-22	48														
 B1140		CONC	PROC - CONC - Issue Letter of Intent		1	29-Apr-22	29-Apr-22	48	-11													
 B1150		CONC	PROC - CONC - Submittal - Prepare and Submit		5	02-May-22	06-May-22	48	-11													
 B1160		CONC	PROC - CONC - Submittal - Review and Approve		5	09-May-22	13-May-22	48	-11													
 B1170		CONC	PROC - CONC - Fab and Deliver		5	16-May-22	20-May-22	48	-11													
 06 Woods, Plastics, and Composites																						

Report: A2724 05B Detailed Remaining Work MIN TASK filter: 01 Remaining Work with LAST.				Consigli Construction Company Iona College - School of Health Sciences A05 - Remaining Work with Last Update as of 03-Apr-22																			2
Activity ID	PATH	RESP	Activity Name	MILE	Rem Dur	Start A=Actual	Finish A=Actual	Total Float	Change 3/20	2022												2 in	
										Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec					
 06 1000 Rough Carpentry																							
 N01-103		FRAM	PROC - FRAMING - Buyout and Issue OAL		10	08-Apr-22	21-Apr-22	39															
 N01-203		FRAM	PROC - FRAMING - Review and Returned Signed OAL		5	22-Apr-22	28-Apr-22	39															
 A2640		FRAM	PROC - FRAMING - Issue Letter of Intent		1	29-Apr-22	29-Apr-22	39	-11														
 A2650		FRAM	PROC - FRAMING - Submittal - Prepare and Submit		5	02-May-22	06-May-22	39	-11														
 A2660		FRAM	PROC - FRAMING - Submittal - Review and Approve		5	09-May-22	13-May-22	39	-11														
 A2670		FRAM	PROC - FRAMING - Fab and Deliver		5	16-May-22	20-May-22	39	-11														
 06 4000 Millwork																							
 N01-120		MILL	PROC - MILLWORK - Buyout and Issue OAL		10	08-Apr-22	21-Apr-22	97															
 N01-220		MILL	PROC - MILLWORK - Review and Returned Signed OAL		5	22-Apr-22	28-Apr-22	97															
 B1240		MILL	PROC - MILLWORK - Issue Letter of Intent		1	29-Apr-22	29-Apr-22	97	-11														
 B1250		MILL	PROC - MILLWORK - Submittal - Prepare and Submit		5	02-May-22	06-May-22	97	-11														
 B1260		MILL	PROC - MILLWORK - Submittal - Review and Approve		5	09-May-22	13-May-22	97	-11														
 B1270		MILL	PROC - MILLWORK - Fab and Deliver		5	16-May-22	20-May-22	97	-11														
 08 Openings																							
 08 1200 HM Door Frames																							
 N01-108	8	DOOR	PROC - HM DOORS and FRAMES - Buyout and Issue OAL		10	08-Apr-22	21-Apr-22	11															
 N01-208	8	DOOR	PROC - HM DOORS and FRAMES - Review and Returned Signed OAL		5	22-Apr-22	28-Apr-22	11															
 A3710	8	DOOR	PROC - HM DOORS and FRAMES - Issue Letter of Intent		1	29-Apr-22	29-Apr-22	11	-6														
 A3720	8	DOOR	PROC - HM DOORS and FRAMES - Submittal - Prepare and Submit		15	02-May-22	20-May-22	11	-6														
 A3730	8	DOOR	PROC - HM DOORS and FRAMES - Submittal - Review and Approve		10	23-May-22	06-Jun-22	11	-6														
 A3740	8	DOOR	PROC - HM DOORS and FRAMES - Frames - Fab and Deliver (4 - 6 weeks)		30	07-Jun-22	19-Jul-22	11	-6														
 N06-100		DOOR	PROC - HM DOORS and FRAMES - Doors - Fab and Deliver (8 - 10 weeks)		50	07-Jun-22	16-Aug-22	47	-6														
 08 7100 Door Hardware																							
 B1190		DOOR	PROC - DOOR HARDWARE - Submittal - Prepare and Submit		20	02-May-22	27-May-22	42	-6														
 B1200		DOOR	PROC - DOOR HARDWARE - Submittal - Review and Approve		10	31-May-22	13-Jun-22	42	-6														
 B1210		DOOR	PROC - DOOR HARDWARE - Fab and Deliver (8 - 10 weeks)		50	14-Jun-22	23-Aug-22	42	-6														
 09 Finishes																							
 09 3000 Ceramic Tile																							
 N01-110		TILE	PROC - CERAMIC TILE - Buyout and Issue OAL		10	08-Apr-22	21-Apr-22	68															
 N01-210		TILE	PROC - CERAMIC TILE - Review and Returned Signed OAL		5	22-Apr-22	28-Apr-22	68															
 A3790		TILE	PROC - CERAMIC TILE - Issue Letter of Intent		1	29-Apr-22	29-Apr-22	68	-6														
 A3800		TILE	PROC - CERAMIC TILE - Submittal - Prepare and Submit		20	02-May-22	27-May-22	68	-6														
 A3810		TILE	PROC - CERAMIC TILE - Submittal - Review and Approve		10	31-May-22	13-Jun-22	68	-6														
 A3820		TILE	PROC - CERAMIC TILE - Fab and Deliver (3 - 5 weeks)		25	14-Jun-22	19-Jul-22	68	-6														
 09 5000 Acoustic Ceilings																							
 N01-112		ACT	PROC - ACOUSTIC CEILINGS - Buyout and Issue OAL		10	08-Apr-22	21-Apr-22	44															
 N01-212		ACT	PROC - ACOUSTIC CEILINGS - Review and Returned Signed OAL		5	22-Apr-22	28-Apr-22	44															
 A3870		ACT	PROC - ACOUSTIC CEILINGS - Issue Letter of Intent		1	29-Apr-22	29-Apr-22	44	-6														
 A3880		ACT	PROC - ACOUSTIC CEILINGS - Submittal - Prepare and Submit		20	02-May-22	27-May-22	44	-6														
 A3890		ACT	PROC - ACOUSTIC CEILINGS - Submittal - Review and Approve		10	31-May-22	13-Jun-22	44	-6														
 A3900		ACT	PROC - ACOUSTIC CEILINGS - Fab and Deliver (3 - 4 weeks)		20	14-Jun-22	12-Jul-22	44	-6														
Project ID: 2724 Printed: 05-Apr-22 21:05 Data Date: 03-Apr-22										 Remaining Work  Near Critical TF<10  Critical Remaining Work  Completed Work  Summary  Buffer  Due Date  Milestone  Near Critical Milestone  Critical Milestones  Actual Milestone  Summary Progress  Start Constraint  Expected Finish												Page 3 of 10	

Consigli Construction Company
Iona College - School of Health Sciences
A05 - Remaining Work with Last Update as of 03-Apr-22



Activity ID	PATH	RESP	Activity Name	MILE	Rem Dur	Start A=Actual	Finish A=Actual	Total Float	Change 3/20	2022												2 in	
										Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec					
09 6500 Flooring																							
N01-111		FLR	PROC - FLOORING - Buyout and Issue OAL		10	08-Apr-22	21-Apr-22	32															
N01-211		FLR	PROC - FLOORING - Review and Returned Signed OAL		5	22-Apr-22	28-Apr-22	32															
A3830		FLR	PROC - FLOORING - Issue Letter of Intent		1	29-Apr-22	29-Apr-22	32	-6														
A3840		FLR	PROC - FLOORING - Submittal - Prepare and Submit		20	02-May-22	27-May-22	32	-6														
A3850		FLR	PROC - FLOORING - Submittal - Review and Approve		10	31-May-22	13-Jun-22	32	-6														
A3860		FLR	PROC - FLOORING - Fab and Deliver		40	14-Jun-22	09-Aug-22	32	-6														
09 9100 Painting																							
N01-118		PAINT	PROC - PAINTING - Buyout and Issue OAL		10	08-Apr-22	21-Apr-22	39															
N01-218		PAINT	PROC - PAINTING - Review and Returned Signed OAL		5	22-Apr-22	28-Apr-22	39															
B1100		PAINT	PROC - PAINTING - Issue Letter of Intent		1	29-Apr-22	29-Apr-22	39	-6														
B1110		PAINT	PROC - PAINTING - Submittal - Prepare and Submit		20	02-May-22	27-May-22	39	-6														
B1120		PAINT	PROC - PAINTING - Submittal - Review and Approve		10	31-May-22	13-Jun-22	39	-6														
B1130		PAINT	PROC - PAINTING - Fab and Deliver		20	14-Jun-22	12-Jul-22	39	-6														
09 Acoustical Wall & Ceiling Panels																							
N01-113		APANEL	PROC - ACOUSTICAL PANELS - Buyout and Issue OAL		10	08-Apr-22	21-Apr-22	44															
N01-213		APANEL	PROC - ACOUSTICAL PANELS - Review and Returned Signed OAL		5	22-Apr-22	28-Apr-22	44															
A3910		APANEL	PROC - ACOUSTICAL PANELS - Issue Letter of Intent		1	29-Apr-22	29-Apr-22	44	-6														
A3920		APANEL	PROC - ACOUSTICAL PANELS - Submittal - Prepare and Submit		20	02-May-22	27-May-22	44	-6														
A3930		APANEL	PROC - ACOUSTICAL PANELS - Submittal - Review and Approve		10	31-May-22	13-Jun-22	44	-6														
A3940		APANEL	PROC - ACOUSTICAL PANELS - Fab and Deliver (10 - 11 weeks)		55	14-Jun-22	30-Aug-22	44	-6														
10 Specialties																							
10 Glass Railings																							
N01-107		RAIL	PROC - GLASS RAILINGS - Buyout and Issue OAL		10	08-Apr-22	21-Apr-22	55															
N01-207		RAIL	PROC - GLASS RAILINGS - Review and Returned Signed OAL		5	22-Apr-22	28-Apr-22	55															
A3670		RAIL	PROC - GLASS RAILINGS - Issue Letter of Intent		1	29-Apr-22	29-Apr-22	55	-6														
A3680		RAIL	PROC - GLASS RAILINGS - Submittal - Prepare and Submit		20	02-May-22	27-May-22	55	-6														
A3690		RAIL	PROC - GLASS RAILINGS - Submittal - Review and Approve		10	31-May-22	13-Jun-22	55	-6														
A3700		RAIL	PROC - GLASS RAILINGS - Fab and Deliver (10 to 16 weeks)		80	14-Jun-22	05-Oct-22	55	-6														
10 Operable Partitions																							
N01-114		PART	PROC - OPERABLE PARTITIONS - Buyout and Issue OAL		10	08-Apr-22	21-Apr-22	37															
N01-214		PART	PROC - OPERABLE PARTITIONS - Review and Returned Signed OAL		5	22-Apr-22	28-Apr-22	37															
A3950		PART	PROC - OPERABLE PARTITIONS - Issue Letter of Intent		1	29-Apr-22	29-Apr-22	37	-6														
A3960		PART	PROC - OPERABLE PARTITIONS - Submittal - Prepare and Submit		20	02-May-22	27-May-22	37	-6														
A3970		PART	PROC - OPERABLE PARTITIONS - Submittal - Review and Approve		10	31-May-22	13-Jun-22	37	-6														
A3980		PART	PROC - OPERABLE PARTITIONS - Fab and Deliver 10 - 12 weeks)		60	14-Jun-22	07-Sep-22	37	-6														
11 Equipment																							
11 Simulated Headwalls																							
N01-115		MILL	PROC - HEADWALLS - Buyout and Issue OAL		10	08-Apr-22	21-Apr-22	47															
N01-215		MILL	PROC - HEADWALLS - Review and Returned Signed OAL		5	22-Apr-22	28-Apr-22	47															
A3990		MILL	PROC - HEADWALLS - Issue Letter of Intent		1	29-Apr-22	29-Apr-22	47	-6														
A4000		MILL	PROC - HEADWALLS - Submittal - Prepare and Submit		20	02-May-22	27-May-22	47	-6														

Consigli Construction Company
Iona College - School of Health Sciences
A05 - Remaining Work with Last Update as of 03-Apr-22



Activity ID	PATH	RESP	Activity Name	MILE	Rem Dur	Start A=Actual	Finish A=Actual	Total Float	Change 3/20	2022												2 in
										Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec				
A4200	3	MECH	PROC - MECH - VRF UNITS - Submittal - Prepare and Submit		5	02-May-22	06-May-22	3	-14													
A4210	3	MECH	PROC - MECH - VRF UNITS - Submittal - Review and Approve		10	09-May-22	20-May-22	3	-14													
A4220	3	MECH	PROC - MECH - VRF UNITS - Fab and Deliver (10 - 12 Weeks)		55	23-May-22	09-Aug-22	3	-14													
MEP Controls / BMS																						
A4120		MECH	PROC - MECH - BMS - Submittal - Prepare and Submit		20	02-May-22	27-May-22	52	-14													
A4130		MECH	PROC - MECH - BMS - Submittal - Review and Approve		10	31-May-22	13-Jun-22	52	-14													
A4140		MECH	PROC - MECH - BMS - Fab and Deliver (7 - 10 Weeks)		50	14-Jun-22	23-Aug-22	52	-14													
26 Electrical																						
Buyout																						
N01-106	9	ELEC	PROC - ELEC - Buyout and Issue OAL		10	08-Apr-22	21-Apr-22	12														
N01-206	9	ELEC	PROC - ELEC - Review and Returned Signed OAL		5	22-Apr-22	28-Apr-22	12														
A2760	9	ELEC	PROC - ELEC - Issue Letter of Intent		1	29-Apr-22	29-Apr-22	12	-6													
Light Fixtures- Standard																						
A4240		ELEC	PROC - ELEC - FIXTURES STANDARD - Submittal - Prepare and Submit		20	02-May-22	27-May-22	32	-6													
A4250		ELEC	PROC - ELEC - FIXTURES STANDARD - Submittal - Review and Approve		10	31-May-22	13-Jun-22	32	-6													
A4260		ELEC	PROC - ELEC - FIXTURES STANDARD - Fab and Deliver (6 - 8 weeks)		40	14-Jun-22	09-Aug-22	32	-6													
Light Fixtures- Controls																						
A4280	9	ELEC	PROC - ELEC - FIXTURES CONTROLS - Submittal - Prepare and Submit		20	02-May-22	27-May-22	12	-6													
A4290	9	ELEC	PROC - ELEC - FIXTURES CONTROLS - Submittal - Review and Approve		10	31-May-22	13-Jun-22	12	-6													
A4300	9	ELEC	PROC - ELEC - FIXTURES CONTROLS - Fab and Deliver (8 - 12 Weeks)		60	14-Jun-22	07-Sep-22	12	-6													
Panelboards & Distribution Equipment																						
A4320	10	ELEC	PROC - ELEC - PANELBOARDS - Submittal - Prepare and Submit		15	02-May-22	20-May-22	12	-6													
A4330	10	ELEC	PROC - ELEC - PANELBOARDS - Submittal - Review and Approve		10	23-May-22	06-Jun-22	12	-6													
A4340	10	ELEC	PROC - ELEC - PANELBOARDS - Fab and Deliver (6 - 10 Weeks)		40	07-Jun-22	02-Aug-22	12	-6													
CONSTRUCTION																						
Roof Level																						
B1280	2	MECH	ROOF - MECH - DOAS - Install and Test		20	06-Oct-22	02-Nov-22	2	-14													
Facade																						
B1080	5	GLAS	FACADE - Window Replacement - West End		15	28-Jul-22	17-Aug-22	8	-21													
B1070	1	GLAS	FACADE - Window Replacement - East End		15	25-Aug-22	15-Sep-22	0	-21													
Lower Level - West Cl 6 (Classrooms)																						
Structure																						
N31-101	6	DEMO	LOWER - WEST - Structural Support Exterior Walls		5	01-Jun-22	07-Jun-22	8	-21													
A1880	6	DEMO	LOWER - WEST - Demo Existing Mezz Slab		15	08-Jun-22	28-Jun-22	8	-21													
Rough-Ins																						
Overhead (underside 2nd fl)																						
B1410			LOWER - WEST - ROUGH-IN - Concrete Stairs to Lower Level		5	23-Jun-22	29-Jun-22	31	-11													
B1400	6		LOWER - WEST - ROUGH-IN - Steel for Folding Partitions		5	29-Jun-22	06-Jul-22	8	-21													
A1970	6	FRAM	LOWER - WEST - ROUGH-IN - Frame Wall (to bottom 2nd Floor)		10	07-Jul-22	20-Jul-22	8	-21													
A1980		PLMB	LOWER - WEST - ROUGH-IN - OH Plumbing		10	21-Jul-22	03-Aug-22	13	-21													

Consigli Construction Company
Iona College - School of Health Sciences
A05 - Remaining Work with Last Update as of 03-Apr-22



Activity ID	PATH	RESP	Activity Name	MILE	Rem Dur	Start A=Actual	Finish A=Actual	Total Float	Change 3/20	2022												2 in
										Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec				
A2000		MECH	LOWER - WEST - ROUGH-IN - OH Mechanical		15	27-Jul-22	16-Aug-22	4	-14													
A2150		FIRE	LOWER - WEST - ROUGH-IN - OH Fire Protection		10	04-Aug-22	17-Aug-22	13	-21													
A1990		ELEC	LOWER - WEST - ROUGH-IN - OH Electric		15	10-Aug-22	30-Aug-22	4	-14													
A2180		INSP	LOWER - WEST - ROUGH-IN - OH Inspections		5	31-Aug-22	07-Sep-22	4	-14													
In-Walls																						
A2230	10	ELEC	LOWER - WEST - ROUGH-IN - In-Wall - Electric		10	27-Jul-22	09-Aug-22	12	-6													
A2010	10	INSP	LOWER - WEST - ROUGH-IN - In-Wall - Inspections		2	10-Aug-22	11-Aug-22	12	-6													
Classroom Finishes																						
A2020	5	DRY	LOWER - WEST - FINISHES - Walls - Drywall Ready for Paint		10	18-Aug-22	31-Aug-22	8	-10													
A2070	5	PAINT	LOWER - WEST - FINISHES - Walls - Prime & Paint First Coat		10	25-Aug-22	08-Sep-22	8	-10													
A2130		ACT	LOWER - WEST - FINISHES - Ceiling Grid		10	08-Sep-22	21-Sep-22	4	-14													
A2120		FIRE	LOWER - WEST - FINISHES - Sprinkler Heads		5	22-Sep-22	28-Sep-22	7	-14													
A2140		MECH	LOWER - WEST - FINISHES - Grills and Diffusers		5	22-Sep-22	28-Sep-22	7	-14													
A2080		ELEC	LOWER - WEST - FINISHES - Electrical Fixtures & Trim		10	20-Sep-22	03-Oct-22	4	-14													
A2110		ACT	LOWER - WEST - FINISHES - ACT Tile		5	04-Oct-22	10-Oct-22	4	-14													
A2100		PAINT	LOWER - WEST - FINISHES - Final Paint		5	11-Oct-22	17-Oct-22	11	-14													
A2160		FLR	LOWER - WEST - FINISHES - Flooring		10	11-Oct-22	24-Oct-22	4	-14													
B1330		WTRM	LOWER - WEST - FINISHES - Window Treatments		5	18-Oct-22	24-Oct-22	16	-14													
B1220		APANEL	LOWER - WEST - FINISHES - Accoutical Panels		10	18-Oct-22	31-Oct-22	11	-14													
A2090		DOOR	LOWER - WEST - FINISHES - Doors & Hardware		5	25-Oct-22	31-Oct-22	4	-14													
Closeout																						
A1950			LOWER - WEST - FINISH - Final Clean and Punchlist		5	01-Nov-22	07-Nov-22	11	-14													
A1960			LOWER - WEST - Construction Complete	L.3	0		07-Nov-22	11	-14													
Lower Level - East CI 6 (Student and Mech)																						
Structure																						
A1870		DEMO	LOWER - EAST - Selective Demos		5	10-May-22	16-May-22	47	-10													
Rough-Ins																						
Floor																						
A3460		DEMO	LOWER - EAST - FLOOR - Demo slab		3	17-May-22	19-May-22	47	-10													
A3470		PLMB	LOWER - EAST - FLOOR - Underslab Plumbing		2	14-Jun-22	15-Jun-22	31	-11													
A3480		CONC	LOWER - EAST - FLOOR - Conc Slab		5	16-Jun-22	22-Jun-22	31	-11													
Overhead																						
A1300	8	FRAM	LOWER - EAST - ROUGH-IN - Frame Wall		5	29-Jul-22	04-Aug-22	11	-6													
A1480		FIRE	LOWER - EAST - ROUGH-IN - OH Fire Protection		5	05-Aug-22	11-Aug-22	39	-6													
A1330	3	MECH	LOWER - EAST - ROUGH-IN - OH Mechanical		10	17-Aug-22	30-Aug-22	3	-14													
A1320	3	ELEC	LOWER - EAST - ROUGH-IN - OH Electric		10	24-Aug-22	07-Sep-22	3	-14													
A1530		INSP	LOWER - EAST - ROUGH-IN - OH Inspections		5	08-Sep-22	14-Sep-22	21	-14													
In-Walls																						
A1570		PLMB	LOWER - EAST - ROUGH-IN - In-Wall - Plumbing		5	05-Aug-22	11-Aug-22	26	-6													
A1580	3	ELEC	LOWER - EAST - ROUGH-IN - In-Wall - Electric		5	08-Sep-22	14-Sep-22	3	-14													
A1340	3	INSP	LOWER - EAST - ROUGH-IN - In-Wall - Inspections		3	15-Sep-22	19-Sep-22	3	-14													
Finishes																						

Report: A2724 05B Detailed Remaining Work MIN
TASK filter: 01 Remaining Work with LAST.

Consigli Construction Company
Iona College - School of Health Sciences
A05 - Remaining Work with Last Update as of 03-Apr-22



Activity ID	PATH	RESP	Activity Name	MILE	Rem Dur	Start A=Actual	Finish A=Actual	Total Float	Change 3/20	2022												2 in
										Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec				
A1490		FLR	LOWER - EAST - FINISHES - Flooring		5	10-Aug-22	16-Aug-22	43	-6													
A1370		MILL	LOWER - EAST - FINISHES - Millwork		5	17-Aug-22	23-Aug-22	43	-6													
A1420		DOOR	LOWER - EAST - FINISHES - Doors & Hardware		5	24-Aug-22	30-Aug-22	47	-6													
A1430		PAINT	LOWER - EAST - FINISHES - Final Paint		5	24-Aug-22	30-Aug-22	43	-6													
B1340		WTRM	LOWER - EAST - FINISHES - Window Treatments		5	08-Sep-22	14-Sep-22	38	-6													
A1350	3	DRY	LOWER - EAST - FINISHES - Walls - Drywall Ready for Paint		10	20-Sep-22	03-Oct-22	3	-14													
A1400	3	PAINT	LOWER - EAST - FINISHES - Walls - Prime & Paint First Coat		5	04-Oct-22	10-Oct-22	3	-14													
A1460	3	ACT	LOWER - EAST - FINISHES - Ceiling Grid		5	11-Oct-22	17-Oct-22	3	-14													
A1450		FIRE	LOWER - EAST - FINISHES - Sprinkler Heads		5	18-Oct-22	24-Oct-22	6	-14													
A1470		MECH	LOWER - EAST - FINISHES - Grills and Diffusers		5	18-Oct-22	24-Oct-22	6	-14													
A1410	3	ELEC	LOWER - EAST - FINISHES - Electrical Fixtures & Trim		10	14-Oct-22	27-Oct-22	3	-14													
A1440	3	ACT	LOWER - EAST - FINISHES - ACT Tile		3	28-Oct-22	01-Nov-22	3	-14													
Bathroom Finishes																						
A1620		TILE	LOWER - EAST - BATH FINISHES - Ceramic Tile		3	11-Oct-22	13-Oct-22	10	-14													
A1380		MILL	LOWER - EAST - BATH FINISHES - Millwork		2	14-Oct-22	17-Oct-22	10	-14													
A1600		PLMB	LOWER - EAST - BATH FINISHES - Plumbing Fixtures		2	18-Oct-22	19-Oct-22	10	-14													
A1390		TPAR	LOWER - EAST - BATH FINISHES - Accessories		3	20-Oct-22	24-Oct-22	10	-14													
Mechanical and Electrical Rooms																						
B1290		MECH	LOWER - EAST - MECH RM - Framing and roughins		10	23-Jun-22	07-Jul-22	61	-41													
B1300		ELEC	LOWER - EAST - ELEC RM - Fit out		25	08-Jul-22	11-Aug-22	61	51													
B1420	4	ELEC	LOWER - EAST - ELEC RM - Shutdown / Switchover		2	15-Nov-22	16-Nov-22	7														
Closeout																						
A1280			LOWER - EAST - FINISH - Final Clean and Punchlist		9	02-Nov-22	14-Nov-22	4	-10													
A1290			LOWER - EAST - Construction Complete	L.3	0		14-Nov-22	4	-10													
First Floor - East CI 6 (Lobby, Group Therapy, and Faculty)																						
Structure																						
A3490		DEMO	FIRST - EAST - Selective Demo		5	03-May-22*	09-May-22	47	-10													
Rough-Ins																						
Overhead																						
A3160	8	FRAM	FIRST - EAST - ROUGH-IN - Frame Wall		5	22-Jul-22	28-Jul-22	11	-6													
A3340		FIRE	FIRST - EAST - ROUGH-IN - OH Fire Protection		5	29-Jul-22	04-Aug-22	39	-6													
A3190	3	MECH	FIRST - EAST - ROUGH-IN - OH Mechanical		10	10-Aug-22	23-Aug-22	3	-14													
A3180		ELEC	FIRST - EAST - ROUGH-IN - OH Electric		10	17-Aug-22	30-Aug-22	4	-14													
A3370		INSP	FIRST - EAST - ROUGH-IN - OH Inspections		5	31-Aug-22	07-Sep-22	21	-14													
In-Walls																						
A3420		ELEC	FIRST - EAST - ROUGH-IN - In-Wall - Electric		5	31-Aug-22	07-Sep-22	4	-14													
A3200		INSP	FIRST - EAST - ROUGH-IN - In-Wall - Inspections		2	08-Sep-22	09-Sep-22	4	-14													
Finishes																						
A3210	1	DRY	FIRST - EAST - FINISHES - Walls - Drywall Ready for Paint		10	16-Sep-22	29-Sep-22	0	-18													
A3260	1	PAINT	FIRST - EAST - FINISHES - Walls - Prime & Paint First Coat		5	30-Sep-22	06-Oct-22	0	-18													
A3320	1	ACT	FIRST - EAST - FINISHES - Ceiling Grid		5	07-Oct-22	13-Oct-22	0	-18													
A3270	1	ELEC	FIRST - EAST - FINISHES - Electrical Fixtures & Trim		5	14-Oct-22	20-Oct-22	0	-18													

Project ID: 2724
Printed: 05-Apr-22 21:05
Data Date: 03-Apr-22

Remaining Work Near Critical TF<10 Critical Remaining Work Completed Work Summary Buffer Due Date
 Milestone Near Critical Milestone Critical Milestones Actual Milestone Summary Progress Start Constraint Expected Finish

Consigli Construction Company
Iona College - School of Health Sciences
A05 - Remaining Work with Last Update as of 03-Apr-22



Activity ID	PATH	RESP	Activity Name	MILE	Rem Dur	Start A=Actual	Finish A=Actual	Total Float	Change 3/20	2022												2 in		
										Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec						
A3310		FIRE	FIRST - EAST - FINISHES - Sprinkler Heads		5	14-Oct-22	20-Oct-22	8	-18															
A3330		MECH	FIRST - EAST - FINISHES - Grills and Diffusers		5	14-Oct-22	20-Oct-22	8	-18															
A3300		ACT	FIRST - EAST - FINISHES - ACT Tile		3	21-Oct-22	25-Oct-22	8	-18															
A3350	1	FLR	FIRST - EAST - FINISHES - Flooring		5	21-Oct-22	27-Oct-22	0	-18															
A3230	1	MILL	FIRST - EAST - FINISHES - Millwork		5	28-Oct-22	03-Nov-22	0	-18															
A3280		DOOR	FIRST - EAST - FINISHES - Doors & Hardware		5	28-Oct-22	03-Nov-22	1	-18															
A3290	1	PAINT	FIRST - EAST - FINISHES - Final Paint		5	04-Nov-22	10-Nov-22	0	-18															
B1350	1	WTRM	FIRST - EAST - FINISHES - Window Treatments		5	07-Nov-22	11-Nov-22	0	-18															
Lobby																								
B1310		STOR	FIRST - EAST - LOBBY - Entrance Storefront - Install		5	07-Oct-22	13-Oct-22	15	-18															
B1320		MILL	FIRST - EAST - LOBBY - Reception Desk		5	28-Oct-22	03-Nov-22	6	-18															
Closeout																								
A3140	1		FIRST - EAST - FINISH - Final Clean and Punchlist		5	14-Nov-22	18-Nov-22	0	-18															
A3150	1		FIRST - EAST - Construction Complete	L.3	0		18-Nov-22	0	-18															
2nd Floor Level																								
Structure																								
A2610		DEMO	SECOND - Selective Demo		10	03-May-22*	16-May-22	47	-20															
Rough-Ins																								
Overhead																								
A2300	8	FRAM	SECOND - ROUGH-IN - Frame Wall		10	08-Jul-22	21-Jul-22	11	-6															
A2480		FIRE	SECOND - ROUGH-IN - OH Fire Protection		10	22-Jul-22	04-Aug-22	40	-6															
A2330	3	MECH	SECOND - ROUGH-IN - OH Mechanical		15	27-Jul-22	16-Aug-22	3	-14															
A2320		ELEC	SECOND - ROUGH-IN - OH Electric		10	10-Aug-22	23-Aug-22	7	-14															
A2510		INSP	SECOND - ROUGH-IN - OH Inspections		5	24-Aug-22	30-Aug-22	27	-14															
In-Walls																								
A2560		ELEC	SECOND - ROUGH-IN - In-Wall - Electric		5	24-Aug-22	30-Aug-22	7	-14															
A2340		INSP	SECOND - ROUGH-IN - In-Wall - Inspections		5	31-Aug-22	07-Sep-22	7	-14															
Finishes																								
A2490		FLR	SECOND - FINISHES - Flooring		10	10-Aug-22	23-Aug-22	32	-6															
A2370		MILL	SECOND - FINISHES - Millwork		10	24-Aug-22	07-Sep-22	32	-6															
A2420		DOOR	SECOND - FINISHES - Doors & Hardware		10	24-Aug-22	07-Sep-22	42	-6															
B1230		PART	SECOND - FINISHES - Folding Partition		10	08-Sep-22	21-Sep-22	37	-6															
A2350		DRY	SECOND - FINISHES - Walls - Drywall Ready for Paint		10	16-Sep-22	29-Sep-22	1	-20															
A2400		PAINT	SECOND - FINISHES - Walls - Prime & Paint First Coat		5	30-Sep-22	06-Oct-22	1	-20															
A2460		ACT	SECOND - FINISHES - Ceiling Grid		5	07-Oct-22	13-Oct-22	1	-20															
A2500		MILL	SECOND - FINISHES - Headwalls		10	07-Oct-22	20-Oct-22	1	-20															
A2450		FIRE	SECOND - FINISHES - Sprinkler Heads		5	14-Oct-22	20-Oct-22	6	-20															
A2470		MECH	SECOND - FINISHES - Grills and Diffusers		5	14-Oct-22	20-Oct-22	6	-20															
A2410		ELEC	SECOND - FINISHES - Electrical Fixtures & Trim		10	14-Oct-22	27-Oct-22	1	-20															
A2430		PAINT	SECOND - FINISHES - Final Paint		5	21-Oct-22	27-Oct-22	1	-20															
A2440		ACT	SECOND - FINISHES - ACT Tile		5	28-Oct-22	03-Nov-22	1	-20															
B1360		WTRM	SECOND - FINISHES - Window Treatments		10	28-Oct-22	10-Nov-22	1	-20															

Consigli Construction Company
Iona College - School of Health Sciences
A05 - Remaining Work with Last Update as of 03-Apr-22



Activity ID	PATH	RESP	Activity Name	MILE	Rem Dur	Start A=Actual	Finish A=Actual	Total Float	Change 3/20	2022											2 in		
											Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec				
 Closeout																							
 A2280			SECOND - FINISH - Final Clean and Punchlist		5	11-Nov-22	17-Nov-22	1	-20														
 A2290			SECOND - Construction Complete	L.3	0		17-Nov-22	1	-20														
 Start-Up and Commissioning																							
 A2620			MEP Start-Up and Commisioning		10	04-Nov-22	17-Nov-22	1	-15														
 A2630	1		Life Safety Walk thrus		5	21-Nov-22	29-Nov-22	0	-14														
