


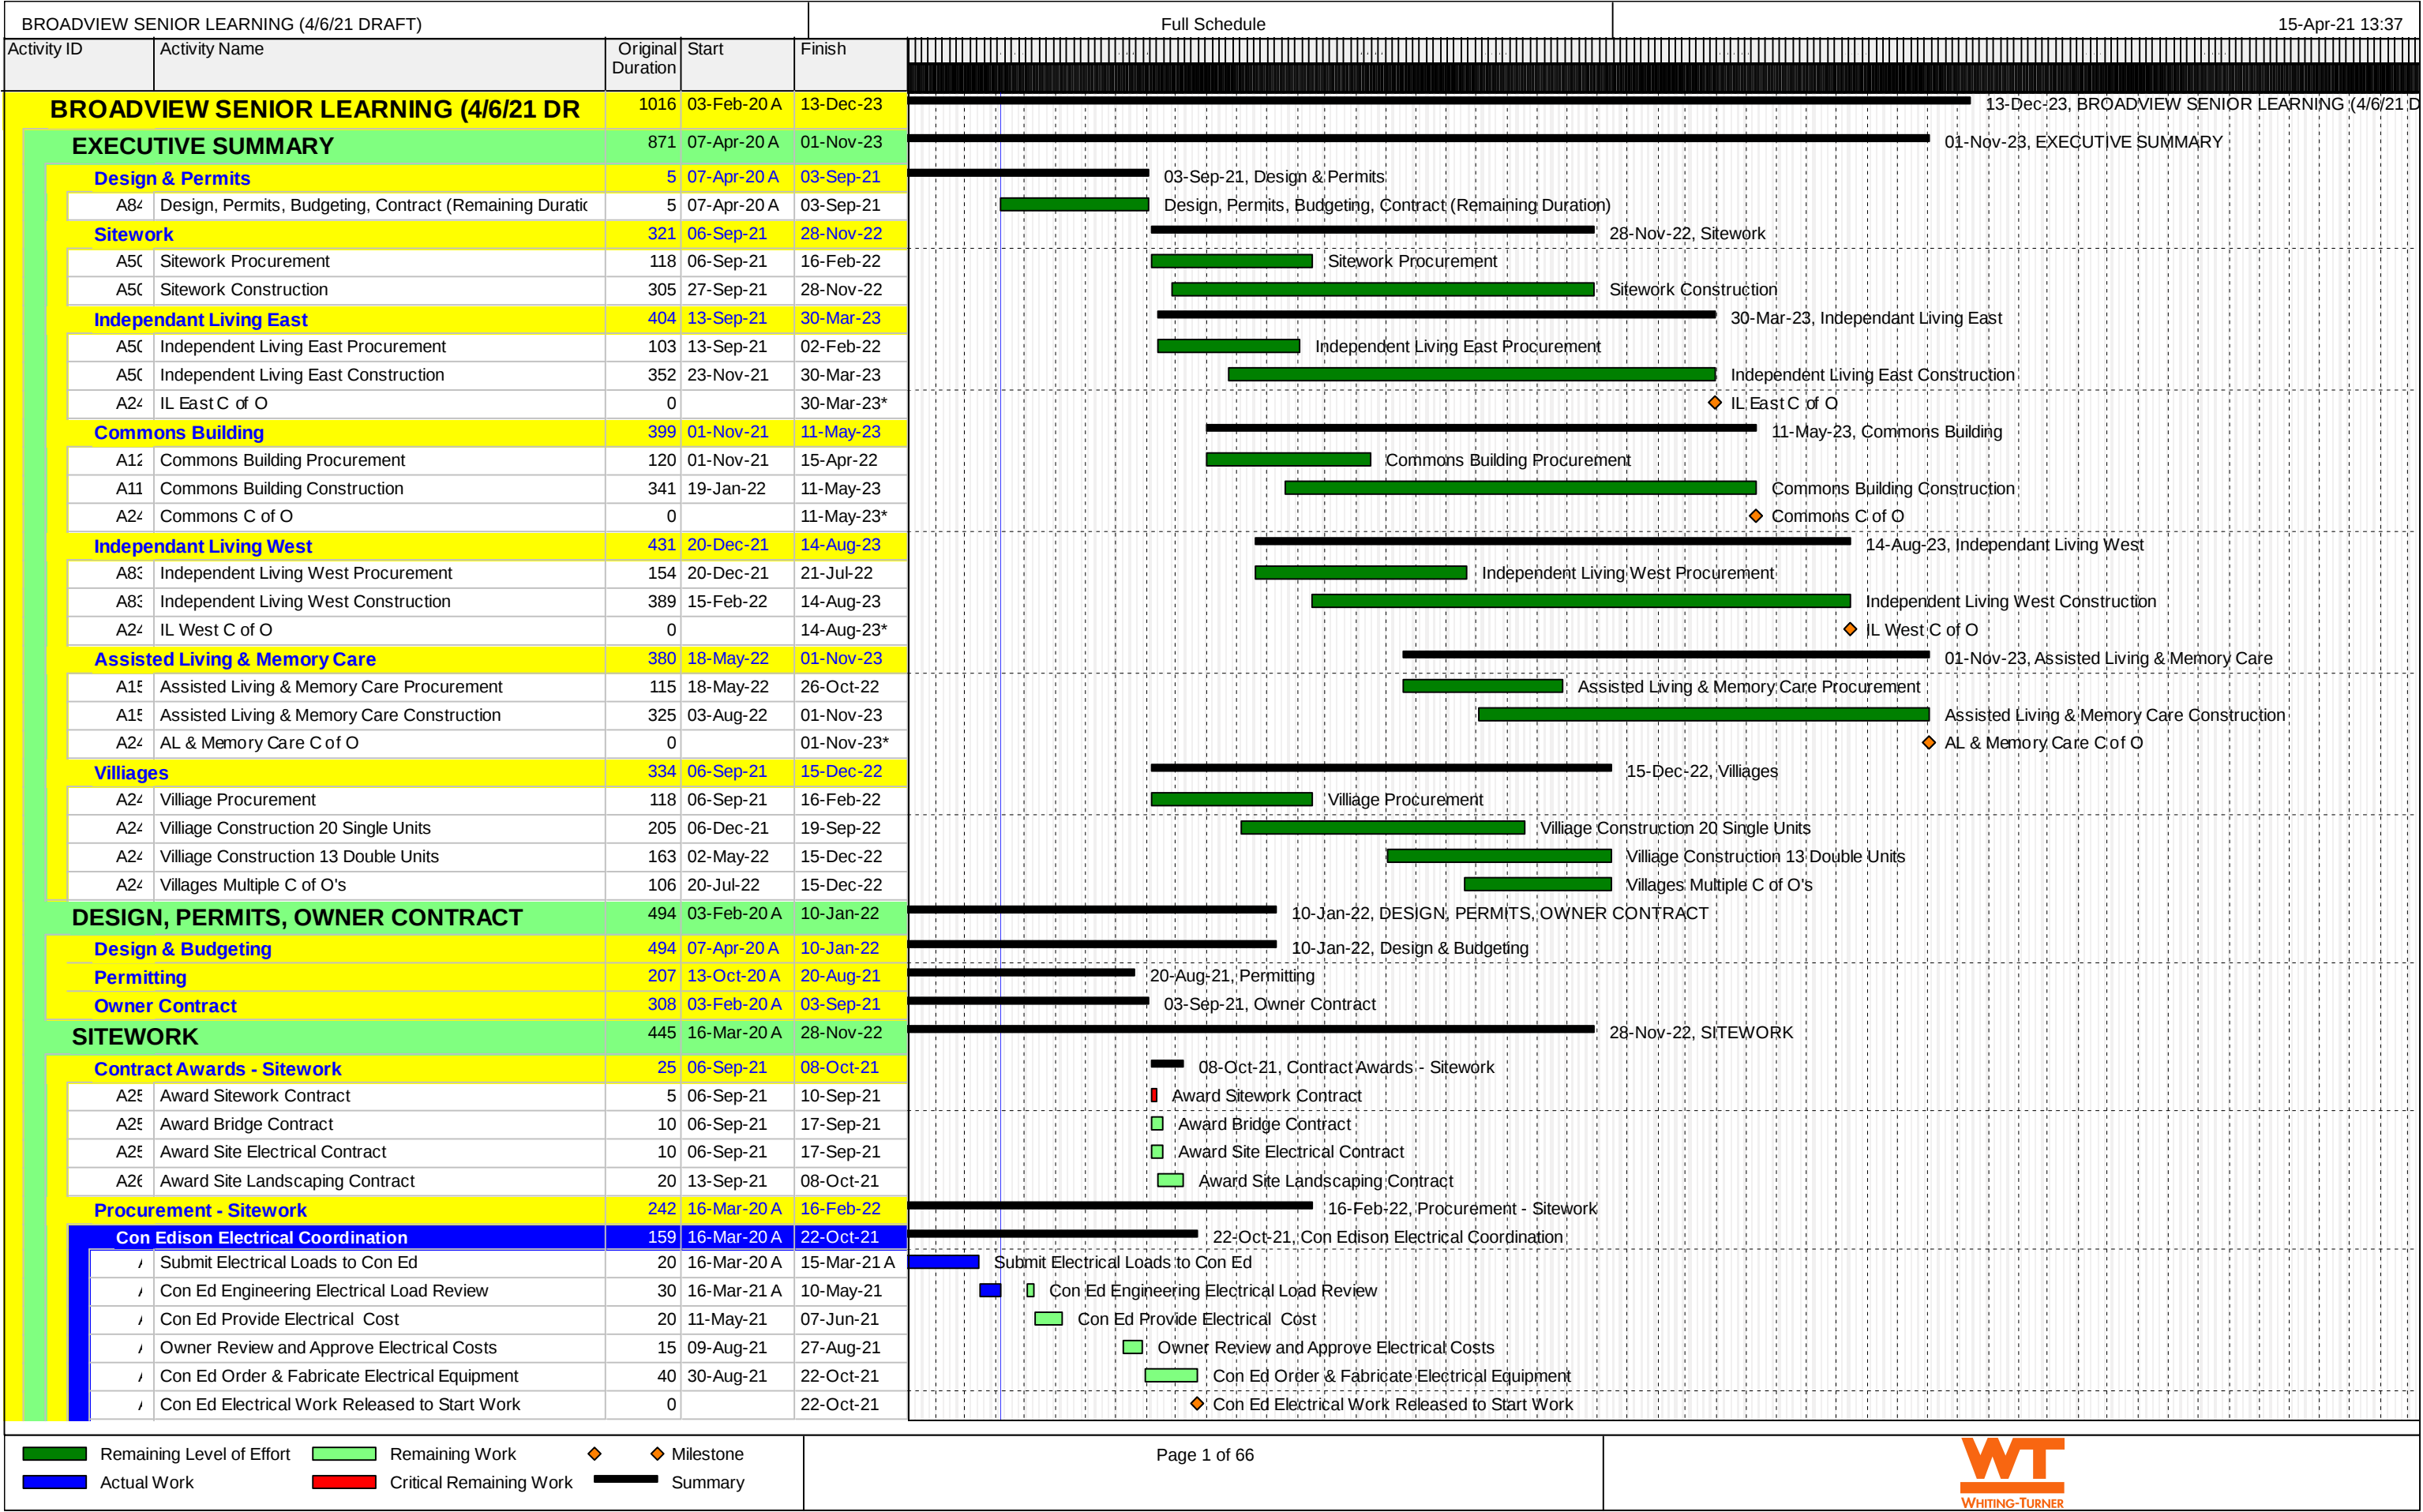

BROADVIEW SENIOR LEARNING (4/6/21 DRAFT)					Full Schedule	15-Apr-21 13:37
Activity ID	Activity Name	Original Duration	Start	Finish		
	Con Edison Gas Coordination		126	03-May-21	25-Oct-21	25-Oct-21, Con Edison Gas Coordination
	/	Submit Gas Loads to Con Ed	20	03-May-21	28-May-21	Submit Gas Loads to Con Ed
	/	Con Ed Engineering Gas Load Review	30	31-May-21	09-Jul-21	Con Ed Engineering Gas Load Review
	/	Con Ed Provide Gas Cost	20	12-Jul-21	06-Aug-21	Con Ed Provide Gas Cost
	/	Owner Review and Approve Gas Costs	15	09-Aug-21	27-Aug-21	Owner Review and Approve Gas Costs
	/	Con Ed Order & Fabricate Gas Equipment	40	30-Aug-21	22-Oct-21	Con Ed Order & Fabricate Gas Equipment
	/	Con Ed Gas Work Released to Start Work	1	25-Oct-21	25-Oct-21	Con Ed Gas Work Released to Start Work
	Earthwork		15	07-Sep-21	27-Sep-21	27-Sep-21, Earthwork
	f	Submit SWPPP	5	07-Sep-21	13-Sep-21	Submit SWPPP
	f	Review & Approve SWPPP	5	14-Sep-21	20-Sep-21	Review & Approve SWPPP
	f	Fabricate & Deliver SWPPP	5	21-Sep-21	27-Sep-21	Fabricate & Deliver SWPPP
	Site Improvements		55	13-Sep-21	30-Nov-21	30-Nov-21, Site Improvements
	f	Submit MSE Retaining Wall	10	13-Sep-21	24-Sep-21	Submit MSE Retaining Wall
	f	Review & Approve MSE Retaining Wall	15	27-Sep-21	15-Oct-21	Review & Approve MSE Retaining Wall
	f	Fabricate & Deliver MSE Retaining Wall	30	18-Oct-21	30-Nov-21	Fabricate & Deliver MSE Retaining Wall
	Utilities (Submittals)		55	13-Sep-21	30-Nov-21	30-Nov-21, Utilities (Submittals)
	f	Submit Sanitary, Storm, Water Piping & Structures	10	13-Sep-21	24-Sep-21	Submit Sanitary, Storm, Water Piping & Structures
	f	Review & Approve Sanitary, Storm, Water Piping & Struc	15	27-Sep-21	15-Oct-21	Review & Approve Sanitary, Storm, Water Piping & Structures
	f	Fabricate & Deliver Sanitary, Storm, Water Piping & Struc	30	18-Oct-21	30-Nov-21	Fabricate & Deliver Sanitary, Storm, Water Piping & Structures
	Bridge Procurement		105	20-Sep-21	16-Feb-22	16-Feb-22, Bridge Procurement
	f	Submit Bridge Components	30	20-Sep-21	29-Oct-21	Submit Bridge Components
	f	Review & Approve Bridge Components	15	01-Nov-21	19-Nov-21	Review & Approve Bridge Components
	f	Fabricate & Deliver Bridge Components	60	22-Nov-21	16-Feb-22	Fabricate & Deliver Bridge Components
	Site Electrical		105	20-Sep-21	16-Feb-22	16-Feb-22, Site Electrical
	f	Submit Site Electrical Feeders & Equipment	30	20-Sep-21	29-Oct-21	Submit Site Electrical Feeders & Equipment
	f	Review & Approve Site Electrical Feeders & Equipment	15	01-Nov-21	19-Nov-21	Review & Approve Site Electrical Feeders & Equipment
	f	Fabricate & Deliver Site Electrical Feeders & Equipment	60	22-Nov-21	16-Feb-22	Fabricate & Deliver Site Electrical Feeders & Equipment
	Site Lighting		100	20-Sep-21	09-Feb-22	09-Feb-22, Site Lighting
	f	Submit Site Lighting	25	20-Sep-21	22-Oct-21	Submit Site Lighting
	f	Review & Approve Site Lighting	15	25-Oct-21	12-Nov-21	Review & Approve Site Lighting
	f	Fabricate & Deliver Site Lighting	60	15-Nov-21	09-Feb-22	Fabricate & Deliver Site Lighting
	Landscaping		60	11-Oct-21	05-Jan-22	05-Jan-22, Landscaping
	f	Submit Landscaping	15	11-Oct-21	29-Oct-21	Submit Landscaping
	f	Review & Approve Landscaping	15	01-Nov-21	19-Nov-21	Review & Approve Landscaping
	f	Fabricate & Deliver Landscaping	30	22-Nov-21	05-Jan-22	Fabricate & Deliver Landscaping
	Construction - Sitework		305	27-Sep-21	28-Nov-22	28-Nov-22, Construction - Sitework
	Mobilization		85	27-Sep-21	24-Jan-22	24-Jan-22, Mobilization
	/	Mobilize, & Install SWPPP	20	27-Sep-21	25-Oct-21	Mobilize, & Install SWPPP
	/	Mobilize Site Offices	20	27-Sep-21	25-Oct-21	Mobilize Site Offices
	/	Clear & Grub @ Roadways	10	25-Oct-21	08-Nov-21	Clear & Grub @ Roadways
/	Strip Topsoil @ Roadways	15	08-Nov-21	29-Nov-21	Strip Topsoil @ Roadways	
/	Cut & Fill @ Roadways	20	29-Nov-21	27-Dec-21	Cut & Fill @ Roadways	
/	Rough Grade Roadways	20	27-Dec-21	24-Jan-22	Rough Grade Roadways	
Village Sitework		50	25-Oct-21	03-Jan-22	03-Jan-22, Village Sitework	
/	Clear & Grub @ Village Area	10	25-Oct-21	08-Nov-21	Clear & Grub @ Village Area	
/	Strip Topsoil Screen & Stock pile @ Village Area	10	08-Nov-21	22-Nov-21	Strip Topsoil Screen & Stock pile @ Village Area	
/	Cut/Fill & Rough Grade @ Village Area	10	22-Nov-21	06-Dec-21	Cut/Fill & Rough Grade @ Village Area	
/	Fine Grade @ Village Area	10	06-Dec-21	20-Dec-21	Fine Grade @ Village Area	
Remaining Level of Effort		Remaining Work		Milestone		
Actual Work		Critical Remaining Work		Summary		
Page 2 of 66					WT WHITING-TURNER	

BROADVIEW SENIOR LEARNING (4/6/21 DRAFT)					Full Schedule		15-Apr-21 13:37
Activity ID	Activity Name	Original Duration	Start	Finish			
	/ Landscaping @ Village Area (Roadside Only)	20	06-Dec-21	03-Jan-22	Landscaping @ Village Area (Roadside Only)		
	/ Above Ground Detention & Bioswale @ Village	20	06-Dec-21	03-Jan-22	Above Ground Detention & Bioswale @ Village		
	Independent Living Complex Sitework	91	25-Oct-21	01-Mar-22	01-Mar-22, Independent Living Complex Sitework		
	/ Clear & Grub Senior Living Area	8	25-Oct-21	04-Nov-21	Clear & Grub Senior Living Area		
	/ Strip Topsoil @ Senior Living Area	5	04-Nov-21	11-Nov-21	Strip Topsoil @ Senior Living Area		
	/ Cut/Fill Rough Grade Senior Living Area	8	11-Nov-21	23-Nov-21	Cut/Fill Rough Grade Senior Living Area		
	/ Above Ground Detention & Bioswale @ SLA	20	23-Nov-21	21-Dec-21	Above Ground Detention & Bioswale @ SLA		
	/ Parking Lots @ Senior Living Area	50	21-Dec-21	01-Mar-22	Parking Lots @ Senior Living Area		
	Site Sanitary	60	30-Nov-21	22-Feb-22	22-Feb-22, Site Sanitary		
	/ Sanitary Mains & Structures	60	30-Nov-21	22-Feb-22	Sanitary Mains & Structures		
	Site Drainage	90	27-Dec-21	02-May-22	02-May-22, Site Drainage		
	/ Site Drainage Structures & Piping	30	27-Dec-21	07-Feb-22	Site Drainage Structures & Piping		
	/ Underground Detention	30	07-Feb-22	21-Mar-22	Underground Detention		
	/ Open Detention & Bioswales	30	21-Mar-22	02-May-22	Open Detention & Bioswales		
	Road B Bridge	45	16-Feb-22	20-Apr-22	20-Apr-22, Road B Bridge		
	/ Prep Bridge Pad	10	16-Feb-22	02-Mar-22	Prep Bridge Pad		
	/ Bridge Structure	35	02-Mar-22	20-Apr-22	Bridge Structure		
	Site Utilities	80	16-Feb-22	08-Jun-22	08-Jun-22, Site Utilities		
	/ Electrical Distribution (Primary Feeders)	60	16-Feb-22	11-May-22	Electrical Distribution (Primary Feeders)		
	/ Water Mains	50	22-Feb-22	03-May-22	Water Mains		
	/ Gas Mains	15	20-Apr-22	11-May-22	Gas Mains		
	/ Electrical Distribution (Secondary Feeders to IL, AL, CMI	20	11-May-22	08-Jun-22	Electrical Distribution (Secondary Feeders to IL, AL, CMNS)		
	Landmark Sitework	75	02-May-22	15-Aug-22	15-Aug-22, Landmark Sitework		
	/ Cut/Fill & Rough Grade @ Landmark Area	30	02-May-22	13-Jun-22	Cut/Fill & Rough Grade @ Landmark Area		
	/ Drainage & Utilities @ Landmark area	20	13-Jun-22	11-Jul-22	Drainage & Utilities @ Landmark area		
	/ Above Ground Detention & Bioswale @ Landmark Area	20	13-Jun-22	11-Jul-22	Above Ground Detention & Bioswale @ Landmark Area		
	/ MSE Retaining Walls @ Landmark Area	25	13-Jun-22	18-Jul-22	MSE Retaining Walls @ Landmark Area		
	/ Final Grading & Topsoil @ Landmark Area	20	18-Jul-22	15-Aug-22	Final Grading & Topsoil @ Landmark Area		
	Roadways	50	11-May-22	20-Jul-22	20-Jul-22, Roadways		
	/ Curbs & Lighting	20	11-May-22	08-Jun-22	Curbs & Lighting		
	/ Fine Grade Roadways	10	08-Jun-22	22-Jun-22	Fine Grade Roadways		
	/ Paving & Striping @ Roadways	10	22-Jun-22	06-Jul-22	Paving & Striping @ Roadways		
	/ Signage @ Roadways	10	06-Jul-22	20-Jul-22	Signage @ Roadways		
	Site Landscaping	93	20-Jul-22	28-Nov-22	28-Nov-22, Site Landscaping		
	/ Roadway Landscaping & Topsoil	30	20-Jul-22	31-Aug-22	Roadway Landscaping & Topsoil		
	/ Landscaping @ Landmark Area	60	15-Aug-22	07-Nov-22	Landscaping @ Landmark Area		
	/ Final Grading & Topsoil @ Senior Living Area	30	03-Oct-22	14-Nov-22	Final Grading & Topsoil @ Senior Living Area		
	/ Landscaping @ Senior Living Area	40	03-Oct-22	28-Nov-22	Landscaping @ Senior Living Area		
	/ Sitework Substantially Complete	0		28-Nov-22	Sitework Substantially Complete		
	INDEPENDENT LIVING BUILDING EAST	409	06-Sep-21	30-Mar-23	30-Mar-23, INDEPENDENT LIVING BUILDING EAST		
	Contract Awards - IL East	40	06-Sep-21	29-Oct-21	29-Oct-21, Contract Awards - IL East		
	A27 Award IL Building East Hambro Contract	5	06-Sep-21	10-Sep-21	Award IL Building East Hambro Contract		
	A27 Award IL Building East Electrical Contract	5	06-Sep-21	10-Sep-21	Award IL Building East Electrical Contract		
	A27 Award IL Building East Plumbing Contract	5	06-Sep-21	10-Sep-21	Award IL Building East Plumbing Contract		
	A26 Award IL Building East Excavation Contract	5	13-Sep-21	17-Sep-21	Award IL Building East Excavation Contract		
	A27 Award IL Building East Concrete Contract	5	13-Sep-21	17-Sep-21	Award IL Building East Concrete Contract		
	A27 Award IL Building East Carpentry Contract	5	13-Sep-21	17-Sep-21	Award IL Building East Carpentry Contract		
	A27 Award IL Building East HVAC Contract	5	13-Sep-21	17-Sep-21	Award IL Building East HVAC Contract		
Remaining Level of Effort Actual Work					Remaining Work Critical Remaining Work		Milestone Summary
					Page 3 of 66		WT WHITING-TURNER

BROADVIEW SENIOR LEARNING (4/6/21 DRAFT)					Full Schedule	15-Apr-21 13:37
Activity ID	Activity Name	Original Duration	Start	Finish		
	A27 Award IL Building East Glazing & Windows Contract	5	13-Sep-21	17-Sep-21	<	

[illegible]

[illegible]

BROADVIEW SENIOR LEARNING (4/6/21 DRAFT)					Full Schedule	15-Apr-21 13:37																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
Activity ID	Activity Name	Original Duration	Start	Finish																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										</

BROADVIEW SENIOR LEARNING (4/6/21 DRAFT)					Full Schedule		15-Apr-21 13:37
Activity ID	Activity Name	Original Duration	Start	Finish			
	Fabricate & Deliver Fire Protection Pump	40	06-Jan-22	02-Mar-22		Fabricate & Deliver Fire Protection Pump	
	HVAC	70	29-Nov-21	07-Mar-22		07-Mar-22, HVAC	
	Submit HVAC Ductwork Model	15	29-Nov-21	17-Dec-21		Submit HVAC Ductwork Model	
	Submit HVAC Equipment	15	29-Nov-21	17-Dec-21		Submit HVAC Equipment	
	Review & Approve HVAC Equipment	15	20-Dec-21	10-Jan-22		Review & Approve HVAC Equipment	
	Fabricate & Deliver HVAC Equipment	40	11-Jan-22	07-Mar-22		Fabricate & Deliver HVAC Equipment	
	Final Review & Approve HVAC Ductwork Model	10	21-Jan-22	03-Feb-22		Final Review & Approve HVAC Ductwork Model	
	Fabricate & Deliver Ductwork	15	04-Feb-22	24-Feb-22		Fabricate & Deliver Ductwork	
	Radiant Panel Ceilings	85	29-Nov-21	28-Mar-22		28-Mar-22, Radiant Panel Ceilings	
	Submit Radiant Panel Ceilings	20	29-Nov-21	27-Dec-21		Submit Radiant Panel Ceilings	
	Review & Approve Radiant Panel Ceilings	15	28-Dec-21	17-Jan-22		Review & Approve Radiant Panel Ceilings	
	Fabricate & Deliver Radiant Panel Ceilings	50	18-Jan-22	28-Mar-22		Fabricate & Deliver Radiant Panel Ceilings	
	Convenience Store Equipment	85	20-Dec-21	18-Apr-22		18-Apr-22, Convenience Store Equipment	
	Submit Convenience Store Equipment	20	20-Dec-21	17-Jan-22		Submit Convenience Store Equipment	
	Review & Approve Convenience Store Equipment	15	18-Jan-22	07-Feb-22		Review & Approve Convenience Store Equipment	
	Fabricate & Deliver Convenience Store Equipment	50	08-Feb-22	18-Apr-22		Fabricate & Deliver Convenience Store Equipment	
	Mailroom Equipment	85	20-Dec-21	18-Apr-22		18-Apr-22, Mailroom Equipment	
	Submit Mailroom Equipment	20	20-Dec-21	17-Jan-22		Submit Mailroom Equipment	
	Review & Approve Mailroom Equipment	15	18-Jan-22	07-Feb-22		Review & Approve Mailroom Equipment	
	Fabricate & Deliver Mailroom Equipment	50	08-Feb-22	18-Apr-22		Fabricate & Deliver Mailroom Equipment	
	Locker Room Equipment	85	20-Dec-21	18-Apr-22		18-Apr-22, Locker Room Equipment	
	Submit Locker Room Equipment	20	20-Dec-21	17-Jan-22		Submit Locker Room Equipment	
	Review & Approve Locker Room Equipment	15	18-Jan-22	07-Feb-22		Review & Approve Locker Room Equipment	
	Fabricate & Deliver Locker Room Equipment	50	08-Feb-22	18-Apr-22		Fabricate & Deliver Locker Room Equipment	
	Laundry Equipment	85	20-Dec-21	18-Apr-22		18-Apr-22, Laundry Equipment	
	Submit Laundry Room Equipment	20	20-Dec-21	17-Jan-22		Submit Laundry Room Equipment	
	Review & Approve Laundry Room Equipment	15	18-Jan-22	07-Feb-22		Review & Approve Laundry Room Equipment	
	Fabricate & Deliver Laundry Room Equipment	50	08-Feb-22	18-Apr-22		Fabricate & Deliver Laundry Room Equipment	
	Woodworking Equipment	85	20-Dec-21	18-Apr-22		18-Apr-22, Woodworking Equipment	
	Submit Woodworking Equipment	20	20-Dec-21	17-Jan-22		Submit Woodworking Equipment	
	Review & Approve Woodworking Equipment	15	18-Jan-22	07-Feb-22		Review & Approve Woodworking Equipment	
	Fabricate & Deliver Woodworking Equipment	50	08-Feb-22	18-Apr-22		Fabricate & Deliver Woodworking Equipment	
	Construction - Commons Building	306	19-Jan-22	23-Mar-23		23-Mar-23, Construction - Commons Building	
	Structure - Commons Building	184	19-Jan-22	04-Oct-22		04-Oct-22, Structure - Commons Building	
	Foundations - Commons Building	70	19-Jan-22	27-Apr-22		27-Apr-22, Foundations - Commons Building	
	Foundation Excavation @ Commons	15	19-Jan-22	09-Feb-22		Foundation Excavation @ Commons	
	Form & Pour Footings & Walls @ Commons	25	26-Jan-22	02-Mar-22		Form & Pour Footings & Walls @ Commons	
	Excavate Pool @ Commons	5	09-Feb-22	16-Feb-22		Excavate Pool @ Commons	
	Form & Pour Pool & Commons	15	16-Feb-22	09-Mar-22		Form & Pour Pool & Commons	
	Foundation Backfill @ Commons	10	02-Mar-22	16-Mar-22		Foundation Backfill @ Commons	
	Masonry Partitions (LL to Roof Level) Commons	25	02-Mar-22	06-Apr-22		Masonry Partitions (LL to Roof Level) Commons	
	Backfill & Prep Pool Deck Area @ Commons	5	09-Mar-22	16-Mar-22		Backfill & Prep Pool Deck Area @ Commons	
	Underground Utilities @ Commons	10	17-Mar-22	31-Mar-22		Underground Utilities @ Commons	
	Prep, Form, & Pour SOG @ Commons	15	06-Apr-22	27-Apr-22		Prep, Form, & Pour SOG @ Commons	
	Structure - Commons Building	79	27-Apr-22	16-Aug-22		16-Aug-22, Structure - Commons Building	
	1st Floor CF Framing @ Bearing Walls @ Commons	5	27-Apr-22	04-May-22		1st Floor CF Framing @ Bearing Walls @ Commons	
	1st Floor Steel @ Commons	20	27-Apr-22	25-May-22		1st Floor Steel @ Commons	
	1st Floor Timber Framing @ Commons	20	04-May-22	01-Jun-22		1st Floor Timber Framing @ Commons	
Remaining Level of Effort Actual Work					Remaining Work Critical Remaining Work		Milestone Summary
Page 19 of 66					WT WHITING-TURNER		

[illegible]

BROADVIEW SENIOR LEARNING (4/6/21 DRAFT)					Full Schedule		15-Apr-21 13:37
Activity ID	Activity Name	Original Duration	Start	Finish			
	Review and Approve Fire Alarm	15	03-Mar-22	23-Mar-22		Review and Approve Fire Alarm	
	Fabricate & Deliver Electrical	10	17-Mar-22	30-Mar-22		Fabricate & Deliver Electrical	
	Fabricate & Deliver Electrical Panels & Gear	60	24-Mar-22	15-Jun-22		Fabricate & Deliver Electrical Panels & Gear	
	Fabricate and Deliver Fire Alarm	25	24-Mar-22	27-Apr-22		Fabricate and Deliver Fire Alarm	
	Final Review & Approve Lighting Model	10	15-Apr-22	28-Apr-22		Final Review & Approve Lighting Model	
	Fabricate & Deliver Lighting	60	29-Apr-22	21-Jul-22		Fabricate & Deliver Lighting	
	Elevators	85	24-Feb-22	22-Jun-22		22-Jun-22, Elevators	
	Submit Elevators	20	24-Feb-22	23-Mar-22		Submit Elevators	
	Review & Approve Elevators	15	24-Mar-22	13-Apr-22		Review & Approve Elevators	
	Fabricate & Deliver Elevators	50	14-Apr-22	22-Jun-22		Fabricate & Deliver Elevators	
	Fire Protection	76	24-Feb-22	09-Jun-22		09-Jun-22, Fire Protection	
	Submit Fire Protection Model	20	24-Feb-22	23-Mar-22		Submit Fire Protection Model	
	Final Review & Approve Fire Protection Model	15	08-Apr-22	28-Apr-22		Final Review & Approve Fire Protection Model	
	Fabricate & Deliver Fire Protection	30	29-Apr-22	09-Jun-22		Fabricate & Deliver Fire Protection	
	Finishes	88	17-Jan-22	18-May-22		18-May-22, Finishes	
	Fireplaces	65	17-Feb-22	18-May-22		18-May-22, Fireplaces	
	Submit Fireplaces	10	17-Feb-22	02-Mar-22		Submit Fireplaces	
	Review & Approve Fireplaces	15	03-Mar-22	23-Mar-22		Review & Approve Fireplaces	
	Fabricate & Deliver Fireplaces	40	24-Mar-22	18-May-22		Fabricate & Deliver Fireplaces	
	Ceilings	60	10-Feb-22	04-May-22		04-May-22, Ceilings	
	Submit Suspended Grid Ceilings	15	10-Feb-22	02-Mar-22		Submit Suspended Grid Ceilings	
	Review & Approve Suspended Grid Ceilings	15	03-Mar-22	23-Mar-22		Review & Approve Suspended Grid Ceilings	
	Fabricate & Deliver Suspended Grid Ceilings	30	24-Mar-22	04-May-22		Fabricate & Deliver Suspended Grid Ceilings	
	Flooring	70	17-Jan-22	22-Apr-22		22-Apr-22, Flooring	
	Submit Carpet & VCT & Wood Flooring	15	17-Jan-22	04-Feb-22		Submit Carpet & VCT & Wood Flooring	
	Submit Tile	10	17-Jan-22	28-Jan-22		Submit Tile	
	Review & Approve Tile	15	31-Jan-22	18-Feb-22		Review & Approve Tile	
	Review & Approve Carpet & VCT & Wood Flooring	15	07-Feb-22	25-Feb-22		Review & Approve Carpet & VCT & Wood Flooring	
	Fabricate & Deliver Tile	40	21-Feb-22	15-Apr-22		Fabricate & Deliver Tile	
	Fabricate & Deliver Carpet & VCT & Wood Flooring	40	28-Feb-22	22-Apr-22		Fabricate & Deliver Carpet & VCT & Wood Flooring	
	Painting	35	17-Jan-22	04-Mar-22		04-Mar-22, Painting	
	Submit Paint	10	17-Jan-22	28-Jan-22		Submit Paint	
	Review & Approve Paint	15	31-Jan-22	18-Feb-22		Review & Approve Paint	
	Fabricate & Deliver Paint	10	21-Feb-22	04-Mar-22		Fabricate & Deliver Paint	
	Toilet Partitions and Accessories	35	17-Jan-22	04-Mar-22		04-Mar-22, Toilet Partitions and Accessories	
	Submit Toilet Partitions and Accessories	10	17-Jan-22	28-Jan-22		Submit Toilet Partitions and Accessories	
	Review & Approve Toilet Partitions and Accessories	15	31-Jan-22	18-Feb-22		Review & Approve Toilet Partitions and Accessories	
	Fabricate & Deliver Toilet Partitions and Accessories	10	21-Feb-22	04-Mar-22		Fabricate & Deliver Toilet Partitions and Accessories	
	Appliances	65	17-Jan-22	15-Apr-22		15-Apr-22, Appliances	
	Submit Appliances	10	17-Jan-22	28-Jan-22		Submit Appliances	
	Review & Approve Appliances	15	31-Jan-22	18-Feb-22		Review & Approve Appliances	
	Fabricate & Deliver Appliances	40	21-Feb-22	15-Apr-22		Fabricate & Deliver Appliances	
	Exterior Siding & Trim	60	17-Jan-22	08-Apr-22		08-Apr-22, Exterior Siding & Trim	
	Submit Exterior Siding & Trim	15	17-Jan-22	04-Feb-22		Submit Exterior Siding & Trim	
	Submit Exterior Special Shapes	15	17-Jan-22	04-Feb-22		Submit Exterior Special Shapes	
	Review & Approve Siding & Trim	15	07-Feb-22	25-Feb-22		Review & Approve Siding & Trim	
	Review & Approve Exterior Special Shapes	15	07-Feb-22	25-Feb-22		Review & Approve Exterior Special Shapes	
	Fabricate & Deliver Siding & Trim	20	28-Feb-22	25-Mar-22		Fabricate & Deliver Siding & Trim	
	Remaining Level of Effort	Remaining Work	Milestone				
	Actual Work	Critical Remaining Work	Summary				

WT

WHITING-TURNER

Page 27 of 66

BROADVIEW SENIOR LEARNING (4/6/21 DRAFT)					Full Schedule		15-Apr-21 13:37
Activity ID	Activity Name	Original Duration	Start	Finish			
	Fabricate & Deliver Exterior Special Shapes	30	28-Feb-22	08-Apr-22		Fabricate & Deliver Exterior Special Shapes	
	HVAC	94	10-Jan-22	19-May-22		19-May-22, HVAC	
	Submit HVAC Ductwork Model	15	10-Jan-22	28-Jan-22		Submit HVAC Ductwork Model	
	Submit HVAC Equipment	15	10-Jan-22	28-Jan-22		Submit HVAC Equipment	
	Review & Approve HVAC Equipment	15	31-Jan-22	18-Feb-22		Review & Approve HVAC Equipment	
	Fabricate & Deliver HVAC Equipment	40	21-Feb-22	15-Apr-22		Fabricate & Deliver HVAC Equipment	
	Final Review & Approve HVAC Ductwork Model	10	15-Apr-22	28-Apr-22		Final Review & Approve HVAC Ductwork Model	
	Fabricate & Deliver Ductwork	15	29-Apr-22	19-May-22		Fabricate & Deliver Ductwork	
	Construction - IL West	339	15-Feb-22	05-Jun-23		05-Jun-23, Construction - IL West	
	Structure - IL West	225	15-Feb-22	27-Dec-22		27-Dec-22, Structure - IL West	
	Foundations - IL West	122	15-Feb-22	04-Aug-22		04-Aug-22, Foundations - IL West	
	Foundation Excavation @ IL West	5	15-Feb-22	22-Feb-22		Foundation Excavation @ IL West	
	Form & Pour Footings & Walls @ IL West	15	22-Feb-22	15-Mar-22		Form & Pour Footings & Walls @ IL West	
	Form & Pour Lower Level Columns @ Commons	10	15-Mar-22	29-Mar-22		Form & Pour Lower Level Columns @ Commons	
	Foundation Waterproofing @ Commons	15	20-Apr-22	11-May-22		Foundation Waterproofing @ Commons	
	Foundation Backfill @ IL (West)	10	11-May-22	25-May-22		Foundation Backfill @ IL (West)	
	Masonry Partitions (LL to Roof Level) Commons	10	11-May-22	25-May-22		Masonry Partitions (LL to Roof Level) Commons	
	Underground Utilities @ Commons	10	09-Jun-22	23-Jun-22		Underground Utilities @ Commons	
	Prep, Form, & Pour Lower Level SOG @ Commons	10	23-Jun-22	07-Jul-22		Prep, Form, & Pour Lower Level SOG @ Commons	
	Form & Pour 1st Fl Elevated Slab	15	14-Jul-22	04-Aug-22		Form & Pour 1st Fl Elevated Slab	
	Structure - IL West	78	04-Aug-22	22-Nov-22		22-Nov-22, Structure - IL West	
	1st Floor CF Framing @ Bearing Walls @ Commons	4	04-Aug-22	10-Aug-22		1st Floor CF Framing @ Bearing Walls @ Commons	
	2nd Floor Hambro Deck @ Commons	10	08-Aug-22	22-Aug-22		2nd Floor Hambro Deck @ Commons	
	Prep & Pour 2nd Fl Elevated Slab @ Commons	5	18-Aug-22	25-Aug-22		Prep & Pour 2nd Fl Elevated Slab @ Commons	
	2nd Floor CF Bearing Walls @ Commons	4	25-Aug-22	31-Aug-22		2nd Floor CF Bearing Walls @ Commons	
	3rd Floor Hambro Deck @ Commons	10	29-Aug-22	12-Sep-22		3rd Floor Hambro Deck @ Commons	
	Prep & Pour 3rd Fl Elevated Slab @ Commons	5	08-Sep-22	15-Sep-22		Prep & Pour 3rd Fl Elevated Slab @ Commons	
	3rd Floor CF Bearing Walls @ Commons	4	15-Sep-22	21-Sep-22		3rd Floor CF Bearing Walls @ Commons	
	4rd Floor Hambro Deck @ Commons	10	19-Sep-22	03-Oct-22		4rd Floor Hambro Deck @ Commons	
	Prep & Pour 4th Fl Elevated Slab @ Commons	5	29-Sep-22	06-Oct-22		Prep & Pour 4th Fl Elevated Slab @ Commons	
	4th Floor CF Bearing Walls @ Commons	4	06-Oct-22	12-Oct-22		4th Floor CF Bearing Walls @ Commons	
	5th Floor Hambro Deck @ Commons	10	10-Oct-22	24-Oct-22		5th Floor Hambro Deck @ Commons	
	Prep & Pour Roof Level Elevated Slab @ Commons	5	20-Oct-22	27-Oct-22		Prep & Pour Roof Level Elevated Slab @ Commons	
	CF Roof Trusses @ Commons	15	25-Oct-22	15-Nov-22		CF Roof Trusses @ Commons	
	Roof Sheathing @ Commons	10	08-Nov-22	22-Nov-22		Roof Sheathing @ Commons	
	Penthouse Porch Framing @ 4th Level South @ Commc	5	15-Nov-22	22-Nov-22		Penthouse Porch Framing @ 4th Level South @ Commons	
	Exterior Doors & Windows - IL West	45	21-Sep-22	23-Nov-22		23-Nov-22, Exterior Doors & Windows - IL West	
	Exterior Air & Moisture Barrier @ Commons	25	21-Sep-22	26-Oct-22		Exterior Air & Moisture Barrier @ Commons	
	Exterior Windows @ Commons	15	19-Oct-22	09-Nov-22		Exterior Windows @ Commons	
	Exterior Doors @ Commons	10	09-Nov-22	23-Nov-22		Exterior Doors @ Commons	
	FR Wood Framed Balconies - IL West	28	24-Oct-22	01-Dec-22		01-Dec-22, FR Wood Framed Balconies - IL West	
	Wood Framed Balconies @ West CY Elevation @ Comn	6	24-Oct-22	01-Nov-22		Wood Framed Balconies @ West CY Elevation @ Commons	
	Wood Framed Balconies @ West Elevation @ Commons	10	27-Oct-22	10-Nov-22		Wood Framed Balconies @ West Elevation @ Commons	
	Wood Framed Balconies @ Corner CY Elevation @ Con	3	01-Nov-22	04-Nov-22		Wood Framed Balconies @ Corner CY Elevation @ Commons	
	Wood Framed Balconies @ South CY Elevation @ Com	6	04-Nov-22	14-Nov-22		Wood Framed Balconies @ South CY Elevation @ Commons	
	Wood Framed Balconies @ West Elevation @ Commons	10	10-Nov-22	24-Nov-22		Wood Framed Balconies @ West Elevation @ Commons	
	Wood Framed Balconies @ West CY Elevation @ Comn	5	14-Nov-22	21-Nov-22		Wood Framed Balconies @ West CY Elevation @ Commons	
	Wood Framed Balconies @ North Elevation @ Common	5	24-Nov-22	01-Dec-22		Wood Framed Balconies @ North Elevation @ Commons	
	Remaining Level of Effort	Remaining Work	Milestone	Page 28 of 66			
	Actual Work	Critical Remaining Work	Summary				
							

BROADVIEW SENIOR LEARNING (4/6/21 DRAFT)					Full Schedule		15-Apr-21 13:37
Activity ID	Activity Name	Original Duration	Start	Finish			
	Final Review & Approve Lighting Model	10	19-Aug-22	01-Sep-22	Final Review & Approve Lighting Model		
	Fabricate & Deliver Lighting	60	02-Sep-22	24-Nov-22	Fabricate & Deliver Lighting		
	Elevators	85	30-Jun-22	26-Oct-22	26-Oct-22, Elevators		
	Submit Elevators	20	30-Jun-22	27-Jul-22	Submit Elevators		
	Review & Approve Elevators	15	28-Jul-22	17-Aug-22	Review & Approve Elevators		
	Fabricate & Deliver Elevators	50	18-Aug-22	26-Oct-22	Fabricate & Deliver Elevators		
	Fire Protection	86	30-Jun-22	27-Oct-22	27-Oct-22, Fire Protection		
	Submit Fire Protection Model	20	30-Jun-22	27-Jul-22	Submit Fire Protection Model		
	Final Review & Approve Fire Protection Model	10	02-Sep-22	15-Sep-22	Final Review & Approve Fire Protection Model		
	Fabricate & Deliver Fire Protection	30	16-Sep-22	27-Oct-22	Fabricate & Deliver Fire Protection		
	HVAC	70	30-Jun-22	05-Oct-22	05-Oct-22, HVAC		
	Submit HVAC Ductwork Model	15	30-Jun-22	20-Jul-22	Submit HVAC Ductwork Model		
	Submit HVAC Equipment	15	30-Jun-22	20-Jul-22	Submit HVAC Equipment		
	Review & Approve HVAC Equipment	15	21-Jul-22	10-Aug-22	Review & Approve HVAC Equipment		
	Fabricate & Deliver HVAC Equipment	40	11-Aug-22	05-Oct-22	Fabricate & Deliver HVAC Equipment		
	Final Review & Approve HVAC Ductwork Model	10	19-Aug-22	01-Sep-22	Final Review & Approve HVAC Ductwork Model		
	Fabricate & Deliver Ductwork	15	02-Sep-22	22-Sep-22	Fabricate & Deliver Ductwork		
	Finishes	80	16-Jun-22	05-Oct-22	05-Oct-22, Finishes		
	Fireplaces	65	16-Jun-22	14-Sep-22	14-Sep-22, Fireplaces		
	Submit Fireplaces	10	16-Jun-22	29-Jun-22	Submit Fireplaces		
	Review & Approve Fireplaces	15	30-Jun-22	20-Jul-22	Review & Approve Fireplaces		
	Fabricate & Deliver Fireplaces	40	21-Jul-22	14-Sep-22	Fabricate & Deliver Fireplaces		
	Ceilings	60	16-Jun-22	07-Sep-22	07-Sep-22, Ceilings		
	Submit Suspended Grid Ceilings	15	16-Jun-22	06-Jul-22	Submit Suspended Grid Ceilings		
	Submit Faux Wood Ceilings	15	16-Jun-22	06-Jul-22	Submit Faux Wood Ceilings		
	Review & Approve Suspended Grid Ceilings	15	07-Jul-22	27-Jul-22	Review & Approve Suspended Grid Ceilings		
	Review & Approve Faux Wood Ceilings	15	07-Jul-22	27-Jul-22	Review & Approve Faux Wood Ceilings		
	Fabricate & Deliver Suspended Grid Ceilings	30	28-Jul-22	07-Sep-22	Fabricate & Deliver Suspended Grid Ceilings		
	Fabricate & Deliver Faux Wood Ceilings	30	28-Jul-22	07-Sep-22	Fabricate & Deliver Faux Wood Ceilings		
	Flooring	70	30-Jun-22	05-Oct-22	05-Oct-22, Flooring		
	Submit Carpet & VCT & Wood Flooring	15	30-Jun-22	20-Jul-22	Submit Carpet & VCT & Wood Flooring		
	Submit Tile	10	30-Jun-22	13-Jul-22	Submit Tile		
	Review & Approve Tile	15	14-Jul-22	03-Aug-22	Review & Approve Tile		
	Review & Approve Carpet & VCT & Wood Flooring	15	21-Jul-22	10-Aug-22	Review & Approve Carpet & VCT & Wood Flooring		
	Fabricate & Deliver Tile	40	04-Aug-22	28-Sep-22	Fabricate & Deliver Tile		
	Fabricate & Deliver Carpet & VCT & Wood Flooring	40	11-Aug-22	05-Oct-22	Fabricate & Deliver Carpet & VCT & Wood Flooring		
	Painting	35	30-Jun-22	17-Aug-22	17-Aug-22, Painting		
	Submit Paint	10	30-Jun-22	13-Jul-22	Submit Paint		
	Review & Approve Paint	15	14-Jul-22	03-Aug-22	Review & Approve Paint		
	Fabricate & Deliver Paint	10	04-Aug-22	17-Aug-22	Fabricate & Deliver Paint		
	Toilet Accessories	35	30-Jun-22	17-Aug-22	17-Aug-22, Toilet Accessories		
	Submit Toilet Accessories	10	30-Jun-22	13-Jul-22	Submit Toilet Accessories		
	Review & Approve Accessories	15	14-Jul-22	03-Aug-22	Review & Approve Accessories		
	Fabricate & Deliver Toilet Accessories	10	04-Aug-22	17-Aug-22	Fabricate & Deliver Toilet Accessories		
	Exterior Siding & Trim	60	30-Jun-22	21-Sep-22	21-Sep-22, Exterior Siding & Trim		
	Submit Exterior Siding & Trim	15	30-Jun-22	20-Jul-22	Submit Exterior Siding & Trim		
	Submit Exterior Special Shapes	15	30-Jun-22	20-Jul-22	Submit Exterior Special Shapes		
	Review & Approve Siding & Trim	15	21-Jul-22	10-Aug-22	Review & Approve Siding & Trim		
Remaining Level of Effort Remaining Work Actual Work Critical Remaining Work Milestone Summary					Page 38 of 66		WT WHITING-TURNER

BROADVIEW SENIOR LEARNING (4/6/21 DRAFT)					Full Schedule	15-Apr-21 13:37
Activity ID	Activity Name	Original Duration	Start	Finish		
	Review & Approve Exterior Special Shapes	15	21-Jul-22	10-Aug-22		
	Fabricate & Deliver Siding & Trim	20	11-Aug-22	07-Sep-22		
	Fabricate & Deliver Exterior Special Shapes	30	11-Aug-22	21-Sep-22		
	Laundry Equipment	45	30-Jun-22	31-Aug-22		
	Submit Laundry Equipment	15	30-Jun-22	20-Jul-22		
	Review & Approve Laundry Equipment	15	21-Jul-22	10-Aug-22		
	Fabricate & Deliver Laundry Equipment	15	11-Aug-22	31-Aug-22		
	Appliances	45	30-Jun-22	31-Aug-22		
	Submit Appliances	15	30-Jun-22	20-Jul-22		
	Review & Approve Appliances	15	21-Jul-22	10-Aug-22		
	Fabricate & Deliver Appliances	15	11-Aug-22	31-Aug-22		
	Construction - AL & Memory Care	275	03-Aug-22	23-Aug-23		
	Structure - AL & Memory Care	186	03-Aug-22	20-Apr-23		
	Foundations	81	03-Aug-22	24-Nov-22		
	Foundation Excavation @ AL & Memory Care	20	03-Aug-22	31-Aug-22		
	Form & Pour Footings & Walls @ AL & Memory Care	25	03-Aug-22	07-Sep-22		
	Foundation Waterproofing @ AL & Memory Care	10	07-Sep-22	21-Sep-22		
	Masonry Partitions (1st Level to Roof Level) AL & Memory Care	20	07-Sep-22	05-Oct-22		
	Foundation Backfill @ AL & Memory Care	10	21-Sep-22	05-Oct-22		
	Underground Utilities @ AL & Memory Care	15	13-Oct-22	03-Nov-22		
	Prep, Form, & Pour SOG @ AL & Memory Care	15	03-Nov-22	24-Nov-22		
	Structure	85	24-Nov-22	23-Mar-23		
	1st Floor CF Framing @ Bearing Walls @ AL & Memory Care	5	24-Nov-22	01-Dec-22		
	1st Floor Steel @ AL & Memory Care	10	24-Nov-22	08-Dec-22		
	2nd Floor Hambro Deck @ AL & Memory Care	10	01-Dec-22	15-Dec-22		
	Prep & Pour 2nd Fl Elevated Slab @ AL & Memory Care	10	08-Dec-22	22-Dec-22		
	2nd Floor CF Framing @ Bearing Walls @ AL & Memory Care	5	22-Dec-22	29-Dec-22		
	2nd Floor Steel @ AL & Memory Care	10	29-Dec-22	12-Jan-23		
	Roof Level Hambro Deck @ AL & Memory Care	10	05-Jan-23	19-Jan-23		
	Prep & Pour Roof Level Elevated Slab @ AL & Memory Care	10	19-Jan-23	02-Feb-23		
	CF Roof Trusses @ AL & Memory Care	15	02-Feb-23	23-Feb-23		
	Roof Sheathing @ AL & Memory Care	10	16-Feb-23	02-Mar-23		
	CF Porch Framing @ AL & Memory Care	5	23-Feb-23	02-Mar-23		
	CF Exterior Framing & Sheathing @ Porte Cochere	15	02-Mar-23	23-Mar-23		
	Exterior Doors & Windows	45	22-Dec-22	23-Feb-23		
	Exterior Air & Moisture Barrier @ AL & Memory Care	25	22-Dec-22	26-Jan-23		
	Exterior Windows @ AL & Memory Care	20	12-Jan-23	09-Feb-23		
	Exterior Door Frames @ AL & Memory Care	10	09-Feb-23	23-Feb-23		
	Roofing	55	02-Feb-23	20-Apr-23		
	Roof Hatches & Ladders	5	02-Feb-23	09-Feb-23		
	CF Framing & Sheathing @ Coupolas	15	09-Feb-23	02-Mar-23		
	Fiber Cement Facia Boards	15	16-Feb-23	09-Mar-23		
	Flat Roof Drains, Roofing, & Tapered Insulation @ AL & Memory Care	15	02-Mar-23	23-Mar-23		
	Pitched Roofing Shingles @ AL & Memory Care	20	02-Mar-23	30-Mar-23		
	Metal Roof Trims & Flashings @ Porte Cochere	15	09-Mar-23	30-Mar-23		
	Metal Roof Trims & Flashings @ AL & Memory Care	15	30-Mar-23	20-Apr-23		
	Interior - AL & Memory Care	174	22-Dec-22	23-Aug-23		
	1st Floor Interior	174	22-Dec-22	23-Aug-23		

Remaining Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

Summary

Page 39 of 66

WT

WHITING-TURNER

[illegible]

BROADVIEW SENIOR LEARNING (4/6/21 DRAFT)					Full Schedule		15-Apr-21 13:37
Activity ID	Activity Name	Original Duration	Start	Finish			
	Submit Plumbing	10	04-Oct-21	15-Oct-21			
	Review & Approve Plumbing	15	18-Oct-21	05-Nov-21			
	Fabricate & Deliver Plumbing	30	08-Nov-21	21-Dec-21			
	Electrical	90	04-Oct-21	09-Feb-22			
	Submit Electrical Cable	10	04-Oct-21	15-Oct-21			
	Submit Electrical Panels	15	04-Oct-21	22-Oct-21			
	Submit Lighting	15	04-Oct-21	22-Oct-21			
	Submit Fire Alarm	15	04-Oct-21	22-Oct-21			
	Review & Approve Electrical Cable	15	18-Oct-21	05-Nov-21			
	Review & Approve Electrical Panels	15	25-Oct-21	12-Nov-21			
	Review & Approve Lighting	15	25-Oct-21	12-Nov-21			
	Review and Approve Fire Alarm	15	25-Oct-21	12-Nov-21			
	Fabricate & Deliver Electrical Cable	10	08-Nov-21	19-Nov-21			
	Fabricate & Deliver Electrical Panels	60	15-Nov-21	09-Feb-22			
	Fabricate & Deliver Lighting	60	15-Nov-21	09-Feb-22			
	Fabricate and Deliver Fire Alarm	25	15-Nov-21	21-Dec-21			
	HVAC	70	18-Oct-21	26-Jan-22			
	Submit HVAC Ductwork	15	18-Oct-21	05-Nov-21			
	Submit HVAC Equipment	15	18-Oct-21	05-Nov-21			
	Review & Approve HVAC Ductwork	15	08-Nov-21	30-Nov-21			
	Review & Approve HVAC Equipment	15	08-Nov-21	30-Nov-21			
	Fabricate & Deliver HVAC Equipment	40	01-Dec-21	26-Jan-22			
	Fabricate & Deliver Ductwork	15	01-Dec-21	21-Dec-21			
	Finishes	80	04-Oct-21	26-Jan-22			
	Fireplaces	65	04-Oct-21	05-Jan-22			
	Submit Fireplaces	10	04-Oct-21	15-Oct-21			
	Review & Approve Fireplaces	15	18-Oct-21	05-Nov-21			
	Fabricate & Deliver Fireplaces	40	08-Nov-21	05-Jan-22			
	Flooring	70	18-Oct-21	26-Jan-22			
	Submit Carpet, Vinyl & Wood Flooring	15	18-Oct-21	05-Nov-21			
	Submit Tile	10	18-Oct-21	29-Oct-21			
	Review & Approve Tile	15	01-Nov-21	19-Nov-21			
	Review & Approve Carpet, Vinyl & Wood Flooring	15	08-Nov-21	30-Nov-21			
	Fabricate & Deliver Tile	40	22-Nov-21	19-Jan-22			
	Fabricate & Deliver Carpet, Vinyl & Wood Flooring	40	01-Dec-21	26-Jan-22			
	Painting	35	18-Oct-21	07-Dec-21			
	Submit Paint	10	18-Oct-21	29-Oct-21			
	Review & Approve Paint	15	01-Nov-21	19-Nov-21			
	Fabricate & Deliver Paint	10	22-Nov-21	07-Dec-21			
	Toilet Accessories	35	18-Oct-21	07-Dec-21			
	Submit Hardware & Toilet Accessories	10	18-Oct-21	29-Oct-21			
	Review & Approve Hardware & Toilet Accessories	15	01-Nov-21	19-Nov-21			
	Fabricate & Deliver Hardware & Toilet Accessories	10	22-Nov-21	07-Dec-21			
	Exterior Siding & Trim	60	18-Oct-21	12-Jan-22			
	Submit Exterior Siding & Trim	15	18-Oct-21	05-Nov-21			
	Submit Exterior Special Shapes	15	18-Oct-21	05-Nov-21			
	Review & Approve Siding & Trim	15	08-Nov-21	30-Nov-21			
	Review & Approve Exterior Special Shapes	15	08-Nov-21	30-Nov-21			
Remaining Level of Effort Actual Work Remaining Work Critical Remaining Work Milestone Summary					Page 46 of 66		WT WHITING-TURNER

[illegible]

