


ID		Task Name	Duration	Start	Finish	Notes	Apr '25					May '25					Jun '25					Jul '25					Aug '25					Sep '25					Oct		
							30	6	13	20	27	4	11	18	25	1	8	15	22	29	6	13	20	27	3	10	17	24	31	7	14	21	28						
1																																							
2		PHASE 5 CONSTRUCTION PHASE																																					
3		HighView Elementary School BE-01, GC-01, MC-01, EC-01																																					
4		Highview Elementary School - Roofing - BE-01	37 days?	Mon 4/1/24	Tue 5/21/24	Weekend work and double shift anticipated																																	
5		Mobilization	1 day	Tue 4/1/25	Tue 4/1/25	Spring Break School Closed March 31 April 4																																	
6		Remove Asphalt Shingle Roof R2	2 days	Wed 4/2/25	Thu 4/3/25	Spring Break School Closed March 31 April 4																																	
7		New Roofing Roof R2	3 days	Fri 4/4/25	Tue 4/8/25	Spring Break School Closed March 31 April 4																																	
8		Wet Removals & Patching	7 days	Wed 4/2/25	Thu 4/10/25	Spring Break School Closed March 31 April 4																																	
9		Roof Cleaning R3,R4	5 days	Fri 4/4/25	Thu 4/10/25	Possible Second Shift. Noise Dependant																																	
10		Flashings R3,R4	5 days	Tue 4/8/25	Mon 4/14/25																																		
11		Roof Priming R3,R4	4 days	Fri 4/11/25	Wed 4/16/25																																		
12		Base Coat R3,R4	4 days	Mon 4/14/25	Thu 4/17/25																																		
13		Top Coat R3,R4	4 days	Wed 4/16/25	Mon 4/21/25																																		
14		Top Sand R3,R4	3 days	Fri 4/18/25	Tue 4/22/25																																		
15		Roof Down Spout Replacements	5 days	Wed 4/23/25	Tue 4/29/25																																		
16		Roof Drain Covers	2 days	Wed 4/23/25	Thu 4/24/25																																		
17		Cleanup & Demobilize	1 day	Fri 4/25/25	Fri 4/25/25																																		
18		Highview Elementary School - Masonry - BE-01	11 days?	Wed 6/26/24	Wed 7/10/24	School Year Project - Weekend work and double																																	
19		Mobilize	1 day	Fri 6/27/25	Fri 6/27/25																																		
20		Window Lintel Repair	7 days	Mon 6/30/25	Tue 7/8/25																																		
21		Masonry Repointing	20 days	Wed 7/9/25	Tue 8/5/25																																		
22		Masonry Cleaning	15 days	Wed 8/6/25	Tue 8/26/25																																		
23		Cleanup & Demobilize	1 day	Wed 8/27/25	Wed 8/27/25																																		
24		Highview Elementary School - Doors & Glazing & Misc. Interior - GC-01		Wed 6/26/24	7/39/24	School Year Project - Weekend work and double shift anticipated																																	
25		Mobilize	1 day	Mon 4/28/25	Mon 4/28/25	Second Shift																																	
26		Door, Hardware, & Glazing Removal and Replacement	45 days	Tue 4/29/25	Mon 6/30/25	Second Shift																																	
27		Cleanup & Demobilize Interior	1 day	Tue 7/1/25	Tue 7/1/25																																		
28		Highview Elementary School - Security Vestibule Renovation - GC-01, MC-01, EC-01	61 days?	Sat 6/14/25	Fri 9/5/25	School Year Project - Weekend Work Required																																	
29		Demolition	3 days	Thu 6/26/25	Mon 6/30/25																																		
30		Wall Framing	4 days	Tue 7/1/25	Fri 7/4/25	Milestone																																	
31		Exterior Storefront & Doors	2 days	Tue 7/1/25	Wed 7/2/25																																		

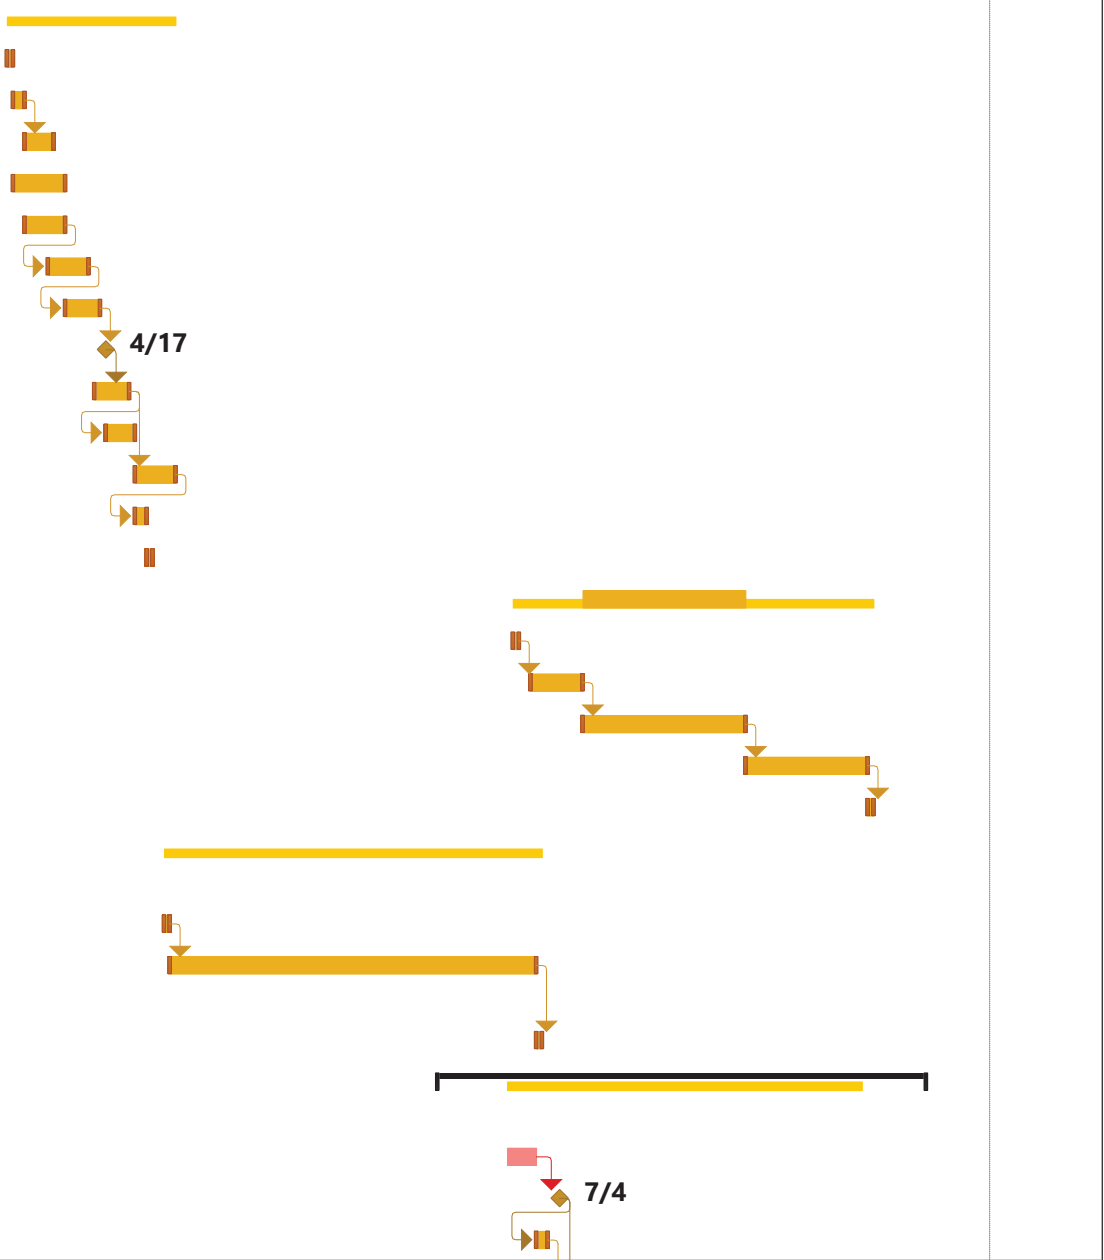

Project: \\nycfil02\PROJ\2021 p
Date: Thu 12/12/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone















Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only















External Tasks

External Milestone


Deadline

Path Predecessor Milestone Task

Path Predecessor Summary Task

Path Predecessor Normal Task

Path Driving Predecessor Milestone Task















Path Driving Predecessor Summary Task

Path Driving Predecessor Normal Task

Critical

Critical Split

Progress

Manual Progress













ID	i	Task Name	Duration	Start	Finish	Notes	Apr '25				May '25				Jun '25				Jul '25				Aug '25				Sep '25				Oct '25		
							30	6	13	20	27	4	11	18	25	1	8	15	22	29	6	13	20	27	3	10	17	24	31	7		14	21
66		Mobilization	1 day	Fri 6/27/25	Fri 6/27/25																												
67		Demolition - GC	3 days	Fri 6/27/25	Tue 7/1/25																												
68		Demolition - PC	2 days	Sat 6/28/25	Mon 6/30/25	Weekend Work																											
69		Framing	5 days	Tue 7/1/25	Mon 7/7/25																												
70		Plumbing Rough-in	7 days	Tue 7/8/25	Wed 7/16/25																												
71		Mechanical Rough-in	1 day	Thu 7/17/25	Thu 7/17/25																												
72		Electrical Rough-in	8 days	Fri 7/18/25	Tue 7/29/25																												
73		Sheetrock	2 days	Wed 7/30/25	Thu 7/31/25																												
74		Taping	4 days	Fri 8/1/25	Wed 8/6/25	Weekend Work																											
75		Floor Mud / Pitch	1 day	Thu 8/7/25	Thu 8/7/25																												
76		Painting	3 days	Fri 8/8/25	Tue 8/12/25	Weekend Work																											
77		Tile	5 days	Sat 8/9/25	Thu 8/14/25																												
78		Epoxy Floors	1 day	Fri 8/15/25	Fri 8/15/25																												
79		Plumbing Fixtures	3 days	Sat 8/16/25	Tue 8/19/25	Weekend Work																											
80		Electrical Connections for Plumbing	2 days	Tue 8/19/25	Wed 8/20/25																												
81		Trim out Lighting and Plumbing	2 days	Wed 8/20/25	Thu 8/21/25																												
82		Partitions	2 days	Fri 8/22/25	Mon 8/25/25																												
83		HVAC grills registers and diffusers	1 day	Tue 8/26/25	Tue 8/26/25																												
84		Toilet Accessories & Mirrors	2 days	Tue 8/26/25	Wed 8/27/25																												
85		Touchups	1 day	Thu 8/28/25	Thu 8/28/25																												
86		Testing & Balancing	1 day	Fri 8/29/25	Fri 8/29/25																												
87		Cleanup and Demobilize	0 days	Mon 9/1/25	Mon 9/1/25																												
88																																	
89		Highview Elementary School - TOILET ROOMS First Floor - GC-01, MC-01, EC-01	47 days	Fri 6/27/25	Mon 9/1/25	Summer 2025 project																											
90		Demolition EC	1 day	Fri 6/27/25	Fri 6/27/25																												
91		Mobilization	1 day	Fri 6/27/25	Fri 6/27/25																												
92		Demolition - GC	5 days	Wed 7/2/25	Tue 7/8/25																												
93		Demolition - PC	4 days	Tue 7/1/25	Fri 7/4/25																												
94		Framing	6 days	Tue 7/8/25	Tue 7/15/25																												
95		Plumbing Rough-in	10 days	Thu 7/17/25	Wed 7/30/25																												
96		Mechanical Rough-in	5 days	Fri 7/18/25	Thu 7/24/25																												
97		Electrical Rough-in	9 days	Wed 7/30/25	Mon 8/11/25																												
98		Sheetrock	4 days	Fri 8/1/25	Wed 8/6/25																												

Project: \\nycfil02\PROJ\2021 p
Date: Thu 12/12/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

◆

◆

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Path Predecessor Milestone Task

Path Predecessor Summary Task

Path Predecessor Normal Task

Path Driving Predecessor Milestone Task

◆

↓

◆

◆

Path Driving Predecessor Summary Task

Path Driving Predecessor Normal Task

Critical

Critical Split

Progress

Manual Progress

Page 3

ID	i	Task Name	Duration	Start	Finish	Notes	Apr '25					May '25					Jun '25					Jul '25					Aug '25					Sep '25					Oct '25
							30	6	13	20	27	4	11	18	25	1	8	15	22	29	6	13	20	27	3	10	17	24	31	7	14	21	28				
134		Toilet Accessories & Mirrors	3 days	Sat 8/30/25	Tue 9/2/25	Weekend Work																															
135		Touchups	2 days	Mon 9/1/25	Tue 9/2/25																																
136		Testing & Balancing	1 day	Mon 9/1/25	Mon 9/1/25																																
137		Cleanup and Demobilize	0 days	Mon 9/1/25	Mon 9/1/25																																
138																																					
139																																					
140		Highview Elementary School - Panel Replacements - EC-01	37 days	Mon 6/23/25	Tue 8/12/25	Summer 2025 project																															
141		Field Verify Existing Circuits	5 days	Mon 6/23/25	Fri 6/27/25																																
142		Remove & Repalce Panel DP-1	8 days	Mon 6/30/25	Wed 7/9/25																																
143		Remove & Repalce Panel BLR	7 days	Thu 7/10/25	Fri 7/18/25																																
144		Remove & Repalce Panel STAGE	7 days	Mon 7/21/25	Tue 7/29/25																																
145		Panel Directories & Labeling	3 days	Wed 7/30/25	Fri 8/1/25																																
146		3rd Party Inspections	1 day	Mon 8/4/25	Mon 8/4/25																																
147		Punchlist	5 days	Tue 8/5/25	Mon 8/11/25																																
148		Cleanup & Demobilize	0 days	Tue 8/12/25	Tue 8/12/25																																
149		Miller Elementary School MC-01, EC-01																																			
150		Miller Elementary School - HVAC Upgrades - GC-01, MC-01, EC-01	113 days	Fri 4/11/25	Tue 9/16/25	Spring Break Start																															
151		Mobilization	1 day	Fri 4/11/25	Fri 4/11/25																																
152		Controls Rough in	20 days	Mon 4/14/25	Fri 5/9/25	Spring Recess																															
153		Electrical Rough in	15 days	Mon 4/14/25	Fri 5/2/25	Spring Recess																															
154		Temp Ceiling Removals	15 days	Fri 6/27/25	Thu 7/17/25																																
155		Rooftop Steel	8 days	Tue 7/1/25	Thu 7/10/25																																
156		Roofing Penetrations and flashings	5 days	Fri 7/4/25	Thu 7/10/25																																
157		Set Condensing Units	1 day	Fri 7/11/25	Fri 7/11/25																																
158		Mount Fancoil units	15 days	Fri 6/27/25	Thu 7/17/25																																
159		Suction & Liquid Piping	20 days	Fri 6/27/25	Thu 7/24/25																																
160		Final Electrical and Controls Connections	15 days	Fri 7/18/25	Thu 8/7/25																																
161		Condensate Piping	15 days	Fri 7/25/25	Thu 8/14/25																																
162		Condensate pumps	5 days	Tue 8/12/25	Mon 8/18/25																																
163		Pressure Testing	5 days	Fri 8/15/25	Thu 8/21/25																																
164		Startup	5 days	Fri 8/22/25	Thu 8/28/25																																
165		Controls back end	20 days	Thu 7/24/25	Wed 8/20/25																																
166		Testing & Balancing	5 days	Wed 8/20/25	Tue 8/26/25																																

Project: \\nycfil02\PROJ\2021 p
Date: Thu 12/12/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

◆

◆

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Path Predecessor Milestone Task

Path Predecessor Summary Task

Path Predecessor Normal Task

Path Driving Predecessor Milestone Task

◆

↓

◆

◆

Path Driving Predecessor Summary Task

Path Driving Predecessor Normal Task

Critical

Critical Split

Progress

Manual Progress

ID	i	Task Name	Duration	Start	Finish	Notes	Apr '25		May '25		Jun '25		Jul '25		Aug '25		Sep '25		Oct '25										
							30	6	13	20	27	4	11	18	25	1	8	15	22	29	6	13	20	27	3	10	17	24	31
167		CX/ Punchlist	5 days	Tue 8/26/25	Mon 9/1/25																								
168		Training	1 day	Tue 9/2/25	Tue 9/2/25																								
169		Turnover	0 days	Wed 9/3/25	Wed 9/3/25																								
170		Closeout	10 days	Wed 9/3/25	Tue 9/16/25																								
171		Maintenance Building - GC-01, EC-01, MC-01																											
172		Maintenance Building Siding & interior - GC-01, EC-01, MC-01	42 days	Thu 6/26/25	Fri 8/22/25	Summer 2025 project																							
173		District Move Out	2 days	Thu 6/26/25	Fri 6/27/25																								
174		Mobilization	1 day	Mon 6/30/25	Mon 6/30/25																								
175		Skylight Removals/Infill	5 days	Tue 7/1/25	Mon 7/7/25																								
176		Siding Removals	5 days	Tue 7/8/25	Mon 7/14/25																								
177		New Siding	5 days	Tue 7/15/25	Mon 7/21/25																								
178		Electrical Demo/ temp lighting	1 day	Tue 7/22/25	Tue 7/22/25																								
179		Ceiling Demo	1 day	Wed 7/23/25	Wed 7/23/25																								
180		HVAC Demo	1 day	Thu 7/24/25	Thu 7/24/25																								
181		New Ceilings	3 days	Fri 7/25/25	Tue 7/29/25																								
182		Electrical Rough-in	2 days	Wed 7/30/25	Thu 7/31/25																								
183		HVAC Rough in - Suction, Liquid, Condensate,	3 days	Fri 8/1/25	Tue 8/5/25																								
184		Set new Condecing unit	1 day	Wed 8/6/25	Wed 8/6/25																								
185		Fain coil unit & Fin Tube	5 days	Thu 8/7/25	Wed 8/13/25																								
186		New Light Fixtures	2 days	Wed 8/6/25	Thu 8/7/25																								
187		Paint	3 days	Fri 8/8/25	Tue 8/12/25																								
188		White out Ceilings	1 day	Wed 8/13/25	Wed 8/13/25																								
189		Flooring	2 days	Thu 8/14/25	Fri 8/15/25																								
190		Punchlist	2 days	Mon 8/18/25	Tue 8/19/25																								
191		Move in	5 days	Mon 8/18/25	Fri 8/22/25																								
192		Maintenance Building Service Upgrade EC-01	37 days	Mon 4/14/25	Tue 6/3/25	Spring Break Start																							
193		Primary Trenching	2 days	Mon 4/14/25	Tue 4/15/25	Spring Recess																							
194		Primary Conduit & Pole Riser	2 days	Wed 4/16/25	Thu 4/17/25	Spring Recess																							
195		Inspections	1 day	Fri 4/18/25	Fri 4/18/25	Spring Recess																							
196		Primary Backfill & Asphalt Patch	1 day	Mon 4/21/25	Mon 4/21/25	Spring Recess																							
197		Set New Transformer Pad	1 day	Tue 4/22/25	Tue 4/22/25																								
198		Grounding	1 day	Wed 4/23/25	Wed 4/23/25																								
199		Secondary Trenching	3 days	Thu 4/24/25	Mon 4/28/25																								

Project: \\nycfil02\PROJ\2021 p
Date: Thu 12/12/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

◆

◆

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Path Predecessor Milestone Task

Path Predecessor Summary Task

Path Predecessor Normal Task

Path Driving Predecessor Milestone Task

◆

↓

◆

◆

Path Driving Predecessor Summary Task

Path Driving Predecessor Normal Task

Critical

Critical Split

Progress

Manual Progress

ID	<
----	---

ID	i	Task Name	Duration	Start	Finish	Notes	Apr '25				May '25				Jun '25				Jul '25				Aug '25				Sep '25				Oct
							30	6	13	20	27	4	11	18	25	1	8	15	22	29	6	13	20	27	3	10	17	24	31	7	14
235		Pour Footings	1 day	Wed 5/21/25	Wed 5/21/25																										
236		Form Foundations	1 day	Thu 5/22/25	Thu 5/22/25																										
237		Rebar	2 days	Fri 5/23/25	Mon 5/26/25																										
238		Pour Foundations	1 day	Tue 5/27/25	Tue 5/27/25																										
239		Form Ramp	1 day	Wed 5/28/25	Wed 5/28/25																										
240		Rebar	1 day	Thu 5/29/25	Thu 5/29/25																										
241		Pour Ramp	1 day	Fri 5/30/25	Fri 5/30/25																										
242		Handrails	1 day	Mon 6/2/25	Mon 6/2/25																										
243		Outdoor Education Center - Boiler & Mini-Split MC-01 & EC-01	2 days	Thu 6/19/25	Fri 6/20/25	Spring Break Start																									
245		Mobilization	1 day	Mon 5/19/25	Mon 5/19/25																										
246		Demo Existing Boiler / Piping	2 days	Tue 5/20/25	Wed 5/21/25																										
247		Set New Boiler	1 day	Thu 5/22/25	Thu 5/22/25																										
248		New HW Piping, Exhaust, Natural Gas	2 days	Fri 5/23/25	Mon 5/26/25																										
249		Electrical Rough in	2 days	Tue 5/27/25	Wed 5/28/25																										
250		Controls	3 days	Thu 5/29/25	Mon 6/2/25																										
251		Startup	1 day	Tue 6/3/25	Tue 6/3/25																										
252		T&B	1 day	Wed 6/4/25	Wed 6/4/25																										
253		Set New ACCU-OEC-1	1 day	Thu 6/5/25	Thu 6/5/25																										
254		Mount AC-OEC-1	1 day	Fri 6/6/25	Fri 6/6/25																										
255		Electrical Rough in	2 days	Mon 6/9/25	Tue 6/10/25																										
256		Liquid & Suction Piping	2 days	Wed 6/11/25	Thu 6/12/25																										
257		Condensate	1 day	Fri 6/13/25	Fri 6/13/25																										
258		Controls	2 days	Mon 6/16/25	Tue 6/17/25																										
259		Startup	1 day	Wed 6/18/25	Wed 6/18/25																										
260		T&B	1 day	Thu 6/19/25	Thu 6/19/25																										
261		Demmobilize	1 day	Fri 6/20/25	Fri 6/20/25																										
262																															
263		Outdoor Education Center - Interior IT Closet				SPRING BREAK PROJECT																									
264		Mobilization	1 day	Mon 4/14/25	Mon 4/14/25	Spring Recess																									
265		Demo	1 day	Mon 4/14/25	Mon 4/14/25	Spring Recess																									
266		Wall Framing	1 day	Tue 4/15/25	Tue 4/15/25	Spring Recess																									
267		Door Frame	1 day	Wed 4/16/25	Wed 4/16/25	Spring Recess																									
268		Sheetrock	1 day	Thu 4/17/25	Thu 4/17/25	Spring Recess																									
269		Taping	1 day	Fri 4/18/25	Fri 4/18/25	Spring Recess																									

Project: \\nycfil02\PROJ\2021 p
Date: Thu 12/12/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

◆

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Path Predecessor Milestone Task

Path Predecessor Summary Task

Path Predecessor Normal Task

Path Driving Predecessor Milestone Task

◆

↓

◆

◆

Path Driving Predecessor Summary Task

Path Driving Predecessor Normal Task

Critical


Critical Split

Progress

Manual Progress

Page 8

ID	i	Task Name	Duration	Start	Finish	Notes	Apr '25				May '25				Jun '25				Jul '25				Aug '25				Sep '25				Oct '25
							30	6	13	20	27	4	11	18	25	1	8	15	22	29	6	13	20	27	3	10	17	24	31	7	
270		Paint	1 day	Mon 4/21/25	Mon 4/21/25	Spring Recess																									
271		Ceilings	1 day	Tue 4/22/25	Tue 4/22/25	Second Shift																									
272		Hang New Door	1 day	Wed 4/23/25	Wed 4/23/25	Second Shift																									
273		Demobilize	1 day	Thu 4/24/25	Thu 4/24/25	Second Shift																									
274																															
275																															
276																															
277																															
278																															
279																															
280																															
281																															
282																															
283																															
284																															
285																															
286																															
287																															
288																															
289																															
290																															
291																															
292																															
293																															
294																															
295																															
296																															
297																															
298																															
299																															
300																															
301																															
302																															
303																															
304																															

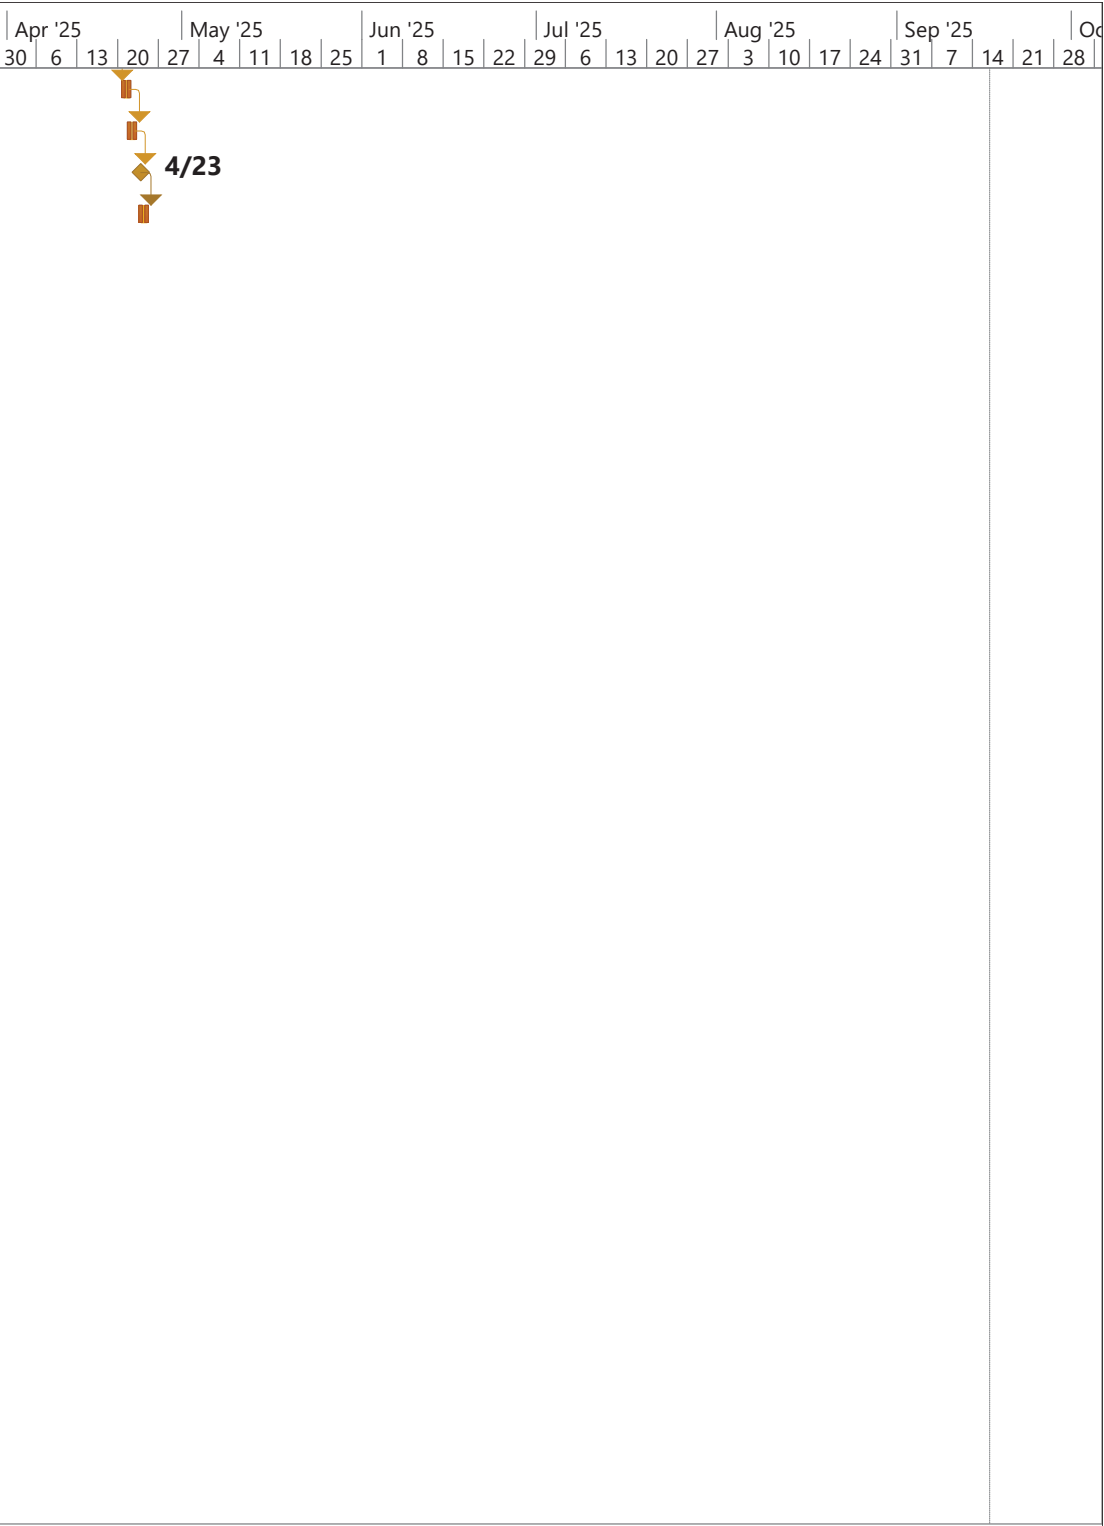

Project: \\nycfil02\PROJ\2021 p
Date: Thu 12/12/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone















Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only















External Tasks

External Milestone


Deadline

Path Predecessor Milestone Task

Path Predecessor Summary Task

Path Predecessor Normal Task

Path Driving Predecessor Milestone Task















Path Driving Predecessor Summary Task

Path Driving Predecessor Normal Task

Critical

Critical Split

Progress

Manual Progress













- 4

Highview Elementary School - Roofing - BE-01
Weekend work and double shift anticipated
- 5

Mobilization
Spring Break School Closed March 31 April 4
- 6

Remove Asphalt Shingle Roof R2
Spring Break School Closed March 31 April 4
- 7

New Roofing Roof R2
Spring Break School Closed March 31 April 4
- 8

Wet Removals & Patching
Spring Break School Closed March 31 April 4
- 9

Roof Cleaning R3,R4
Possible Second Shift. Noise Dependant
- 18

Highview Elementary School - Masonry - BE-02
School Year Project - Weekend work and double shift anticipated
- 24

Highview Elementary School - Doors & Glazing & Misc. Interior - GC-01
School Year Project - Weekend work and double shift anticipated
- 25

Mobilize
Second Shift
- 26

Door, Hardware, & Glazing Removal and Replacement
Second Shift
- 28

Highview Elementary School - Security Vestibule Renovation - GC-01, MC-01, EC-01
School Year Project - Weekend Work Required
- 30

Wall Framing
Milestone
- 32

Mechanical Rough-in & Equipment Walls
Weekend Work
- 35

Bullit Resistive Panel & Sheetrock Walls
Milestone
- 36

Ceiling Framing
Weekend Work
- 38

Electrical Rough-in Clg
Weekend Work
- 44

Finishes & Casework
Milestone
- 45

Interior Doors
Weekend Work
- 46

Testing & Ballancing
Milestone
- 48

District Move in
Milestone
- 51

Highview Elementary School - GYM - GC-01 & EC-01
Summer 2025 project
- 64

Highview Elementary School - TOILET ROOMS Ground Floor - GC-01, MC-01, EC-01
Summer 2025 project
- 68

Demolition - PC
Weekend Work
- 74

Taping
Weekend Work
- 76

Painting
Weekend Work
- 79

Plumbing Fixtures
Weekend Work

- 89

Highview Elementary School - TOILET ROOMS First Floor - - GC-01, MC-01, EC-01

Summer 2025 project
- 101

Painting

Weekend Work
- 109

Toilet Accessories & Mirrors

Weekend Work
- 114

Highview Elementary School - TOILET ROOMS Second Floor - - GC-01, MC-01, EC-01

Summer 2025 project
- 120

Plumbing Rough-in

Weekend Work
- 121

Mechanical Rough-in

Weekend Work
- 123

Sheetrock

Weekend Work
- 125

Floor Mud

Weekend Work
- 134

Toilet Accessories & Mirrors

Weekend Work
- 140

Highview Elementary School - Panel Replacements - - EC-01

Summer 2025 project
- 150

Miller Elementary School - HVAC Upgrades - GC-01, MC-01, EC-01

Spring Break Start
- 152

Controls Rough in

Spring Recess
- 153

Electrical Rough in

Spring Recess
- 172

Maintenance Building Siding & interior - GC-01, EC-01, MC-01

Summer 2025 project
- 192

Maintenance Building Service Upgrade EC-01

Spring Break Start
- 193

Primary Trenching

Spring Recess
- 194

Primary Conduit & Pole Riser

Spring Recess
- 195

Inspections

Spring Recess
- 196

Primary Backfill & Asphalt Patch

Spring Recess
- 218

Outdoor Education Center - Site Work - GC-01

Spring Break Start
- 219

Mobilization

Spring Recess
- 220

Remove North Stair & Handrails

Spring Recess
- 221

Remove East Stair & Handrails

Spring Recess
- 222

Form Footings

Spring Recess
- 243

Outdoor Education Center - Boiler & Mini-Split MC-01 & EC-01

Spring Break Start
- 263

Outdoor Education Center - Interior IT Closet

SPRING BREAK PROJECT

- 264 Mobilization
Spring Recess
- 265 Demo
Spring Recess
- 266 Wall Framing
Spring Recess
- 267 Door Frame
Spring Recess
- 268 Sheetrock
Spring Recess
- 269 Taping
Spring Recess
- 270 Paint
Spring Recess
- 271 Ceilings
Second Shift
- 272 Hang New Door
Second Shift
- 273 Demobilize
Second Shift
