


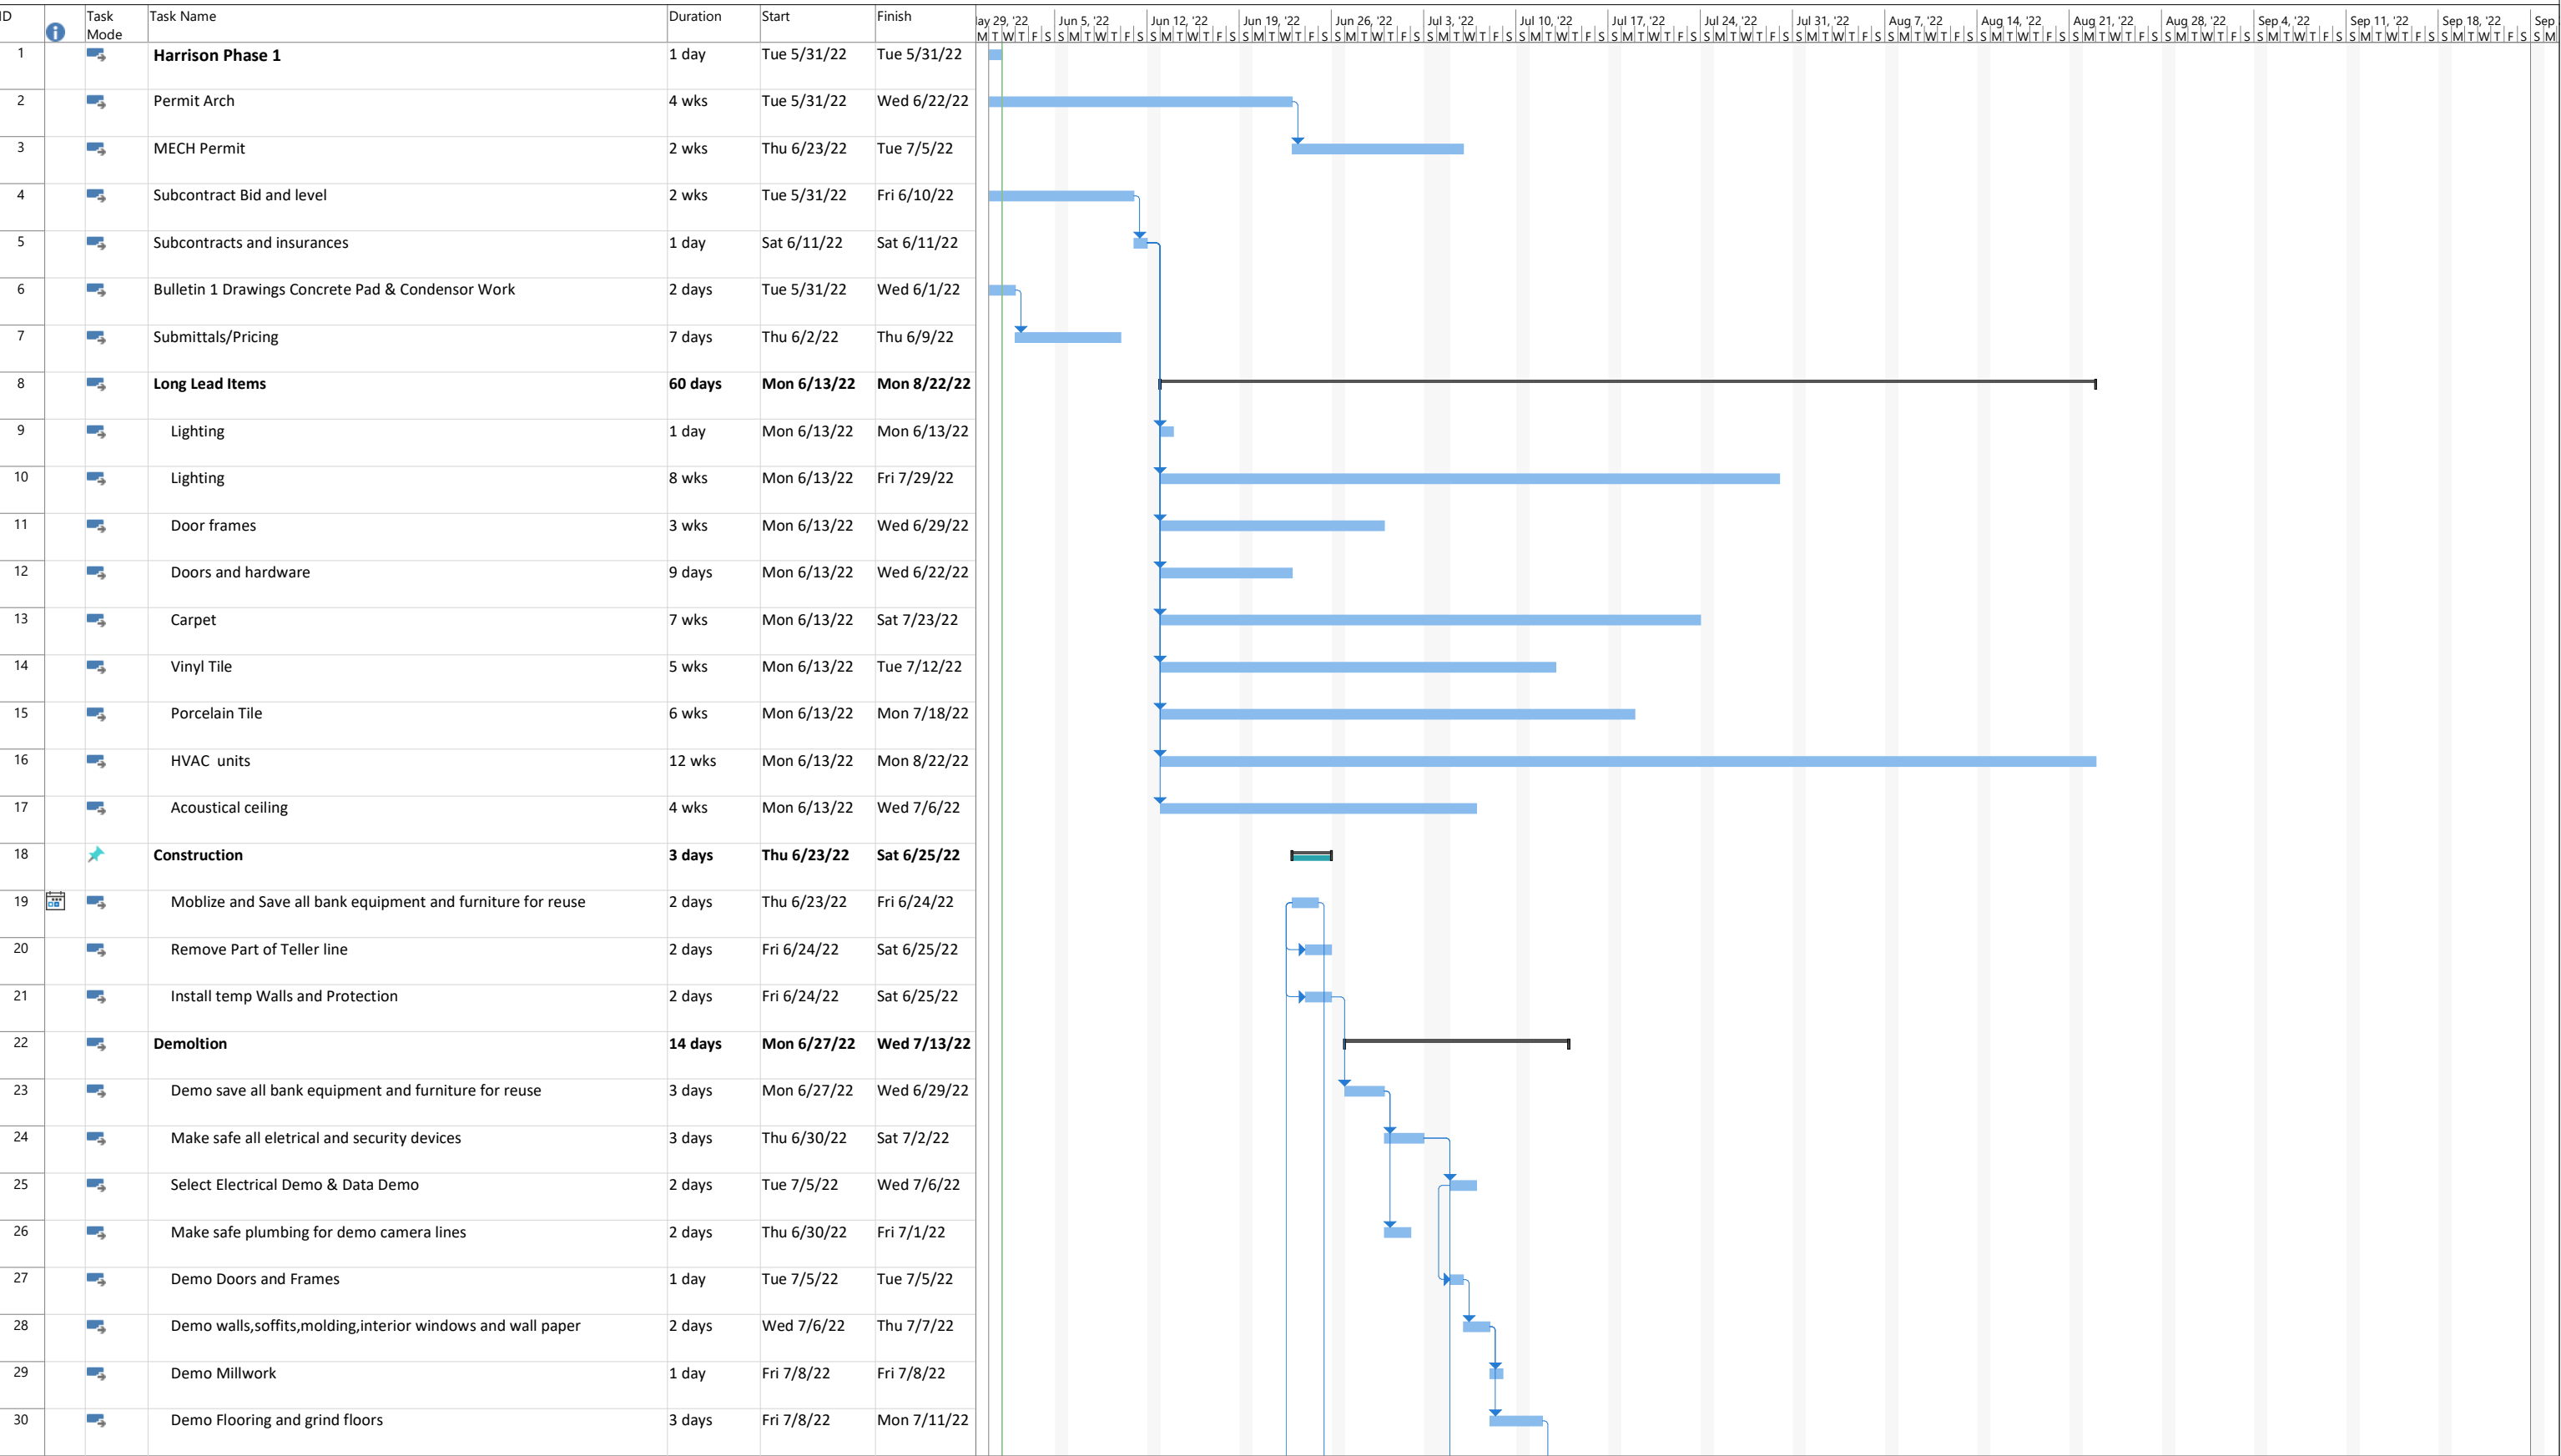

RW Dake Construction
1070 North Farms Road, Suite 3
Wallingford, CT 06495

M & T GAP - Harrison
389 Halstead Ave
Harrison, NY 10528

M & T Bank
One M & T Plaza
Buffalo, NY 14203

[illegible]

ID	Task Mode	Task Name	Duration	Start	Finish	May 29, '22	Jun 5, '22	Jun 12, '22	Jun 19, '22	Jun 26, '22	Jul 3, '22	Jul 10, '22	Jul 17, '22	Jul 24, '22	Jul 31, '22	Aug 7, '22	Aug 14, '22	Aug 21, '22	Aug 28, '22	Sep 4, '22	Sep 11, '22	Sep 18, '22	Sep 25, '22		
						M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S
61		Install accessories	2 days	Tue 8/16/22	Wed 8/17/22																				
62		Plumbing	24 days	Sat 7/16/22	Fri 8/12/22																				
63		Rough inwalls and trench for new restroom sanitary	3 days	Sat 7/16/22	Tue 7/19/22																				
64		Inspection	1 day	Wed 7/20/22	Wed 7/20/22																				
65		Fill in trenching	1 day	Thu 7/21/22	Thu 7/21/22																				
66		Above ceiling piping and install recircualting pump	3 days	Thu 7/21/22	Sat 7/23/22																				
67		Above ceiling inspection	1 day	Fri 8/12/22	Fri 8/12/22																				
68		Insulation	1 day	Mon 7/25/22	Mon 7/25/22																				
69		Install fixtures	1 day	Wed 8/3/22	Wed 8/3/22																				
70		Carpentry	43 days	Sat 6/25/22	Mon 8/15/22																				
71		Frame work room 112 walls, remove ceiling and support it for walls to be installed sheet rock 1 side, locate wall for restroom 111 install partial wall so plumbing can be roughed in. Install temp door access through mecanical room or other rest room	1 day	Sat 6/25/22	Sat 6/25/22																				
72		Layout and approval	2 days	Thu 7/14/22	Fri 7/15/22																				
73		Frame walls and open walls for new eletrical	2 days	Sat 7/16/22	Mon 7/18/22																				
74		Install blocking	1 day	Mon 7/18/22	Mon 7/18/22																				
75		Sheetrock one side	1 day	Tue 7/19/22	Tue 7/19/22																				
76		In wall inspections	1 day	Wed 7/20/22	Wed 7/20/22																				
77		Soffits and headers	2 days	Tue 7/19/22	Wed 7/20/22																				
78		Insulate walls	1 day	Tue 7/19/22	Tue 7/19/22																				
79		Close walls	1 day	Thu 7/21/22	Thu 7/21/22																				
80		Tape and spackle	4 days	Fri 7/22/22	Tue 7/26/22																				
81		Fire caulk and inspection	2 days	Fri 7/22/22	Sat 7/23/22																				
82		Install ceiling grid	2 days	Wed 7/27/22	Thu 7/28/22																				
83		Install cut tiles	1 day	Fri 7/29/22	Fri 7/29/22																				
84		Install door frames	1 day	Wed 7/27/22	Wed 7/27/22																				
85		Install doors and hardware & Restrooms Accessories	2 days	Wed 7/27/22	Thu 7/28/22																				
86		White out ceilings	2 days	Sat 8/13/22	Mon 8/15/22																				
87		Window Treatments	25 days	Tue 7/19/22	Tue 8/16/22																				
88		Field Measure	1 day	Tue 7/19/22	Tue 7/19/22																				

RW Dake Construction
1070 North Farms Road, Suite 3
Wallingford, CT 06495

M & T GAP - Harrison
389 Halstead Ave
Harrison, NY 10528

M & T Bank
One M & T Plaza
Buffalo, NY 14203

ID	Task Mode	Task Name	Duration	Start	Finish	Gantt Chart																																																							
89		Fabricate	4 wks	Wed 7/20/22	Thu 8/11/22																																																								
90		Install	1 day	Tue 8/16/22	Tue 8/16/22																																																								
91		Paints and Coatings	16 days	Thu 7/28/22	Mon 8/15/22																																																								
92		Prep and prime walls	3 days	Thu 7/28/22	Sat 7/30/22																																																								
93		1st Coat	2 days	Mon 8/1/22	Tue 8/2/22																																																								
94		Final Coat	2 days	Sat 8/13/22	Mon 8/15/22																																																								
95		Seal Windows	1 day	Wed 8/3/22	Wed 8/3/22																																																								
96		Flooring	9 days	Wed 8/3/22	Fri 8/12/22																																																								
97		Prep Floors	2 days	Wed 8/3/22	Thu 8/4/22																																																								
98		Install Base partial	2 days	Fri 8/5/22	Sat 8/6/22																																																								
99		Install Porcelain partial	3 days	Mon 8/8/22	Wed 8/10/22																																																								
100		Install Base partial	2 days	Thu 8/11/22	Fri 8/12/22																																																								
101		Furniture, Marketing & Dirtt	4 days	Tue 8/16/22	Fri 8/19/22																																																								
102		Install furniture, marketing &Dirtt	3 days	Tue 8/16/22	Thu 8/18/22																																																								
103		Final clean	1 day	Fri 8/19/22	Fri 8/19/22																																																								
104		Inspection	69 days	Tue 5/31/22	Fri 8/19/22																																																								
105		Final Inspection Phase 1	1 day	Fri 8/19/22	Fri 8/19/22																																																								
106																																																													
107		Phase 2 Teller Line Side	1 day	Tue 5/31/22	Tue 5/31/22																																																								
108		Construction	4 days	Tue 8/23/22	Fri 8/26/22																																																								
109		Save all bank equipment and furniture for reuse	2 days	Tue 8/23/22	Wed 8/24/22																																																								
110		Install temp walls, access ways and protection	1 day	Thu 8/25/22	Thu 8/25/22																																																								
111		Demo Teller Line	1 day	Fri 8/26/22	Fri 8/26/22																																																								
112		Demolition	18 days	Thu 8/25/22	Wed 9/14/22																																																								
113		Make safe break room protect IT rack	1 day	Thu 8/25/22	Thu 8/25/22																																																								
114		Demo Break room	1 day	Fri 8/26/22	Fri 8/26/22																																																								
115		Demo Restroom to be removed	1 day	Fri 8/26/22	Fri 8/26/22																																																								
116		Demo ceiling grid vestibule	1 day	Fri 8/26/22	Fri 8/26/22																																																								
117		Demo temp wall	1 day	Wed 9/14/22	Wed 9/14/22																																																								
118		Demo attick access	1 day	Sat 8/27/22	Sat 8/27/22																																																								

RW Dake Construction
1070 North Farms Road, Suite 3
Wallingford, CT 06495

M & T GAP - Harrison
389 Halstead Ave
Harrison, NY 10528

M & T Bank
One M & T Plaza
Buffalo, NY 14203

[illegible]

RW Dake Construction
1070 North Farms Road, Suite 3
Wallingford, CT 06495

M & T GAP - Harrison
389 Halstead Ave
Harrison, NY 10528

M & T Bank
One M & T Plaza
Buffalo, NY 14203

ID	i	Task Mode	Task Name	Duration	Start	Finish	ay 29, '22	Jun 5, '22	Jun 12, '22	Jun 19, '22	Jun 26, '22	Jul 3, '22	Jul 10, '22	Jul 17, '22	Jul 24, '22	Jul 31, '22	Aug 7, '22	Aug 14, '22	Aug 21, '22	Aug 28, '22	Sep 4, '22	Sep 11, '22	Sep 18, '22	Sep 25, '22
149			Finish lobby ceiling	1 day	Fri 8/26/22	Fri 8/26/22																		
150			Install ceiling grid in restroom with cuts	1 day	Sat 8/27/22	Sat 8/27/22																		
151			Install ceiling grid and tile cuts vestibule	1 day	Fri 8/26/22	Fri 8/26/22																		
152			Frame new attic stair drop and installs	1 day	Sat 8/27/22	Sat 8/27/22																		
153			Circulation ceiling grid	1 day	Mon 8/29/22	Mon 8/29/22																		
154			Above ceiling inspection	1 day	Wed 8/31/22	Wed 8/31/22																		
155			White out ceilings	1 day	Thu 9/1/22	Thu 9/1/22																		
156			In wall Inspection	1 day	Thu 9/1/22	Thu 9/1/22																		
157			Close Walls	1 day	Thu 9/1/22	Thu 9/1/22																		
158			Tape and compound	4 days	Fri 9/2/22	Tue 9/6/22																		
159			Doors and Frames	1 day	Wed 9/7/22	Wed 9/7/22																		
160			Infill Deal Draw Removal	3 days	Tue 8/30/22	Thu 9/1/22																		
161			Prep Infill for new Atm	3 days	Sat 9/3/22	Tue 9/6/22																		
162			Install new atm	1 day	Wed 9/7/22	Wed 9/7/22																		
163			Millwork	26 days	Fri 8/26/22	Sat 9/24/22																		
164			Layout teller line for VAT system work	1 day	Fri 8/26/22	Fri 8/26/22																		
165			Install teller counter case work	1 day	Sat 8/27/22	Sat 8/27/22																		
166			Install check desk	1 day	Sat 9/24/22	Sat 9/24/22																		
167			Breakroom millwork	1 day	Sat 8/27/22	Sat 8/27/22																		
168			Window Treatments	42 days	Tue 5/31/22	Tue 7/19/22																		
169			Field Measure	1 day	Tue 7/19/22	Tue 7/19/22																		
170			Fabricate	1 day	Tue 7/19/22	Tue 7/19/22																		
171			Install	1 day	Tue 5/31/22	Tue 5/31/22																		
172			Painting and Coatings	90 days	Tue 5/31/22	Tue 9/13/22																		
173			Prep prime walls	2 days	Wed 9/7/22	Thu 9/8/22																		
174			1st Coat	2 days	Fri 9/9/22	Sat 9/10/22																		
175			Final Coat	2 days	Tue 5/31/22	Wed 6/1/22																		
176			Install Wall Covering	2 days	Mon 9/12/22	Tue 9/13/22																		
177			Flooring	11 days	Mon 9/12/22	Fri 9/23/22																		
178			Prep Floors	2 days	Mon 9/12/22	Tue 9/13/22																		

D		Task Name	Duration	Start	Finish	May 29, '22	Jun 5, '22	Jun 12, '22	Jun 19, '22	Jun 26, '22	Jul 3, '22	Jul 10, '22	Jul 17, '22	Jul 24, '22	Jul 31, '22	Aug 7, '22	Aug 14, '22	Aug 21, '22	Aug 28, '22	Sep 4, '22	Sep 11, '22	Sep 18, '22	Sep 25, '22		
						M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S
179		Install carpet	2 days	Wed 9/14/22	Thu 9/15/22																				
180		Install porcelain	3 days	Mon 9/19/22	Wed 9/21/22																				
181		Install Vinyl	2 days	Fri 9/16/22	Sat 9/17/22																				
182		Install Base	2 days	Thu 9/22/22	Fri 9/23/22																				
183		Furniture & Marketing	3 days	Mon 9/12/22	Wed 9/14/22																				
184		Install Marketing	2 days	Mon 9/12/22	Tue 9/13/22																				
185		Install Furniture	2 days	Mon 9/12/22	Tue 9/13/22																				
186		Final Clean	1 day	Wed 9/14/22	Wed 9/14/22																				
187		Inspection	1 day	Wed 9/14/22	Wed 9/14/22																				
188		Final Inspection	1 day	Wed 9/14/22	Wed 9/14/22																				
