

SUBMITTAL COVERSHEET **Nanuet UFSD –Phase 3 Projects**

Architect:
KSQ Architects
215 W 40th Street, 15th Floor
New York, NY 10018

Owner:
Nanuet Union Free School District
101 Church Street
Nanuet, NY 10954

Construction Manager:
Jacobs
One Penn Plaza, 54th floor
New York, NY 10019

Contractor: Joe Lombardo Plumbing & Heating of Rockland Inc

Contract: Ron Lombardo

Address: 321 Spook Rock Road Suite 109A

845-357-6537

Telephone:

Suffern, New York 10901

Fax: 845-357-8529

School Name: Nanuet Union Free School District Phase 3 Bond Projects @ Barr Middle School & Nanuet High School

Type of Submittal:

Re-submittal: ☐ No ☐ Yes

☐ Shop Drawings

☐ Product Data

☐ Schedule

☐ Sample

☐

☐ Test Report

☐ Certificate

☐ Color Sample

☐ Warranty

☐

Submittal Description:

LOMBARDO'S PROJECT MILESTONE SCHEDULE

Product Name:

Manufacturer:

LOMBARDO

**Subcontractor/
Supplier:**

PEARLS CONSTRUCTION

References:

Spec. Section No.: 011100

Drawing No(s):

Paragraph:

Rm. or Detail No(s):

Architect's/ Engineer's Review Stamp

Contractor Review Statement:

These documents have been checked for accuracy and coordinated with job conditions and Contract requirements by this office and have been found to comply with the provisions of the Contract Documents.

Ronald J. Lombardo

10.11.23


Name:

Date:

Company Name:

Joe Lombardo Plumbing & Heating of Rockland Inc.

Remarks:

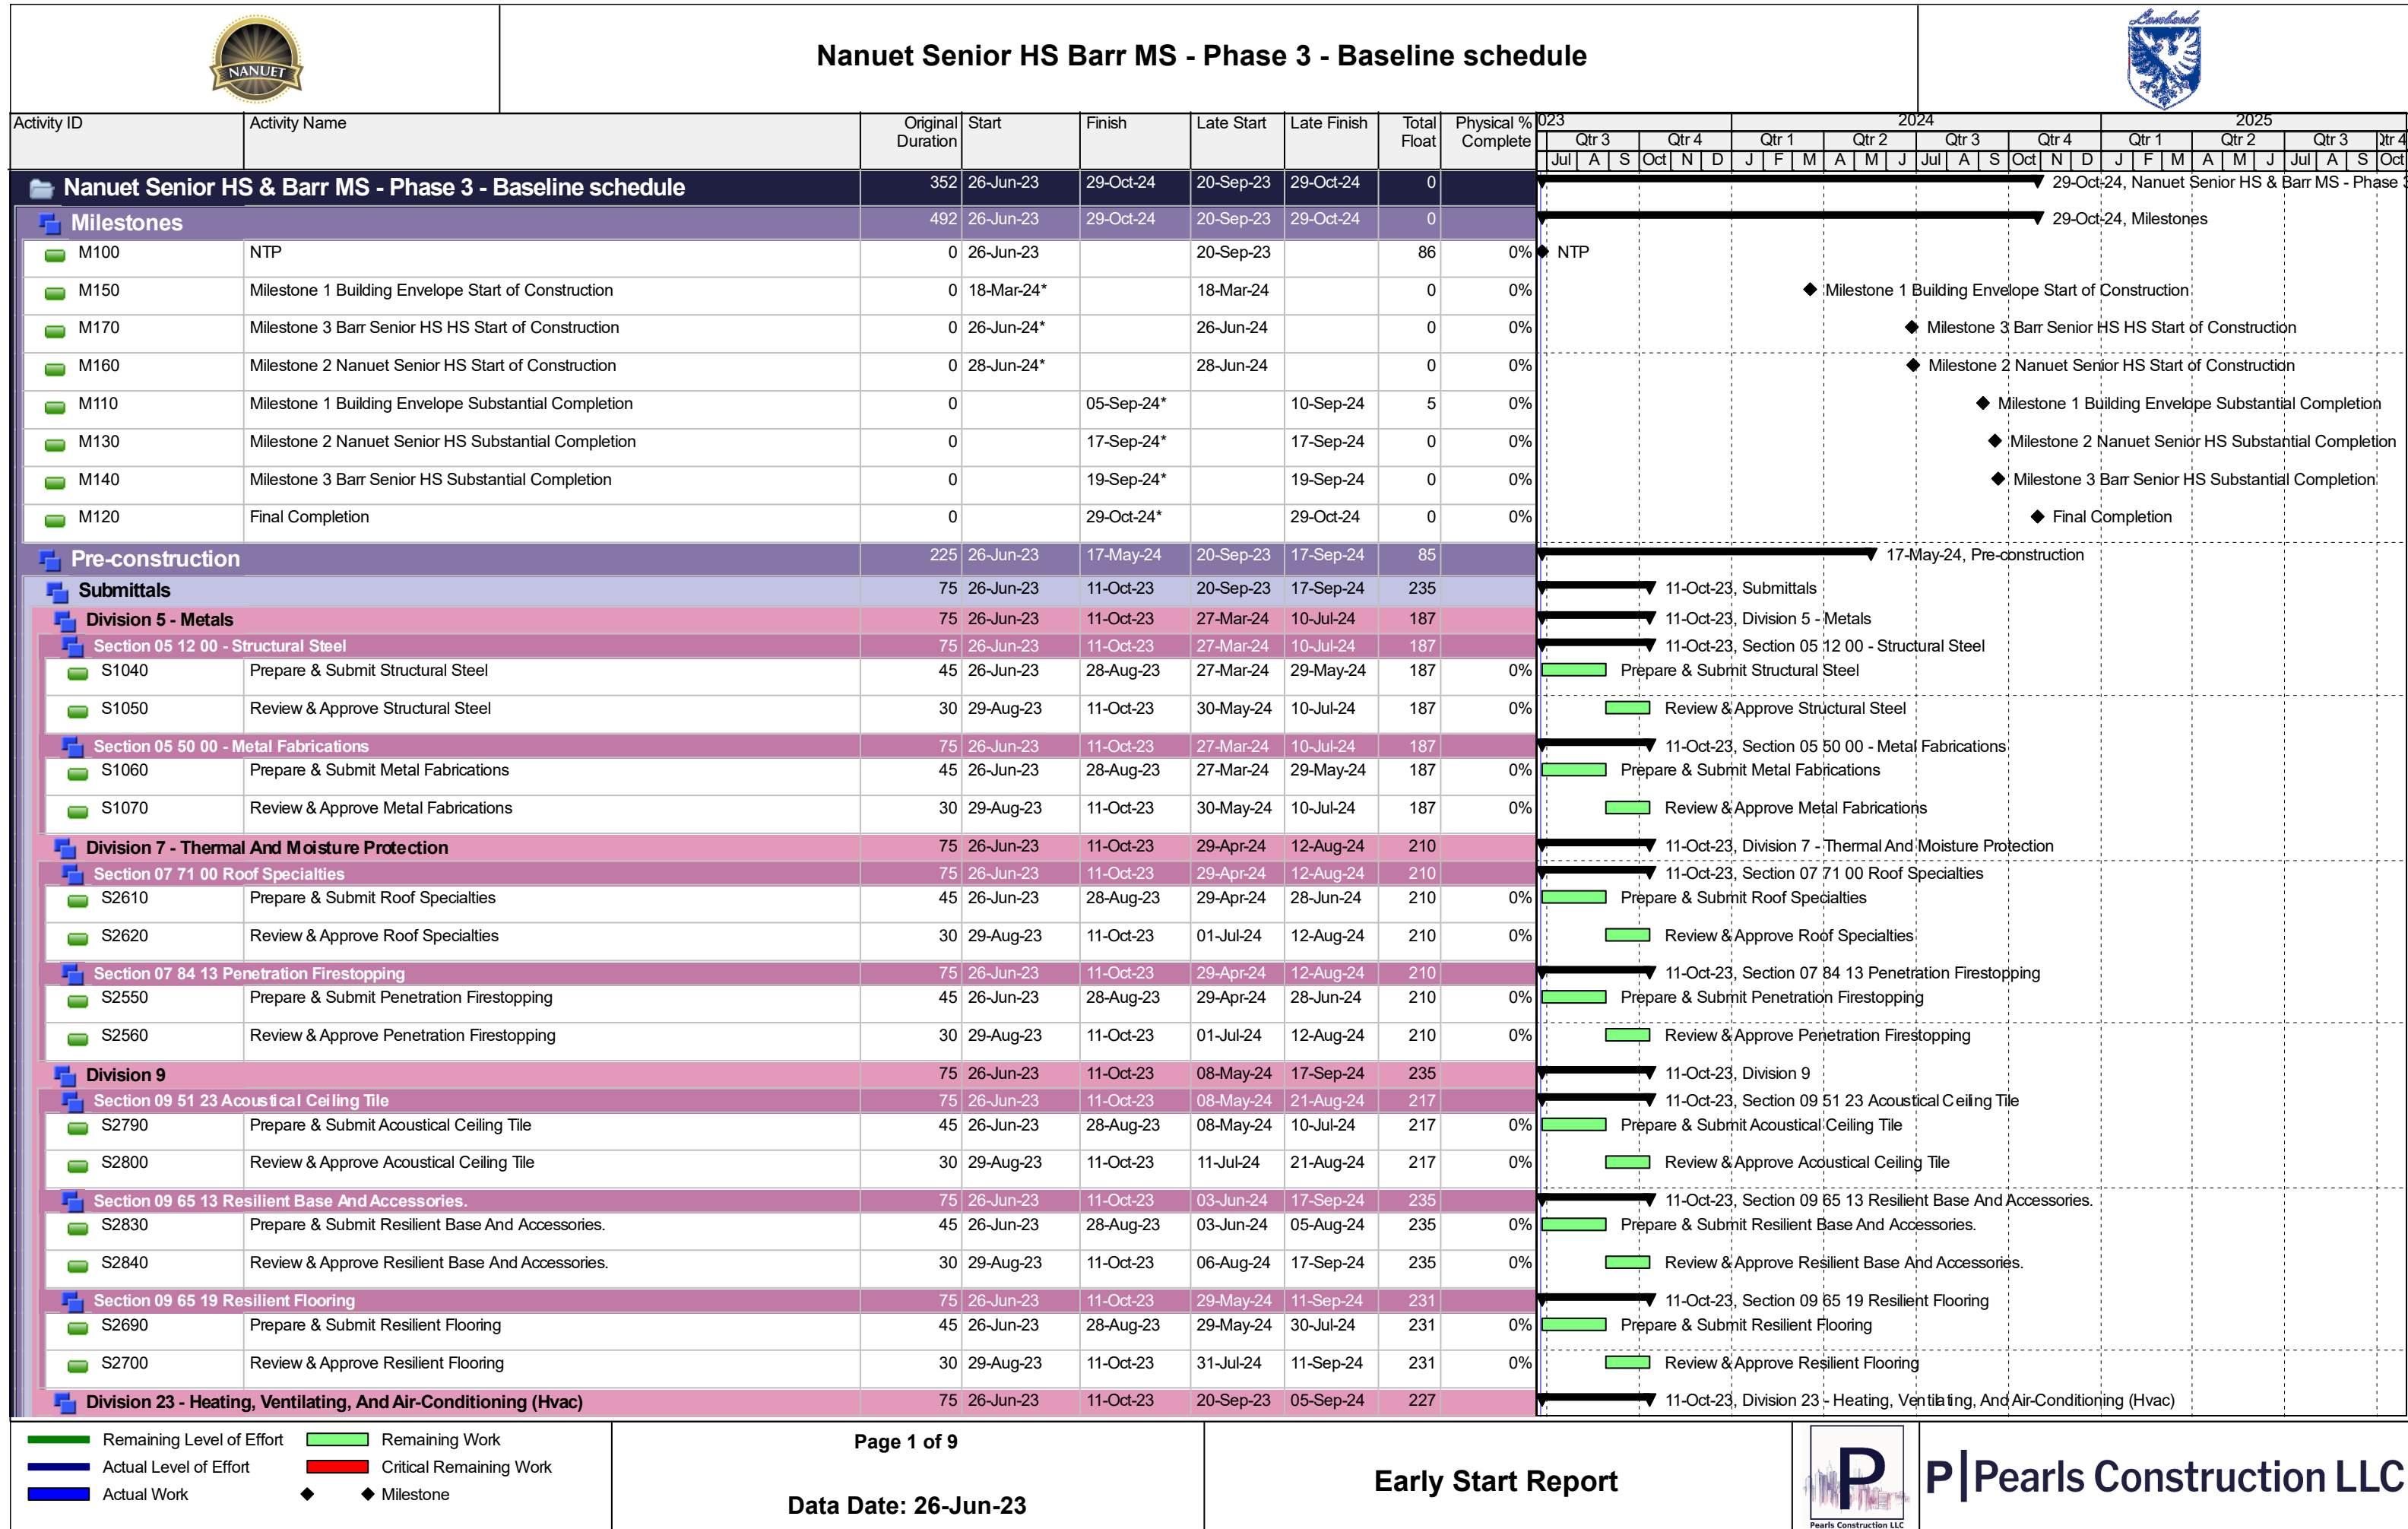



Nanuet Senior HS Barr MS - Phase 3 - Baseline schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	2023												2024												2025											
									Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4								
									Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct								
Section 23 05 01 Basic Hvac Materials And Methods									11-Oct-23, Section 23 05 01 Basic Hvac Materials And Methods																																			
S2530	Prepare & Submit Basic Hvac Materials And Methods	45	26-Jun-23	28-Aug-23	11-Apr-24	12-Jun-24	198	0%	Prepare & Submit Basic Hvac Materials And Methods																																			
S2540	Review & Approve Basic Hvac Materials And Methods	30	29-Aug-23	11-Oct-23	13-Jun-24	25-Jul-24	198	0%	Review & Approve Basic Hvac Materials And Methods																																			
Section 23 05 16 Expansion Fittings And Loops For Hvac Piping									11-Oct-23, Section 23 05 16 Expansion Fittings And Loops For Hvac Piping																																			
S2010	Prepare & Submit Expansion Fittings And Loops For Hvac Piping	45	26-Jun-23	28-Aug-23	11-Apr-24	12-Jun-24	198	0%	Prepare & Submit Expansion Fittings And Loops For Hvac Piping																																			
S2020	Review & Approve Expansion Fittings And Loops For Hvac Piping	30	29-Aug-23	11-Oct-23	13-Jun-24	25-Jul-24	198	0%	Review & Approve Expansion Fittings And Loops For Hvac Piping																																			
Section 23 05 19 Meters And Gauges For Hvac Piping									11-Oct-23, Section 23 05 19 Meters And Gauges For Hvac Piping																																			
S1990	Prepare & Submit Meters And Gauges For Hvac Piping	45	26-Jun-23	28-Aug-23	11-Apr-24	12-Jun-24	198	0%	Prepare & Submit Meters And Gauges For Hvac Piping																																			
S2000	Review & Approve Meters And Gauges For Hvac Piping	30	29-Aug-23	11-Oct-23	13-Jun-24	25-Jul-24	198	0%	Review & Approve Meters And Gauges For Hvac Piping																																			
Section 23 05 48 Vibration Controls For Hvac Piping And Equipment									11-Oct-23, Section 23 05 48 Vibration Controls For Hvac Piping And Equipment																																			
S2110	Prepare & Submit Vibration Controls For Hvac Piping And Equipment	45	26-Jun-23	28-Aug-23	20-Sep-23	27-Nov-23	60	0%	Prepare & Submit Vibration Controls For Hvac Piping And Equipment																																			
S2120	Review & Approve Vibration Controls For Hvac Piping And Equipment	30	29-Aug-23	11-Oct-23	28-Nov-23	10-Jan-24	60	0%	Review & Approve Vibration Controls For Hvac Piping And Equipment																																			
Section 23 05 53 Identification For Hvac Piping And Equipment									11-Oct-23, Section 23 05 53 Identification For Hvac Piping And Equipment																																			
S2210	Prepare & Submit Identification For Hvac Piping And Equipment	45	26-Jun-23	28-Aug-23	11-Apr-24	12-Jun-24	198	0%	Prepare & Submit Identification For Hvac Piping And Equipment																																			
S2220	Review & Approve Identification For Hvac Piping And Equipment	30	29-Aug-23	11-Oct-23	13-Jun-24	25-Jul-24	198	0%	Review & Approve Identification For Hvac Piping And Equipment																																			
Section 23 05 93 Testing, Adjusting, And Balancing For Hvac									11-Oct-23, Section 23 05 93 Testing, Adjusting, And Balancing For Hvac																																			
S2310	Prepare & Submit Testing, Adjusting, And Balancing For Hvac	45	26-Jun-23	28-Aug-23	08-May-24	10-Jul-24	217	0%	Prepare & Submit Testing, Adjusting, And Balancing For Hvac																																			
S2320	Review & Approve Testing, Adjusting, And Balancing For Hvac	30	29-Aug-23	11-Oct-23	11-Jul-24	21-Aug-24	217	0%	Review & Approve Testing, Adjusting, And Balancing For Hvac																																			
Section 23 07 13 Duct Insulation									11-Oct-23, Section 23 07 13 Duct Insulation																																			
S2410	Prepare & Submit Duct Insulation	45	26-Jun-23	28-Aug-23	25-Apr-24	26-Jun-24	208	0%	Prepare & Submit Duct Insulation																																			
S2420	Review & Approve Duct Insulation	30	29-Aug-23	11-Oct-23	27-Jun-24	08-Aug-24	208	0%	Review & Approve Duct Insulation																																			
Section 23 07 16 Hvac Equipment Insulation									11-Oct-23, Section 23 07 16 Hvac Equipment Insulation																																			
S2510	Prepare & Submit HVAC Equipment Insulation	45	26-Jun-23	28-Aug-23	08-May-24	10-Jul-24	217	0%	Prepare & Submit HVAC Equipment Insulation																																			
S2520	Review & Approve HVAC Equipment Insulation	30	29-Aug-23	11-Oct-23	11-Jul-24	21-Aug-24	217	0%	Review & Approve HVAC Equipment Insulation																																			
Section 23 07 19 Hvac Piping Insulation									11-Oct-23, Section 23 07 19 Hvac Piping Insulation																																			
S1220	Prepare & Submit HVAC Piping Insulation	45	26-Jun-23	28-Aug-23	04-Apr-24	05-Jun-24	193	0%	Prepare & Submit HVAC Piping Insulation																																			
S1230	Review & Approve HVAC Piping Insulation	30	29-Aug-23	11-Oct-23	06-Jun-24	18-Jul-24	193	0%	Review & Approve HVAC Piping Insulation																																			
Section 23 08 00 Commissioning Of Hvac									11-Oct-23, Section 23 08 00 Commissioning Of Hvac																																			
S1970	Prepare & Submit Commissioning Of HVAC	45	26-Jun-23	28-Aug-23	22-May-24	24-Jul-24	227	0%	Prepare & Submit Commissioning Of HVAC																																			
S1980	Review & Approve Commissioning Of HVAC	30	29-Aug-23	11-Oct-23	25-Jul-24	05-Sep-24	227	0%	Review & Approve Commissioning Of HVAC																																			
Section 23 09 23 Direct-Digital Control System For Hvac									11-Oct-23, Section 23 09 23 Direct-Digital Control System For Hvac																																			
S2090	Prepare & Submit Direct-Digital Control System For Hvac	45	26-Jun-23	28-Aug-23	25-Apr-24	26-Jun-24	208	0%	Prepare & Submit Direct-Digital Control System For Hvac																																			
S2100	Review & Approve Direct-Digital Control System For Hvac	30	29-Aug-23	11-Oct-23	27-Jun-24	08-Aug-24	208	0%	Review & Approve Direct-Digital Control System For Hvac																																			
Section 23 21 13 Hydronic Piping									11-Oct-23, Section 23 21 13 Hydronic Piping																																			
S2190	Prepare & Submit Hydronic Piping	45	26-Jun-23	28-Aug-23	08-Apr-24	07-Jun-24	195	0%	Prepare & Submit Hydronic Piping																																			
S2200	Review & Approve Hydronic Piping	30	29-Aug-23	11-Oct-23	10-Jun-24	22-Jul-24	195	0%	Review & Approve Hydronic Piping																																			
Section 23 21 14 Hydronic Specialties									11-Oct-23, Section 23 21 14 Hydronic Specialties																																			



Remaining Level of Effort Critical Remaining Work Actual Work ◆ ◆ Milestone Page 3 of 9 Data Date: 26-Jun-23	Early Start Report	P P Pearls Construction LLC
--	--	---



Nanuet Senior HS Barr MS - Phase 3 - Baseline schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	023		2024												2025																			
									Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4						
									Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct						
	S2480	Review & Approve Heat Exchangers For Hvac	30	29-Aug-23	11-Oct-23	10-Jun-24	22-Jul-24	195	0%			Review & Approve Heat Exchangers For Hvac																														
	Section 23 62 13 Air Cooled Refrigerant Compressor And Condenser Unit		75	26-Jun-23	11-Oct-23	08-Apr-24	22-Jul-24	195				11-Oct-23, Section 23 62 13 Air Cooled Refrigerant Compressor And Condenser Unit																														
	S2030	Prepare & Submit Air Cooled Refrigerant Compressor And Condenser Unit	45	26-Jun-23	28-Aug-23	08-Apr-24	07-Jun-24	195	0%		Prepare & Submit Air Cooled Refrigerant Compressor And Condenser Unit																															
	S2040	Review & Approve Air Cooled Refrigerant Compressor And Condenser Unit	30	29-Aug-23	11-Oct-23	10-Jun-24	22-Jul-24	195	0%			Review & Approve Air Cooled Refrigerant Compressor And Condenser Unit																														
	Section 23 73 13 Indoor Air-Handling Units		75	26-Jun-23	11-Oct-23	13-Nov-23	04-Mar-24	96				11-Oct-23, Section 23 73 13 Indoor Air-Handling Units																														
	S2130	Prepare & Submit Indoor Air-Handling Units	45	26-Jun-23	28-Aug-23	13-Nov-23	19-Jan-24	96	0%		Prepare & Submit Indoor Air-Handling Units																															
	S2140	Review & Approve Indoor Air-Handling Units	30	29-Aug-23	11-Oct-23	22-Jan-24	04-Mar-24	96	0%			Review & Approve Indoor Air-Handling Units																														
	Section 23 74 13 Packaged Rooftop Units		75	26-Jun-23	11-Oct-23	08-Apr-24	22-Jul-24	195				11-Oct-23, Section 23 74 13 Packaged Rooftop Units																														
	S2230	Prepare & Submit Packaged Rooftop Units	45	26-Jun-23	28-Aug-23	08-Apr-24	07-Jun-24	195	0%		Prepare & Submit Packaged Rooftop Units																															
	S2240	Review & Approve Packaged Rooftop Units	30	29-Aug-23	11-Oct-23	10-Jun-24	22-Jul-24	195	0%			Review & Approve Packaged Rooftop Units																														
	Section 23 81 29 Variable Refrigerant Flow Hvac Systems		75	26-Jun-23	11-Oct-23	08-Apr-24	22-Jul-24	195				11-Oct-23, Section 23 81 29 Variable Refrigerant Flow Hvac Systems																														
	S2330	Prepare & Submit Variable Refrigerant Flow Hvac Systems	45	26-Jun-23	28-Aug-23	08-Apr-24	07-Jun-24	195	0%		Prepare & Submit Variable Refrigerant Flow Hvac Systems																															
	S2340	Review & Approve Variable Refrigerant Flow Hvac Systems	30	29-Aug-23	11-Oct-23	10-Jun-24	22-Jul-24	195	0%			Review & Approve Variable Refrigerant Flow Hvac Systems																														
	Section 23 82 00 Convection Heating And Cooling Units		75	26-Jun-23	11-Oct-23	08-Apr-24	22-Jul-24	195				11-Oct-23, Section 23 82 00 Convection Heating And Cooling Units																														
	S2430	Prepare & Submit Convection Heating And Cooling Units	45	26-Jun-23	28-Aug-23	08-Apr-24	07-Jun-24	195	0%		Prepare & Submit Convection Heating And Cooling Units																															
	S2440	Review & Approve Convection Heating And Cooling Units	30	29-Aug-23	11-Oct-23	10-Jun-24	22-Jul-24	195	0%			Review & Approve Convection Heating And Cooling Units																														
	Division 26 - Electrical		75	26-Jun-23	11-Oct-23	10-May-24	23-Aug-24	219				11-Oct-23, Division 26 - Electrical																														
	Section 26 29 23 Variable-Frequency Motor Controllers		75	26-Jun-23	11-Oct-23	10-May-24	23-Aug-24	219				11-Oct-23, Section 26 29 23 Variable-Frequency Motor Controllers																														
	S1670	Prepare & Submit Variable-Frequency Motor Controllers	45	26-Jun-23	28-Aug-23	10-May-24	12-Jul-24	219	0%		Prepare & Submit Variable-Frequency Motor Controllers																															
	S1680	Review & Approve Variable-Frequency Motor Controllers	30	29-Aug-23	11-Oct-23	15-Jul-24	23-Aug-24	219	0%			Review & Approve Variable-Frequency Motor Controllers																														
	Procurement		150	12-Oct-23	17-May-24	11-Jan-24	23-Aug-24	69				17-May-24, Procurement																														
	S1300	Fabricate & Deliver R-MS-1 & 2	40	12-Oct-23	11-Dec-23	18-Jun-24	13-Aug-24	171	0%			Fabricate & Deliver R-MS-1 & 2																														
	S1310	Fabricate & Deliver EF-8, 10, 21 & 23	150	12-Oct-23	17-May-24	11-Jan-24	12-Aug-24	60	0%			Fabricate & Deliver EF-8, 10, 21 & 23																														
	S1320	Fabricate & Deliver Dampers	88	12-Oct-23	21-Feb-24	11-Apr-24	13-Aug-24	123	0%			Fabricate & Deliver Dampers																														
	S1340	Fabricate & Deliver UV-MS- 1-41	55	12-Oct-23	03-Jan-24	06-Jun-24	22-Aug-24	163	0%			Fabricate & Deliver UV-MS- 1-41																														
	S1350	Fabricate & Deliver HP-MS-3-9	60	12-Oct-23	10-Jan-24	20-May-24	12-Aug-24	150	0%			Fabricate & Deliver HP-MS-3-9																														
	S1360	Fabricate & Deliver CV-HS-1-11	40	12-Oct-23	11-Dec-23	25-Jun-24	20-Aug-24	176	0%			Fabricate & Deliver CV-HS-1-11																														
	S1370	Fabricate & Deliver UH-HS-1	20	12-Oct-23	08-Nov-23	29-Jul-24	23-Aug-24	199	0%			Fabricate & Deliver UH-HS-1																														
	S1380	Fabricate & Deliver CUH- HS-1, 2, 3	40	12-Oct-23	11-Dec-23	25-Jun-24	20-Aug-24	176	0%			Fabricate & Deliver CUH- HS-1, 2, 3																														
	S1390	Fabricate & Deliver R2-1, 2, 3, & 4	40	12-Oct-23	11-Dec-23	25-Jun-24	20-Aug-24	176	0%			Fabricate & Deliver R2-1, 2, 3, & 4																														
	S1400	Fabricate & Deliver F-HS-2 & 3	150	12-Oct-23	17-May-24	11-Jan-24	12-Aug-24	60	0%			Fabricate & Deliver F-HS-2 & 3																														
	S1410	Fabricate & Deliver L-1 Louver with bird screen	88	12-Oct-23	21-Feb-24	22-Apr-24	22-Aug-24	130	0%			Fabricate & Deliver L-1 Louver with bird screen																														
	S1420	Fabricate & Deliver RTU-HS- 4 & 5	110	12-Oct-23	22-Mar-24	14-Mar-24	15-Aug-24	103	0%			Fabricate & Deliver RTU-HS- 4 & 5																														
	S1430	Fabricate & Deliver BC-HS-1 & 2	70	12-Oct-23	25-Jan-24	06-Mar-24	11-Jun-24	97	0%			Fabricate & Deliver BC-HS-1 & 2																														
	S1440	Fabricate & Deliver HC-HS-2 to 4	40	12-Oct-23	11-Dec-23	28-Jun-24	23-Aug-24	179	0%			Fabricate & Deliver HC-HS-2 to 4																														

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work


Milestone





Nanuet Senior HS Barr MS - Phase 3 - Baseline schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	2023		2024												2025													
									Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4
									Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct
 S1450	Fabricate & Deliver AHU-HS-3	120	12-Oct-23	05-Apr-24	05-Mar-24	20-Aug-24	96	0%			 Fabricate & Deliver AHU-HS-3																									
 S1460	Fabricate & Deliver ACCU-HS 2	60	12-Oct-23	10-Jan-24	23-May-24	15-Aug-24	153	0%			 Fabricate & Deliver ACCU-HS 2																									
 S1470	Fabricate & Deliver CP-HS-2	140	12-Oct-23	03-May-24	08-Feb-24	23-Aug-24	79	0%			 Fabricate & Deliver CP-HS-2																									
 S1480	Fabricate & Deliver HX-HS-2	40	12-Oct-23	11-Dec-23	28-Jun-24	23-Aug-24	179	0%			 Fabricate & Deliver HX-HS-2																									
 S1490	Fabricate & Deliver P-HS-3 & 4	120	12-Oct-23	05-Apr-24	05-Mar-24	20-Aug-24	96	0%			 Fabricate & Deliver P-HS-3 & 4																									
 S1500	Fabricate & Deliver B&G Suction Diffuser	80	12-Oct-23	08-Feb-24	28-Mar-24	18-Jul-24	113	0%			 Fabricate & Deliver B&G Suction Diffuser																									
 S1510	Fabricate & Deliver B&G Triple Duty Valve	100	12-Oct-23	08-Mar-24	29-Feb-24	18-Jul-24	93	0%			 Fabricate & Deliver B&G Triple Duty Valve																									
 S1520	Fabricate & Deliver Flex Hose 6"X 24"	30	12-Oct-23	27-Nov-23	15-Jul-24	23-Aug-24	189	0%			 Fabricate & Deliver Flex Hose 6"X 24"																									
 S1530	Fabricate & Deliver EXP-HS-2 & 3	80	12-Oct-23	08-Feb-24	03-May-24	23-Aug-24	139	0%			 Fabricate & Deliver EXP-HS-2 & 3																									
 S1540	Fabricate & Deliver Flex Hose Exp Loops	30	12-Oct-23	27-Nov-23	15-Jul-24	23-Aug-24	189	0%			 Fabricate & Deliver Flex Hose Exp Loops																									
 S3200	Fabricate & Deliver FT-MS-1	35	12-Oct-23	04-Dec-23	05-Jul-24	22-Aug-24	183	0%			 Fabricate & Deliver FT-MS-1																									
 Construction		167	26-Jan-24	19-Sep-24	07-Jun-24	19-Sep-24	0				 19-Sep-24, Construction																									
 Mobilization		10	26-Jan-24	08-Feb-24	12-Jun-24	25-Jun-24	97				 08-Feb-24, Mobilization																									
 C6920	Mobilization & Site Prep.	10	26-Jan-24	08-Feb-24	12-Jun-24	25-Jun-24	97	0%			 Mobilization & Site Prep.																									
 Nanuet Senior HS		130	18-Mar-24	17-Sep-24	07-Jun-24	17-Sep-24	0				 17-Sep-24, Nanuet Senior HS																									
 Demolition		14	28-Jun-24	18-Jul-24	28-Jun-24	18-Jul-24	0				 18-Jul-24, Demolition																									
 C5910	Remove Spandrel Panels In Existing Storefront Window System - Basement - Nanuet Senior HS	1	28-Jun-24	28-Jun-24	28-Jun-24	28-Jun-24	0	0%			 Remove Spandrel Panels In Existing Storefront Window System - B																									
 C7030	Remove HVAC Ducts & Piping - Nanuet Senior HS	14	28-Jun-24	18-Jul-24	28-Jun-24	18-Jul-24	0	0%			 Remove HVAC Ducts & Piping - Nanuet Senior HS																									
 C5920	Remove Unit Ventilator - First Floor - Nanuet Senior HS	1	01-Jul-24	01-Jul-24	01-Jul-24	01-Jul-24	0	0%			 Remove Unit Ventilator - First Floor - Nanuet Senior HS																									
 C5950	Remove & Salvage Existing Wainscoting Pipe Enclosure - First Floor - Nanuet Senior HS	1	02-Jul-24	02-Jul-24	02-Jul-24	02-Jul-24	0	0%			 Remove & Salvage Existing Wainscoting Pipe Enclosure - First Flo																									
 C5930	Remove Spandrel Panels In Existing Storefront Window System - Second Floor - Nanuet Senior HS	1	03-Jul-24	03-Jul-24	03-Jul-24	03-Jul-24	0	0%			 Remove Spandrel Panels In Existing Storefront Window System - S																									
 Asbestos Abatement Nanuet Senior HS		83	18-Mar-24	11-Jul-24	07-Jun-24	11-Jul-24	0				 11-Jul-24, Asbestos Abatement Nanuet Senior HS																									
 C5830	Perform Asbestos Abatement @ Roof - Nanuet Senior HS	15	18-Mar-24	05-Apr-24	07-Jun-24	27-Jun-24	59	0%			 Perform Asbestos Abatement @ Roof - Nanuet Senior HS																									
 C5820	Perform Asbestos Abatement @ Second Floor - Nanuet Senior HS	5	05-Jul-24	11-Jul-24	05-Jul-24	11-Jul-24	0	0%			 Perform Asbestos Abatement @ Second Floor - Nanuet Senior HS																									
 Basement		47	12-Jul-24	17-Sep-24	12-Jul-24	17-Sep-24	0				 17-Sep-24, Basement																									
 Architectural		6	10-Sep-24	17-Sep-24	10-Sep-24	17-Sep-24	0				 17-Sep-24, Architectural																									
 C6870	Patch Ceilings - Basement - Nanuet Senior HS	2	10-Sep-24	11-Sep-24	10-Sep-24	11-Sep-24	0	0%			 Patch Ceilings - Basement - Nanuet Senior HS																									
 C6910	Patch Walls - Basement - Nanuet Senior HS	3	12-Sep-24	16-Sep-24	12-Sep-24	16-Sep-24	0	0%			 Patch Walls - Basement - Nanuet Senior HS																									
 C6760	Patch Flooring - Basement - Nanuet Senior HS	1	17-Sep-24	17-Sep-24	17-Sep-24	17-Sep-24	0	0%			 Patch Flooring - Basement - Nanuet Senior HS																									
 Mechanical		41	12-Jul-24	09-Sep-24	12-Jul-24	09-Sep-24	0				 09-Sep-24, Mechanical																									
 C6600	Install Mechanical Ducts & Pipes Hangers - Basement - Nanuet Senior HS	2	12-Jul-24	15-Jul-24	12-Jul-24	15-Jul-24	0	0%			 Install Mechanical Ducts & Pipes Hangers - Basement - Nanuet S																									
 C6630	Install Above ceiling Terminal Equipment - Basement - Nanuet Senior HS	6	16-Jul-24	23-Jul-24	25-Jul-24	01-Aug-24	7	0%			 Install Above ceiling Terminal Equipment - Basement - Nanuet S																									
 C6610	Install HVAC Ducts & Pipes - Basement - Nanuet Senior HS	10	19-Jul-24	01-Aug-24	19-Jul-24	01-Aug-24	0	0%			 Install HVAC Ducts & Pipes - Basement - Nanuet Senior HS																									
 C6620	Insulate HVAC Ducts & Pipes - Basement - Nanuet Senior HS	8	02-Aug-24	13-Aug-24	02-Aug-24	13-Aug-24	0	0%			 Insulate HVAC Ducts & Pipes - Basement - Nanuet Senior HS																									
 C6640	Mechanical Rough-Ins Inspection - Basement - Nanuet Senior HS	3	14-Aug-24	16-Aug-24	14-Aug-24	16-Aug-24	0	0%			 Mechanical Rough-Ins Inspection - Basement - Nanuet Senior																									

Remaining Level of Effort

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone



Nanuet Senior HS Barr MS - Phase 3 - Baseline schedule



Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	2023												2024												2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
									Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
									Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
	C5870	Remove Roof Top Exhaust Fan & All Associated Controls & Wiring - Roof - Nanuet Senior HS	8	28-Jun-24	10-Jul-24	28-Jun-24	10-Jul-24	0	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												</

Remaining Level of Effort

Actual Level of Effort


Actual Work

Remaining Work

Critical Remaining Work

Milestone



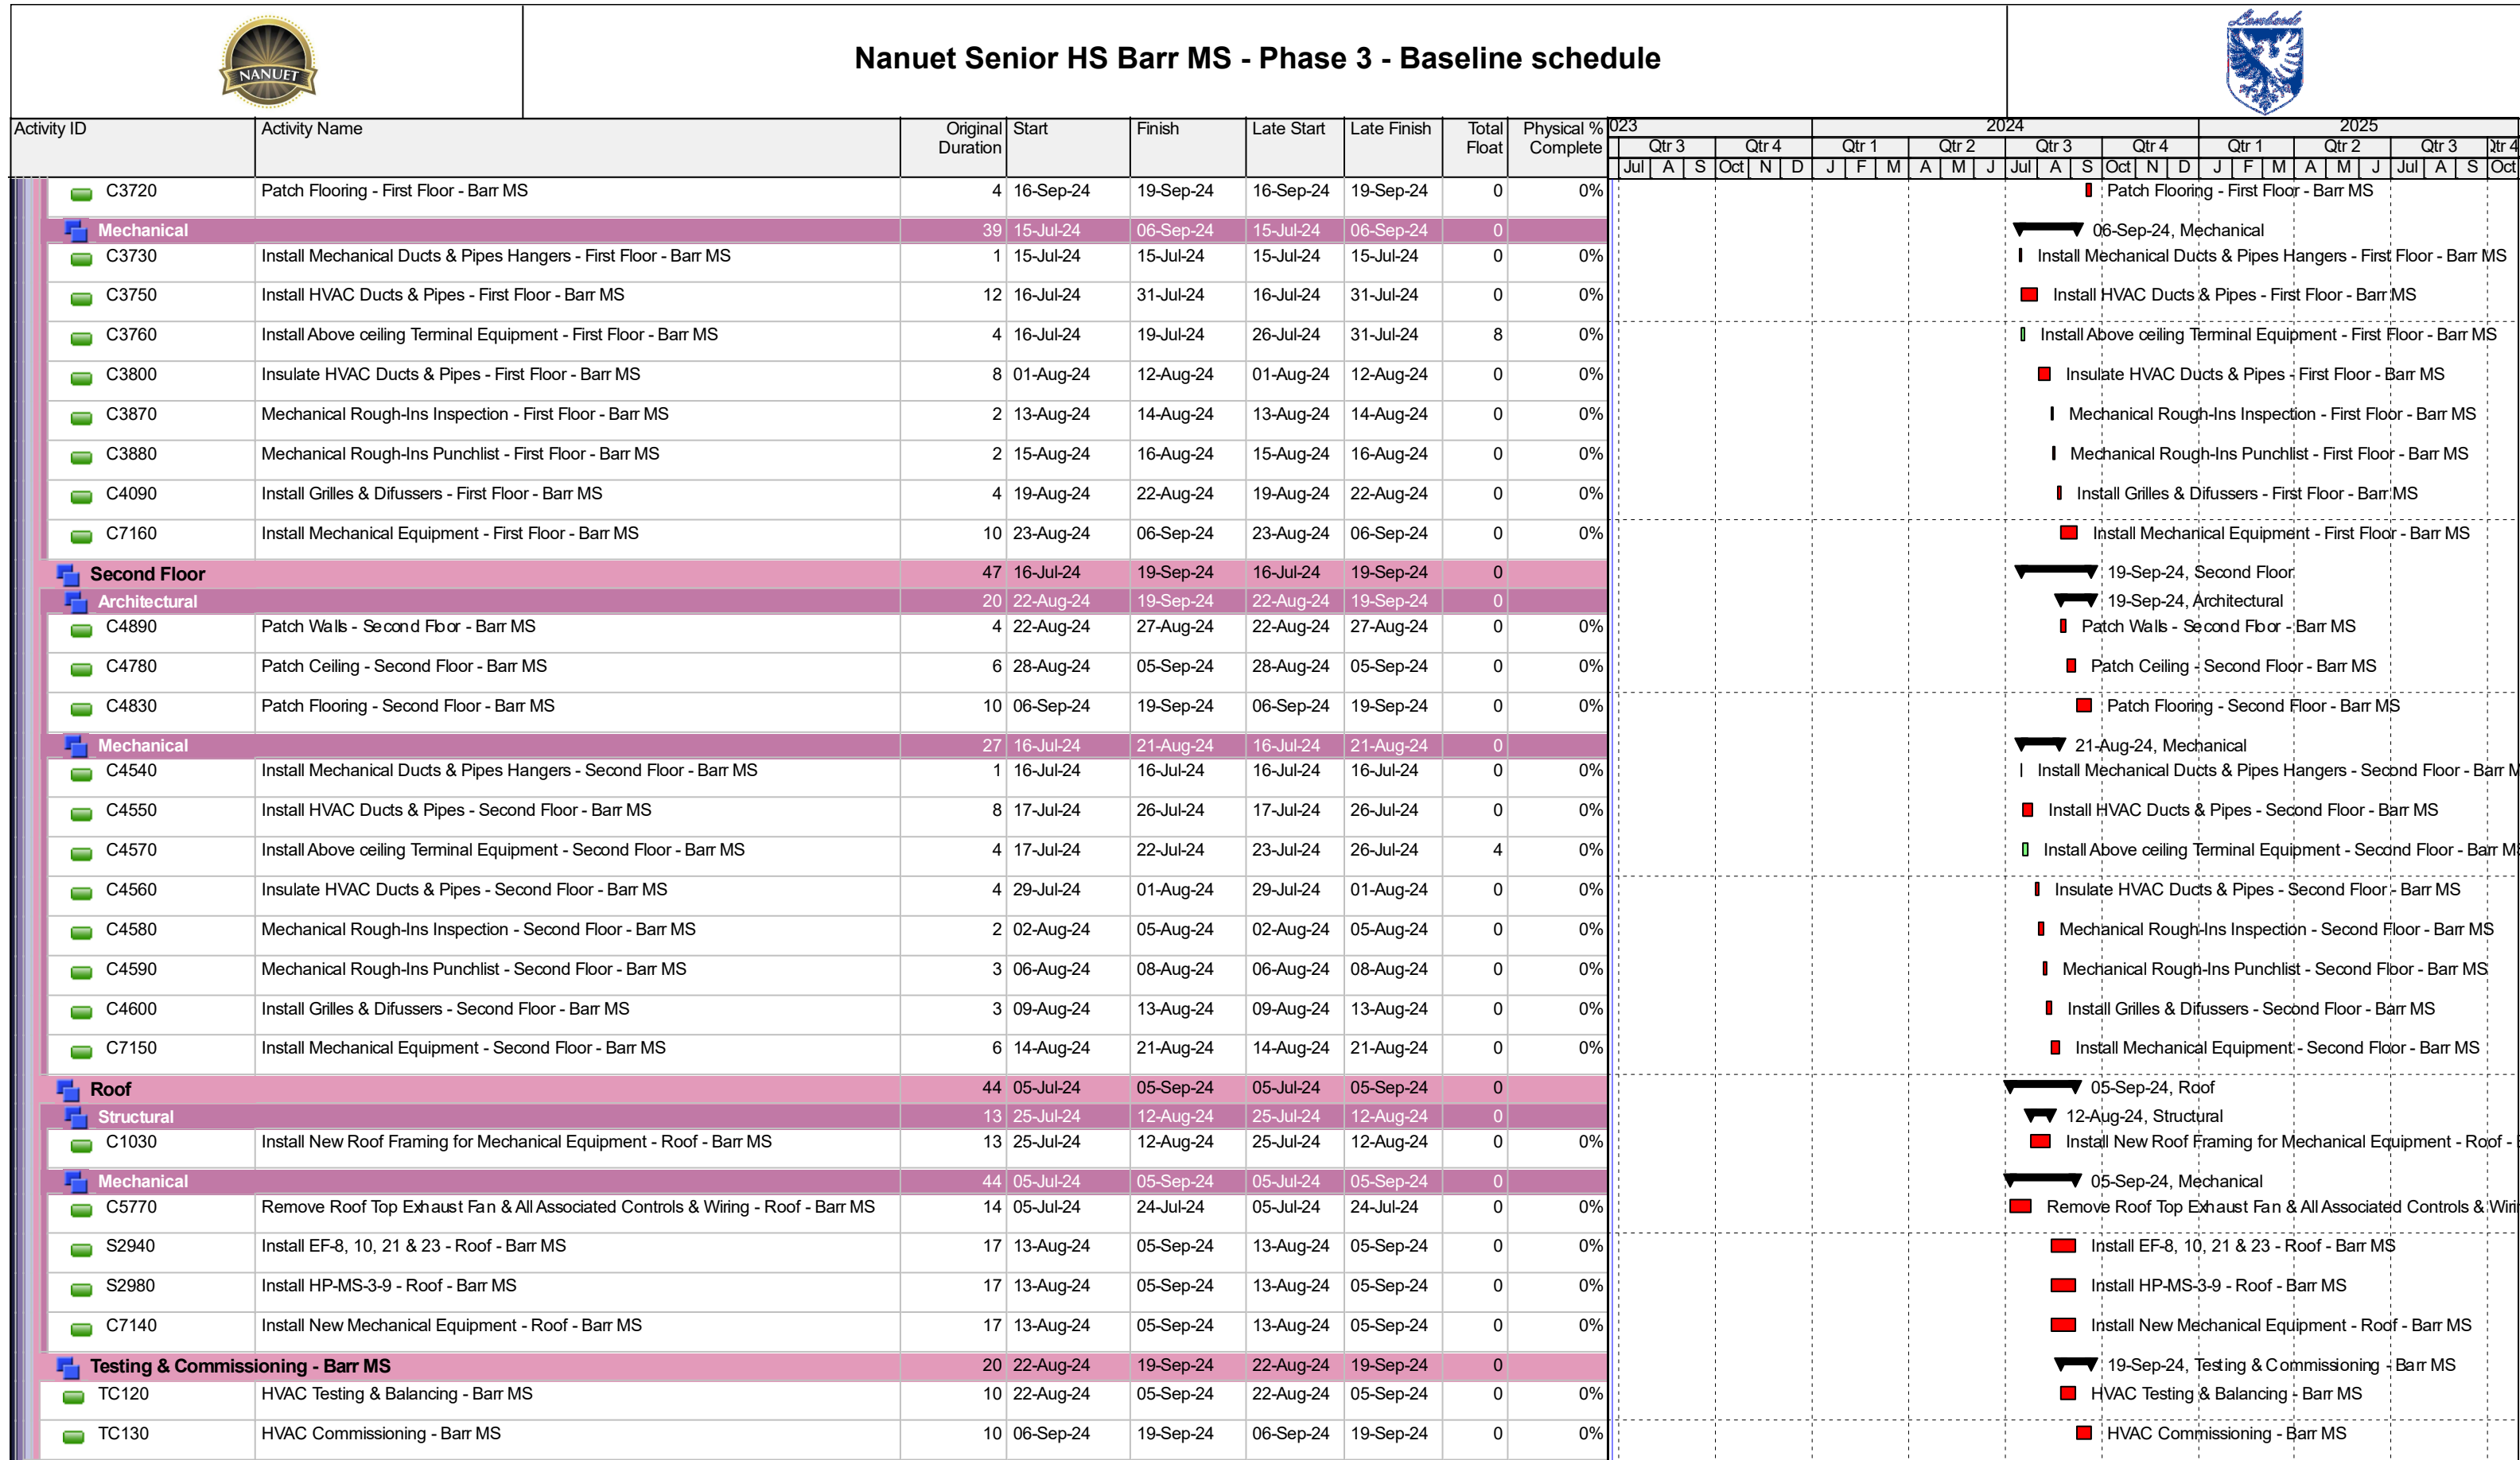



Nanuet Senior HS Barr MS - Phase 3 - Baseline schedule

