



Nanuet Senior HS Barr MS - Phase 3 - Update #01



Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	2023												2024												2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
									Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4			Qtr 1			Qtr 2			Qtr 3			Qtr 4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
									Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
	 S2840	Review & Approve Resilient Base And Accessories.	30	07-Feb-24	20-Mar-24	06-Aug-24	17-Sep-24	127	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	

Remaining Level of Effort

Actual Level of Effort


Actual Work


Remaining Work

Critical Remaining Work

Milestone



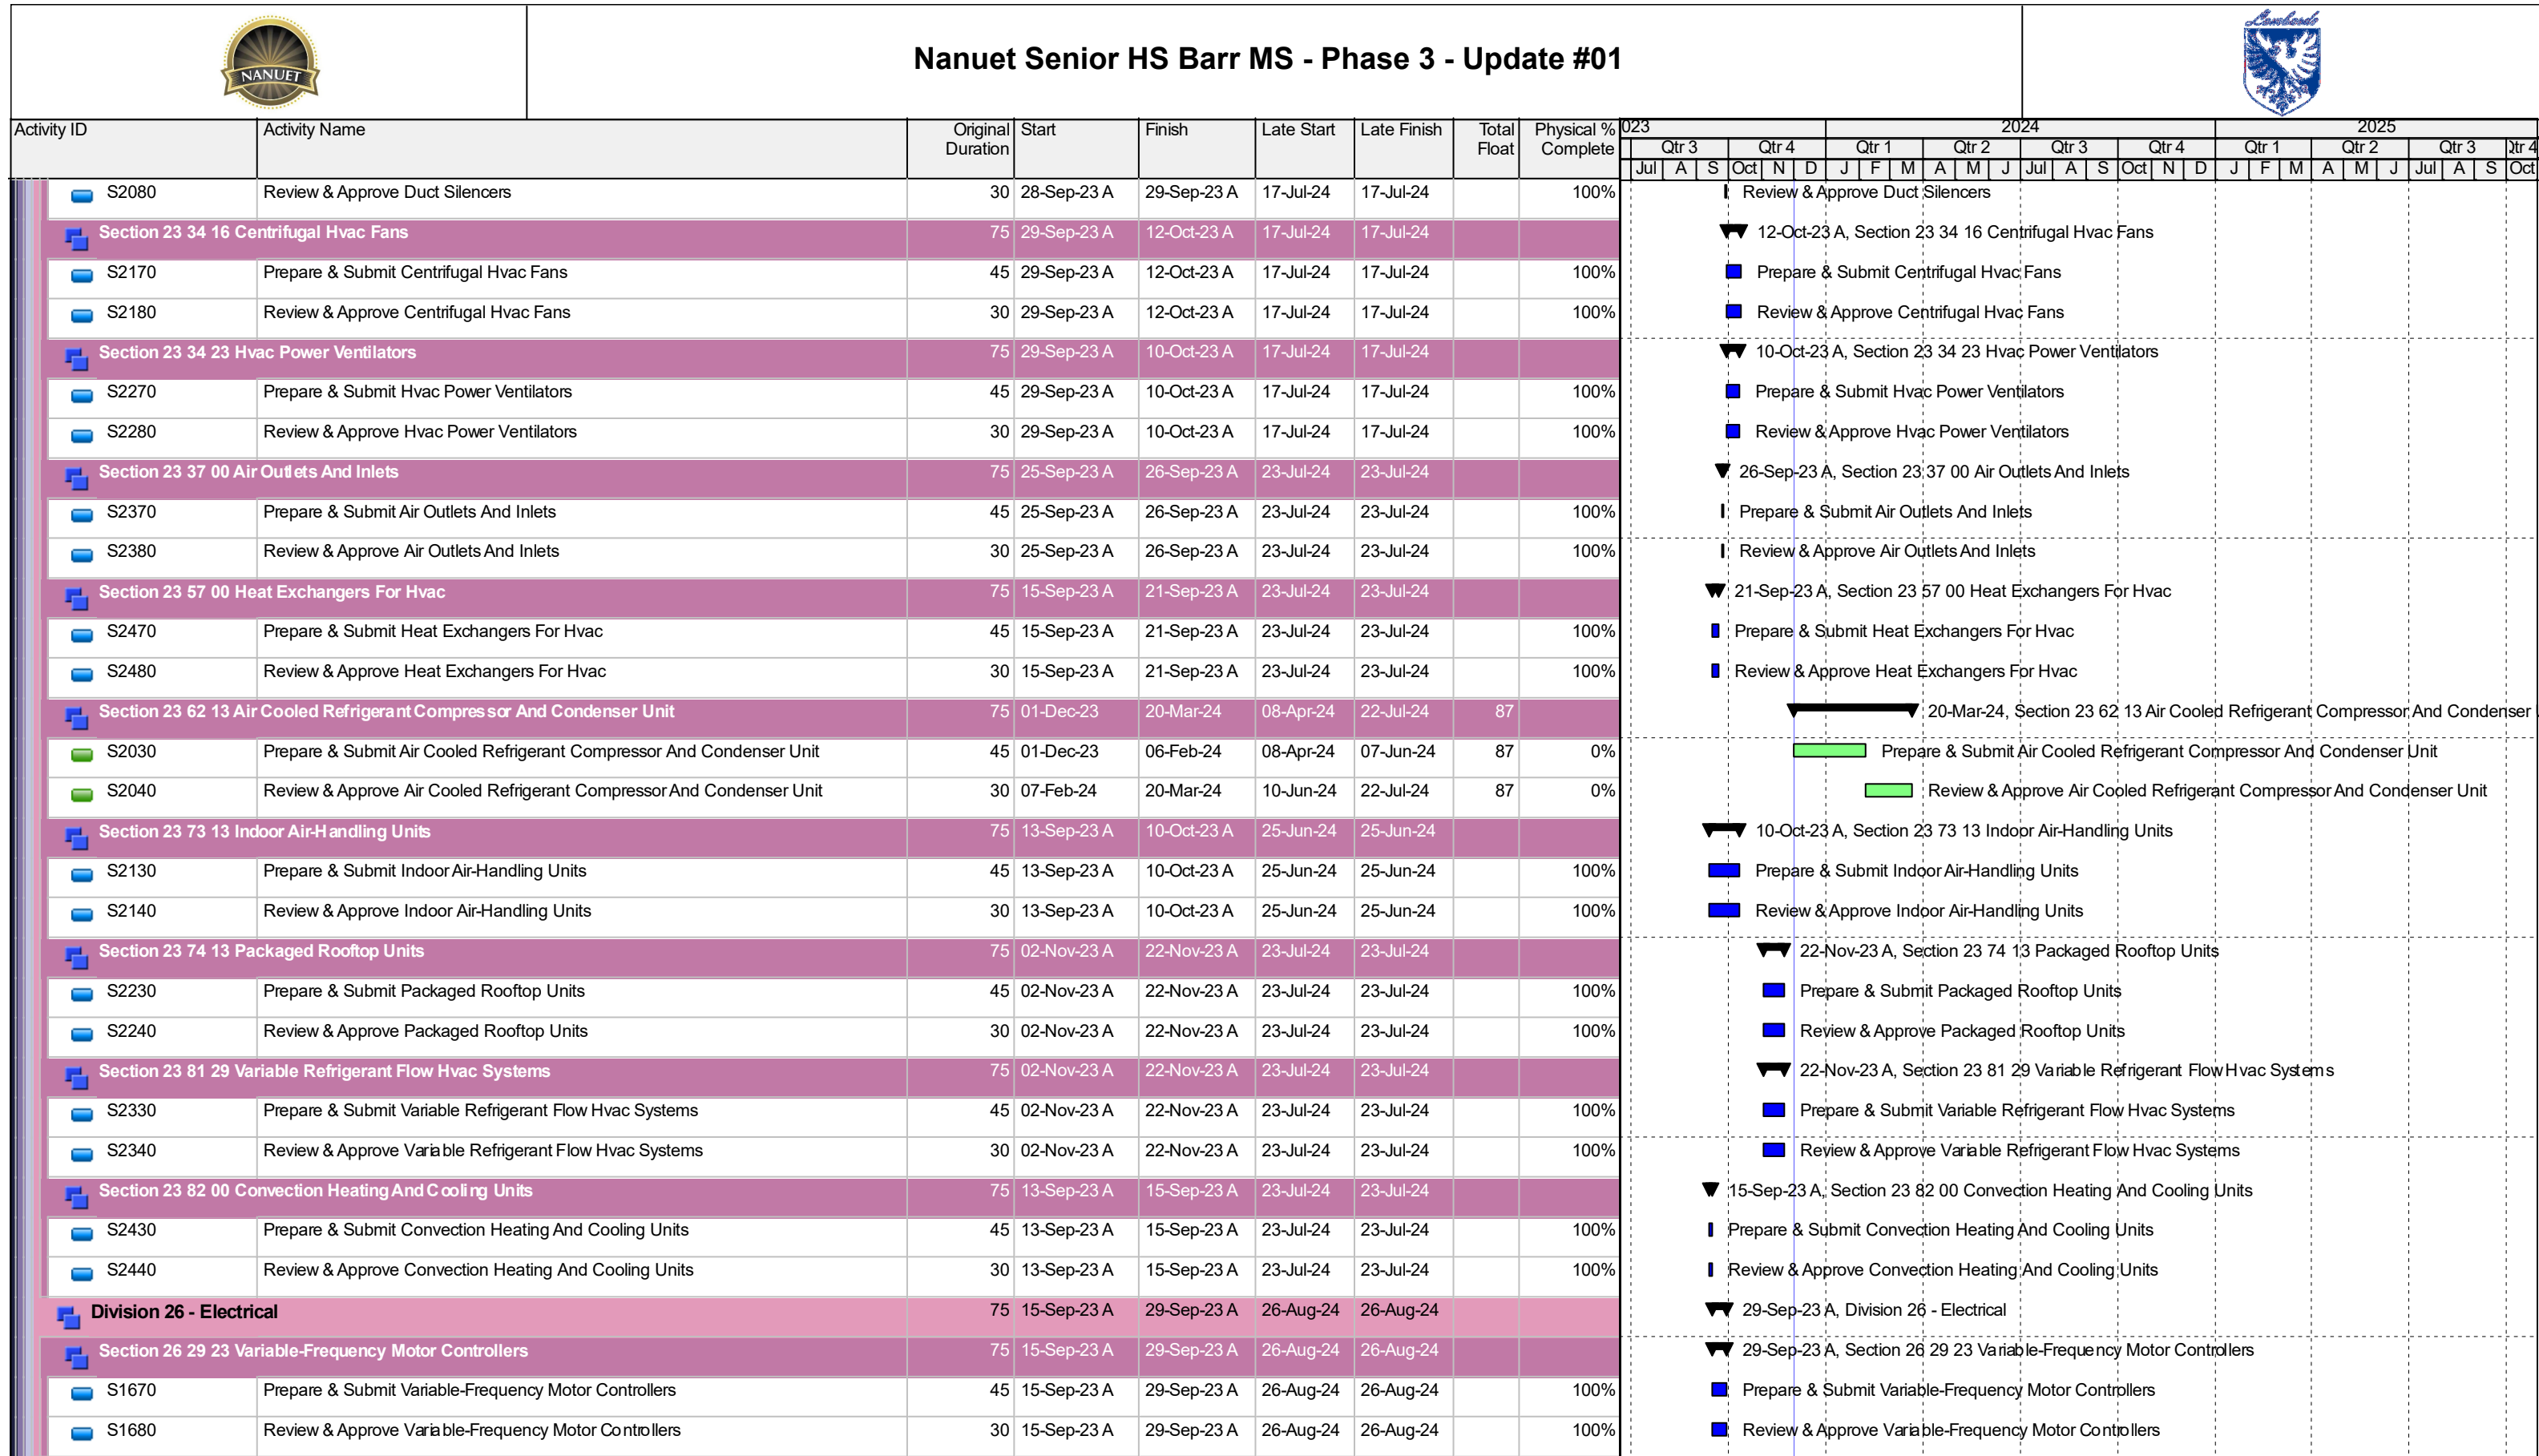

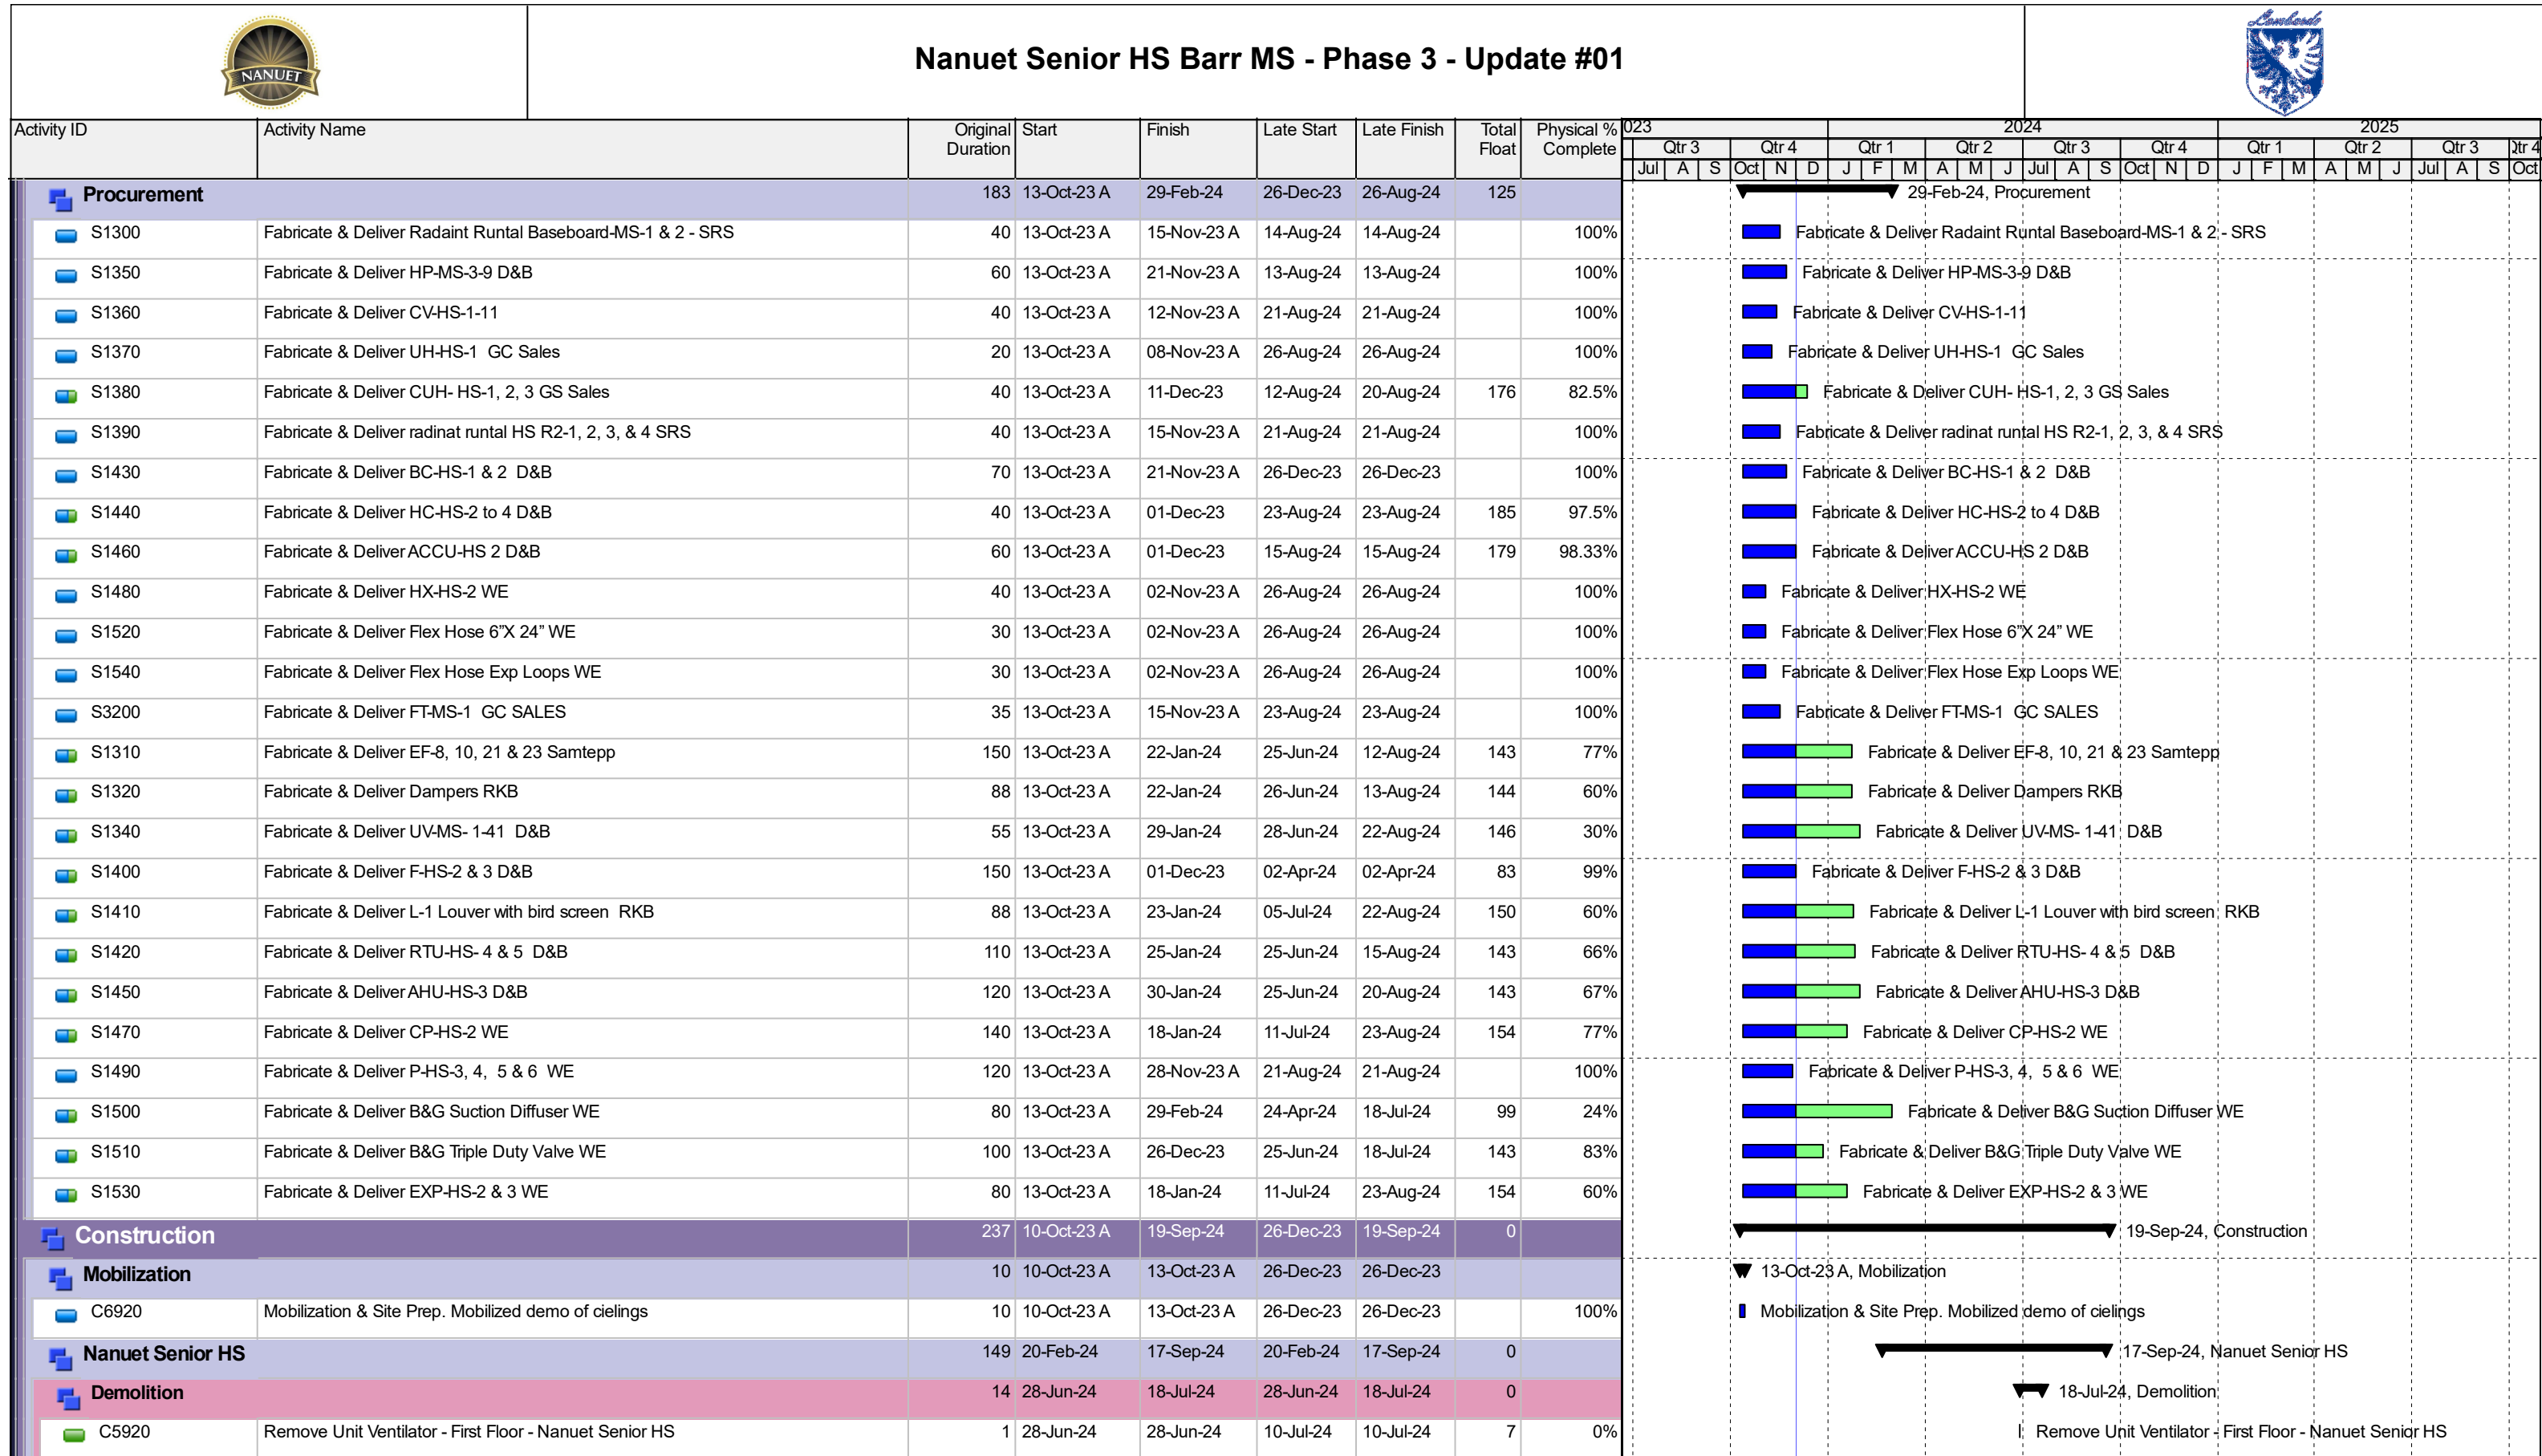



Remaining Level of Effort Actual Level of Effort Actual Work Remaining Work Critical Remaining Work Milestone	Page 8 of 9 Data Date: 30-Nov-23	All Activities Report	 Pearls Construction LLC
---	--	----------------------------------	---

		Nanuet Senior HS Barr MS - Phase 3 - Update #01																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
Activity ID	Activity Name	Original Duration	Start	Finish	Late Start	Late Finish	Total Float	Physical % Complete	2023							2024							2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
									Qtr 3			Qtr 4		Qtr 1			Qtr 2		Qtr 3			Qtr 4		Qtr 1			Qtr 2		Qtr 3			Qtr 4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
									Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct	N	D	J	F	M	A	M	J	Jul	A	S	Oct																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
	 C4780	Patch Ceiling - Second Floor - Barr MS	6	28-Aug-24	05-Sep-24	28-Aug-24	05-Sep-24	0	0%																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		</
