
#1. For the floor in Café Nook 101, where should changes in floor finishes occur? Please provide finish floor plan for Café Nook 101 showing flooring transitions.

## PLEASE SEE ATTACHED SKETCH 01.

#2. Finish #3 calls for wall tile on "Kitchen Wall." .Please specify walls to receive tile in kitchen area. PLEASE SEE ATTACHED SKETCH 01.

- a. Please specify Kitchen Wall Tile. SEE RFI #7
- b. Please Confirm: Kitchen Area is part of Café Nook 101. CONFIRMED
- #3. Please confirm basis of design and finishes in restrooms to match phase 1 and phase 2 as per screenshot below: CONFIRMED

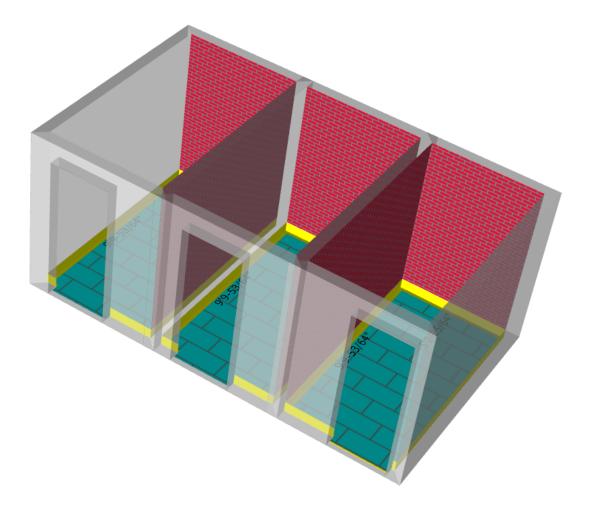

#4. On the Finish Schedule, Finish #5(Sheet Vinyl) Specifies the base as "Integral Cove Base, 6" High. Johnsonite #76 Cinnamon."

Is the base for Finish #5 meant to be Integral Base using the sheet vinyl,

Is it Johnsonite 6" Vinyl Cove Base, #76 Cinnamon? PLEASE DISCARD THE VINYL COVE BASE

| ₹.     | WALLBAINT       | rainty Eggshell finish      | BENJAMINMOORE                           | WBALBOAMIOTOG27W     | 7  |
|--------|-----------------|-----------------------------|---|----------------------|----|
| ξ      | BASE            | INTEGRAL COVE BASE, 6" HIGH | JOHNSONITE                              | 76 CINNAMON          | 3  |
| $\sim$ | $\cdots \cdots$ | <del></del>                 | *************************************** | MASS11 NATURAL WHITE | 3  |
|        | FLOOR           | HOMOGENEOUS SHEET VINYL     | ARMSTRONG                               | COLORARI MEDINIONE   | LA |

#5. Floor #3 LVT is specified as "Patcraft" but no style is identified. Please specify the LVT from finish #3. TIMBER GROVE 30 MIL / COLOR & PATTERN TBD

|       | (INDIALLED AT DEATING AILEA)                     |          |   |
|-------|--|----------|---|
| FLOOR | LUXURY VINYL TILE ( INSTALLED AT NOOK CORRIDOR)  | PATCRAFT | - |
| FLOOD | DODCELAIN CEDAMIC THE (INSTALLED DELIND COLINTED |          |   |


#6. Floor #3 Ceramic Tile is Specified as "Daltile" but no style is identified. Please specify the ceramic tile from Finish #3. PLEASE DISCARD FLOOR CERAMIC TILE. WE WILL USE TIMBER GROVE 30 MIL / COLOR & PATTERN TBD. PLEASE SEE SKETCH 01

| - 1 |       |  |         |   |
|-----|-------|--|---------|---|
|     | FLOOR | PORCELAIN CERAMIC TILE (INSTALLED BEHIND COUNTER, AT KITCHEN AREA) | DALTILE | - |

#7. Floor #3 Wall Tile is Specified as "Daltile, 2x6 White" but no style is identified. Please specify the ceramic tile from Finish #3. (We have found that 2 " x 6" have recently been special order only, with long lead times and high costs. Can we figure for 3" x 6" instead?) 0100 WHITE, 3X6 IS ACCEPTABLE ONLY FOR THE KITCHEN WALL, NOT FOR THE TOILETS. 0100 WHITE FINISH COLOR MIGHT CHANGE TO MATCH THE ACCENT WALL COLOR TBD.

|  |         | í     |
|--|---------|-------|
| PORCELAIN CERAMIC TILE, 2" X 6" STAGGERED BRICK (KITCHEN WALL) | DALTILE | WHITE |
|  |         |       |

#8. Finish Schedule on A1.3 calls for 6" vinyl cove base in Vestibule 100. Floor base detail #7 on A9.1 shows no wall base over walk-off carpet. For Vestibule 100 walk-off carpet, figure for 6" vinyl cove base, or no wall base finish? DISCARD VYNYL COVE BASE.

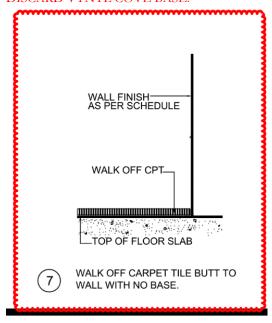

Thank you
