NR HS Extension Boiler

Classic Schedule Layout

18-Jul-24 06:55

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish
NR Boiler	**NR HS Extension Boiler**	248	248	25-Jul-24	07-Jul-25
A1000	Bid	1	1	25-Jul-24*	25-Jul-24
A1010	Award	5	5	26-Jul-24	01-Aug-24
A1020	Contract-Bond-Insurnace	15	15	02-Aug-24	22-Aug-24
A1030	Mech Submittals	15	15	02-Aug-24	22-Aug-24
A1040	Abatement Submittal	10	10	02-Aug-24	15-Aug-24
NR Boiler.Fall 2024 Plan A - 100% Boilers Only Complete by Oct 15,2024		232	232	16-Aug-24	07-Jul-25
A1050	Abate and Remove Boilers	10	10	16-Aug-24	29-Aug-24
A1060	Install Boilers	10	10	30-Aug-24	12-Sep-24
A1090	Boiler BMS	5	5	13-Sep-24	19-Sep-24
A1100	Test and Commission	5	5	20-Sep-24	26-Sep-24
A1180	Return June 2025 after heating season confirmed to complete remaining work	30	30	27-May-25*	07-Jul-25
NR Boiler.Summer 2025 Plan B - 100% Project Complete by Oct 15,2024		40	40	16-Aug-24	10-Oct-24
A1110	Abate and Remove Boilers	10	10	16-Aug-24	29-Aug-24
A1120	Install Boilers	10	10	30-Aug-24	12-Sep-24
A1130	Demo Pumps-Pipe-Tanks ect.	10	10	30-Aug-24	12-Sep-24
A1150	Boiler BMS	5	5	13-Sep-24	19-Sep-24
A1170	Install ET, Pumps, ect.	5	5	13-Sep-24	19-Sep-24
A1140	Pipe Boilers-Pumps-HWH	10	10	20-Sep-24	03-Oct-24
A1160	Test and Commission	5	5	04-Oct-24	10-Oct-24

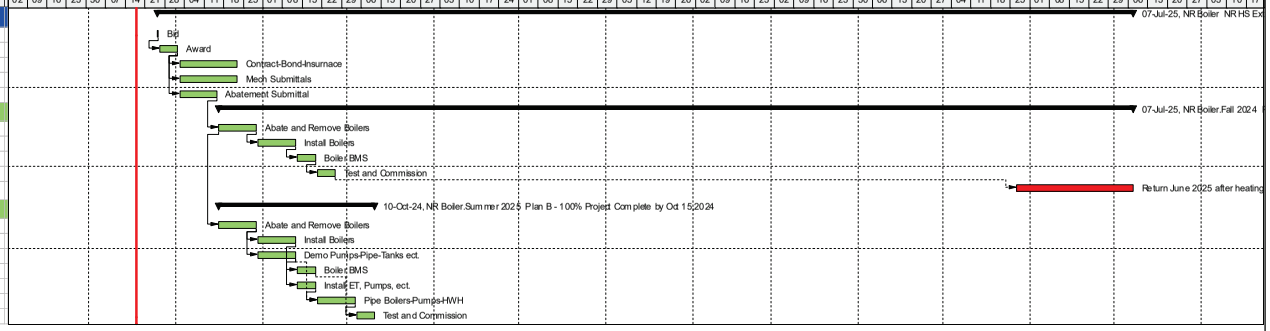

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | summary

TASK filter: All Activities

© Oracle Corporation
